


000021524

INTEROFFICE CORRESPONDENCE

DATE: January 28, 1994

TO: S. M. Nesta, Ecology & NEPA Division, Bldg. T130J, X6386

FROM:  D. R. Ericson, Solar Ponds Projects, Bldg. 080, X6965

SUBJECT: EVALUATION OF THE NEED FOR MIGRATORY BIRD & ENDANGERED SPECIES
SURVEY BEFORE CONSTRUCTION ACTIVITIES COMMENCE ON OU4-
DRE-001-94

In accordance with direction outlined in the Migratory Bird Evaluation, Solar Pond Projects requests you to review all presently proposed construction activities during the Phase I Remedial Process. In order to apprise you early in the planning process, the schedule enclosed is our preliminary working schedule. The schedule may reflect revisions made until construction begins. Marsha Murdock of your staff has requested the enclosed OU4 map outlining the area which may be involved in construction activities, as well as a detailed schedule for your review.

The necessity of an actual survey must be determined. However, due to planning assumptions an Ecological Survey has recently been included in the schedule in congruence with Pre-Construction activities.

Please review the schedule & let me know what resources must be budgeted for your organization. Your input on this matter by March 1, 1994 would be greatly appreciated.

If you have any questions feel free to call me at X6965, or Michelle Mckee of my staff at X8717.

MCM:mcm


Enclosure:
As Stated

cc:

S. R. Keith	w/o encl.
J. A. Ledford	" "
K. C. London	" "
M. C. McKee	" "
M. B. Murdock	w/encl.
ERM Records	
Project Files	

DOCUMENT CLASSIFICATION
REVIEW WAIVER PER
CLASSIFICATION OFFICE

REVIEW DRAFT

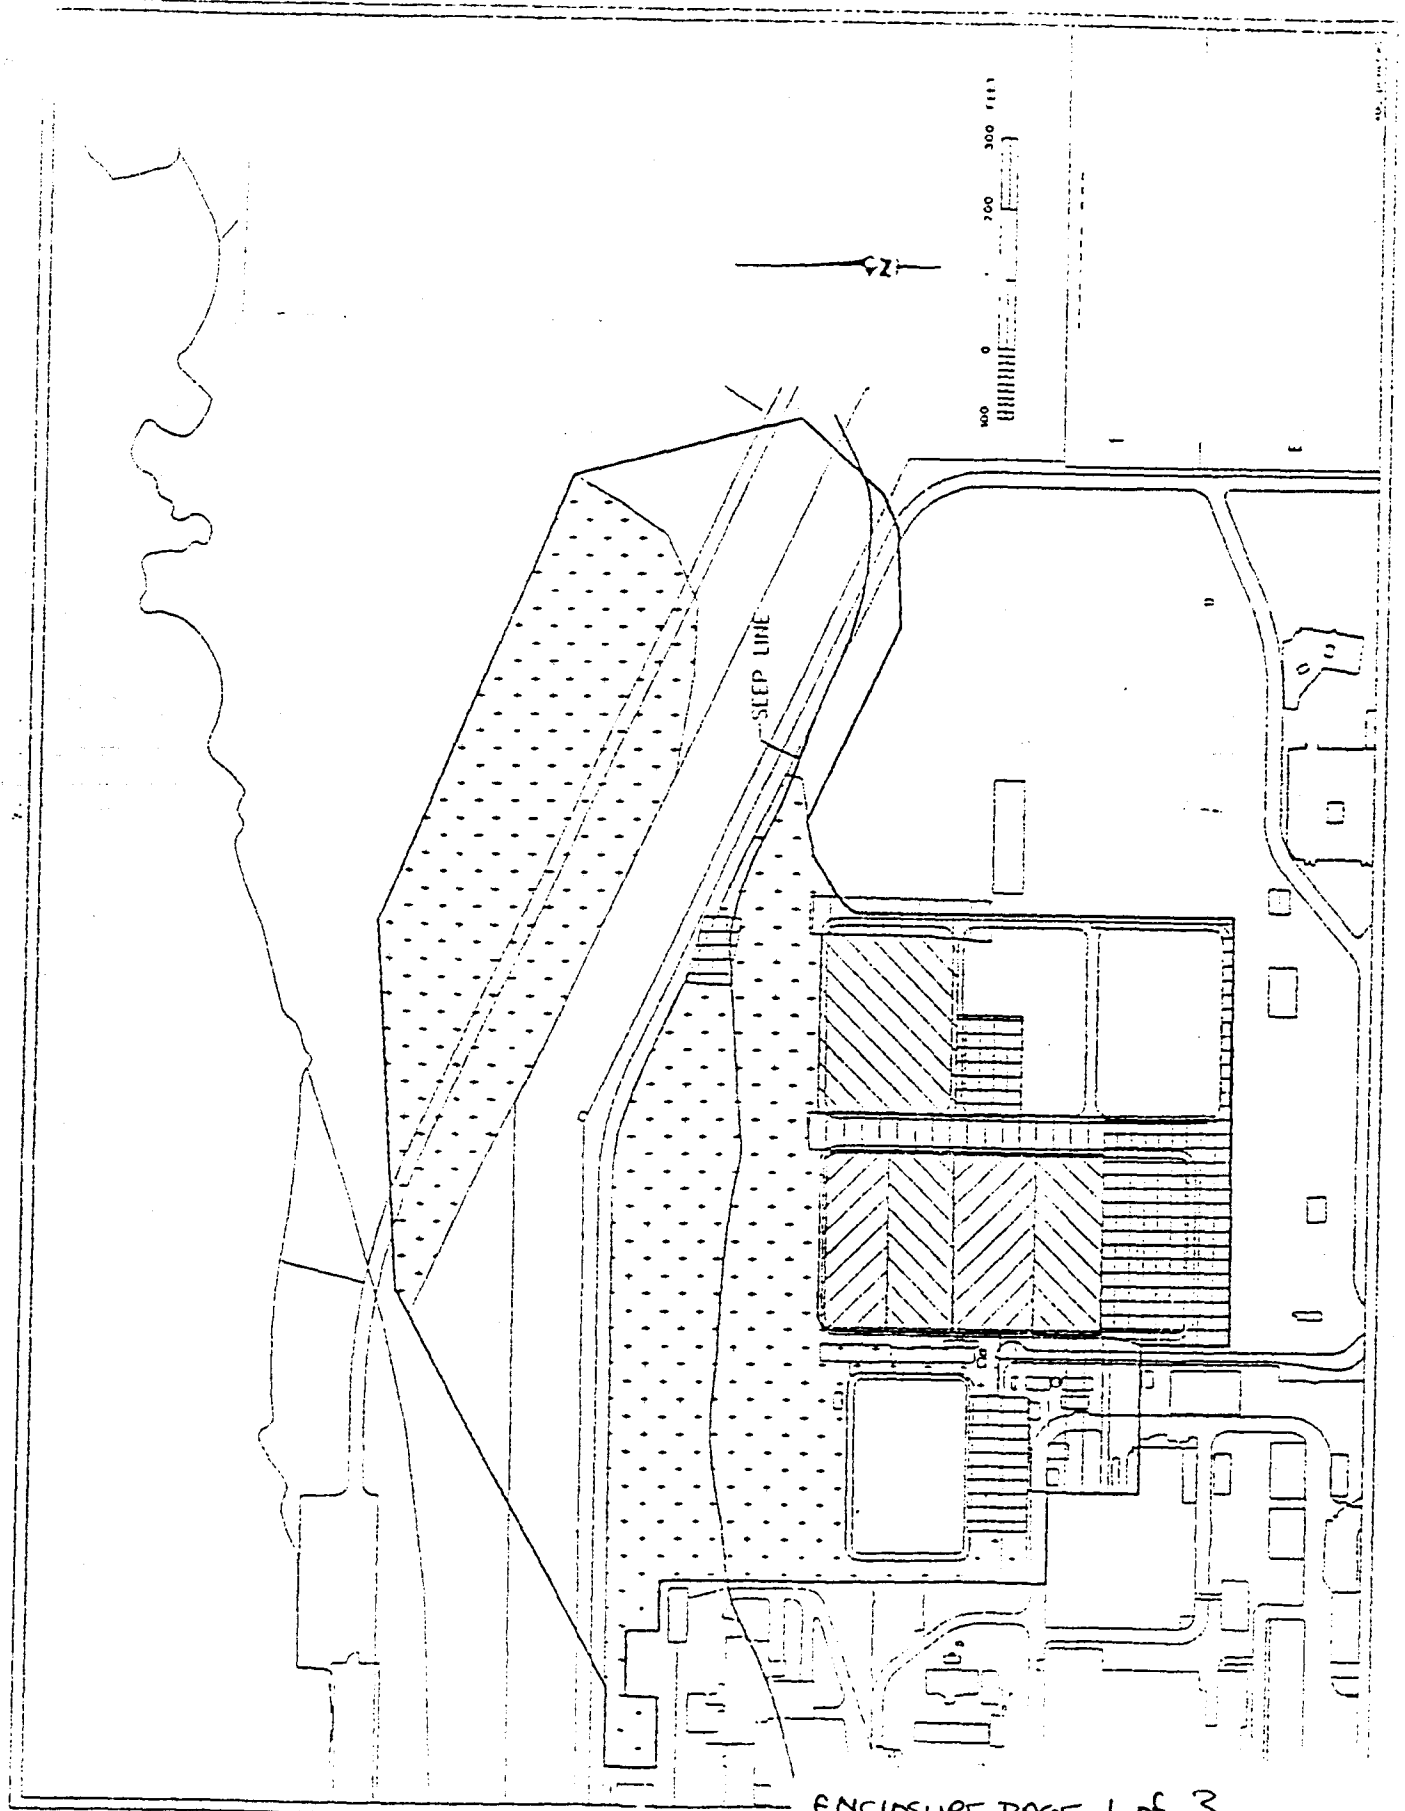

ACTIVITY		EARLY START	EARLY FINISH	ORIG DUR	REM DUR	TOTL FLT	RESP
ACTIVITY ID DESCRIPTION							
10521000	WASTE DISPOSAL PLAN	16FEB95	17MAY95	42	42	52	MRA
10522000	EXCAVATION PERMIT	16FEB95	24MAY95	30	30	64	MRA
10523000	INCP ROUNDTABLE	30JUN95	2JUL95	5	5	0	MRA
10524000	SECURITY PLAN	16FEB95	24MAY95	30	30	64	MRA
10525000	SITE SPECIFIC H & S PLAN	24MAY95	24JUN95	42	42	0	MRA
10526000	JOB SAFETY ANALYSIS	24MAY95	13JUN95	30	30	12	MRA
10531000	REQUEST FOR PROPOSAL	15FEB94	24MAY94	31	31	179	JKH
10531100	BID PACKAGE	15FEB94	28FEB94	10	10	179	MRA
10531200	DAVIS BACON	1MAY94	7MAY94	5	5	195	MRA
10531300	SHORT LIST OF BIDDERS	1MAY94	24MAY94	21	21	179	MRA
10531400	KEY DECISION #3	1MAY94	7MAY94	5	5	195	MRA
10532000	PROPOSAL	14DEC94	19JUN95	21	21	0	MRA
10533000	DOE HQ PROCUREMENT COORDINATION	20JUN95	2FEB95	10	10	0	MRA
10534000	TECHNICAL EVALUATION	3FEB95	23FEB95	15	15	0	MRA
10535000	COST EVALUATION	24FEB95	14MAY95	15	15	0	MRA
10536000	NEGOTIATIONS	17MAY95	17MAY95	21	21	0	MRA
10537000	RECOMMENDATION TO DOE HQ	18MAY95	24MAY95	5	5	0	MRA
10538000	DOE HQ APPROVAL	25MAY95	14MAY95	5	5	0	MRA
10541000	TRAINING	24MAY95	31MAY95	21	21	4	MRA
10542000	MOBILIZATION	2JUN95	6JUL95	21	21	0	MRA
10543000	START CONSTRUCTION (TAG #6)	2JUL95		0	0	0	MRA
10543004	(TAG #6 COMMITMENT)	27SEP95		0	0	0	MRA
10544000	DRAFT SAFETY ASSESSMENT DOCUMENT	17DEC94	7FEB94	35	13	6	MRA

Enclosure page 2 of 3.

