

00977 RF 94

DUE
DATE

Department of Energy

ROCKY FLATS OFFICE
P O BOX 928
GOLDEN COLORADO 80402-0928



000021256

MAR 08 1994

94-DOE-02372

ACTION

DIST. LTR ENC

BERMAN, H S	
CARNIVAL, G J	
COPP, R D	
CORDOVA, R C	
DAVIS, J G	
FERRERA, D W	
FRANZ, W A	
HANNI, B J	
HEALY, T J	
HEDAH, T G	
HILBIG, J G	
HUTCHINS, N M	
KELL, R E	
KIRBY, W A	
KUESTER, A W	
MAHAFFEY, J W	
MANN, H P	
MARX, G E	
McKENNA, F G	
MORGAN, R V	
PIZZUTO, V M	
POTTER, G L	
SANDLIN, N B	
SATTERWHITE, D G	
SCHUBERT, A L	
SETLOCK, G H	
STIGER, S G	XX
SULLIVAN, M T	
SWANSON, E R	
WILKINSON, R B	
WILSON, J M	

O'Kourte T XX

Busby W XX

O'Neill K XX

Mr Martin Hestmark
U S Environmental Protection Agency, Region VIII
ATTN Rocky Flats Project Manager, 8HWM-RI
999 18th Street, Suite 500, 8WM-C
Denver, Colorado 80202-2405

Mr Gary Baughman
Hazardous Waste Facilities Unit Leader
Colorado Department of Health
4300 Cherry Creek Drive South
Denver, Colorado 80222-1530

Gentlemen

Over the past several months, staff members from the Department of Energy (DOE), the Environmental Protection Agency, and the Colorado Department of Health have discussed methods to reduce costs and speed up the environmental cleanup at the Rocky Flats Plant. During these discussions, it was decided, in principle, to rescope the original schedules for Operable Units (OUs) 7 and 11, beginning with the Phase I Resource Conservation and Recovery Act Facility Investigation/Remedial Investigation (RFI/RI) Work Plans. As part of this rescoping, the original Phase I Work Plans for both OU-7 and 11 will be modified and several of the Table VI Milestones listed in the Interagency Agreement will be deleted or replaced by technical memorandums. In addition, we propose the transfer of Individual Hazardous Substance Sites 166 1, 166 2, 166 3, and 167 1 from OU-6 to OU-7.

The enclosure contains highlights of the proposed changes and new schedules. Your review, comments, and formal approval of the revised scopes of these OUs are requested.

The DOE would like to acknowledge the efforts of all parties in developing this rescoping strategy, a strategy that streamlines our regulatory and technical process to promote cleanup rather than paperwork. We look forward to continued cooperative efforts and the improvement of the overall performance of our environmental restoration effort.

CORRESPONDENCE CONTROL x x
ADMIN RECORD/380 X 2
PATSI/T130G

Reviewed for Addressee
Corres Control RFP

3-11-94 C
DATE BY

Ref Ltr #

DOE ORDER # 5400 1

ADMIN RECORD



M Hestmark & G Baughman
94-DOE-02372

2

MAR 08 1994

If you have any specific questions concerning the rescoping effort, please direct them to Jen Pepe at 966-2184, or Dave George at 966-5669

Sincerely,



Jessie Roberson
Acting Assistant Manager for
Environmental Restoration

Enclosure

cc w/Enclosure
F Lockhart, ER, RFO
S Stiger, AGMERM
D George, ER, RFO
T O'Rourke, EG&G
W Busby, EG&G
K O'Neill, EG&G

OPERABLE UNIT 11 PROPOSED RESCOPED ACTIVITIES

The following original IAG milestones were delivered as scheduled

SUBMIT DRAFT PHASE I RFI/RI WORK PLAN
SUBMIT FINAL PHASE I RFI/RI WORK PLAN

JUNE 8, 1990
JANUARY 2, 1992

The milestone SUBMIT DRAFT PHASE I RFI/RI REPORT has been increased in scope. The original milestone was scheduled for delivery on September 20, 1994. With the change in scope, the target date for completion is scheduled for at or near September 20, 1994.

Phase I and Phase II are proposed to be combined to a single phase to reduce the duration of closure.

The milestone SUBMIT DRAFT PHASE I PROPOSED IMIRA DECISION DOCUMENT is assumed to include a Justification for No Further Action.

All of the milestones following are assumed to be deleted per the Justification for No Further Action.

OPERABLE UNIT 11 IAG TABLE VI MILESTONES PROPOSED TO BE REVISED OR DELETED

MILESTONE

POTENTIAL DISPOSITION

SUBMIT DRAFT PHASE I RFV/RI REPORT
SUBMIT FINAL PHASE I RFV/RI REPORT

Revised*
Revised**

SUBMIT DRAFT PHASE I PROPOSED IM/IRA DD
SUBMIT FINAL PHASE I PROPOSED IM/IRA DD
SUBMIT PHASE I IM/IRA RESPONSIVENESS SUMMARY
SUBMIT PHASE I FINAL IM/IRA DECISION DOCUMENT AND
FINAL RESPONSIVENESS SUMMARY
SUBMIT IM DESIGN CD/RD WORK PLAN
SUBMIT PHASE I IM/IRA IMPLEMENTATION DOCUMENT
SUBMIT TITLE II DESIGN
BEGIN PHASE I IM/IRA CONSTRUCTION

Deleted**
Deleted**
Deleted**
Deleted**

SUBMIT DRAFT PHASE II RFI/RI WORK PLAN
SUBMIT FINAL PHASE II RFI/RI WORK PLAN
SUBMIT DRAFT PHASE II RFI/RI REPORT
SUBMIT FINAL PHASE II RFI/RI REPORT

Deleted*
Deleted*
Deleted*
Deleted*

SUBMIT DRAFT PHASE II CMS/FS REPORT
SUBMIT FINAL PHASE II CMS/FS REPORT

Deleted*
Deleted*

SUBMIT DRAFT PHASE II PP
SUBMIT FINAL PHASE II PP
SUBMIT DRAFT PHASE II RESPONSIVENESS SUMMARY
SUBMIT FINAL PHASE II RESPONSIVENESS SUMMARY

Deleted*
Deleted*
Deleted*
Deleted*

SUBMIT DRAFT PHASE II CAD/FAD
SUBMIT FINAL PHASE II CAD/FAD

Revised**
Revised**

SUBMIT CD/RD WORK PLAN
SUBMIT DRAFT TITLE II DESIGN PLANS
SUBMIT FINAL TITLE II DESIGN PLANS

Revised**
Revised**
Revised**

BEGIN PHASE II CAVRA CONSTRUCTION

Revised**

*Integration of Phase I & Phase II Requirements

** Assuming No Further Action Justification Per Integrated Phases RFI/RI Results

OPERABLE UNIT 7 PROPOSED RESCOPED ACTIVITIES

The following original IAG milestones were delivered as scheduled

SUBMIT DRAFT PHASE I RFI/RI WORK PLAN
SUBMIT FINAL PHASE I RFI/RI WORK PLAN

JUNE 8, 1990
AUGUST 28, 1991

The following milestone was delayed due to a Stop Work Order

SUBMIT DRAFT PHASE I RFI/RI REPORT

OCTOBER 12, 1993

The remedial action necessary to close Operable Unit 7 is guided by the CHWA. In following the guidance of the CHWA, some previously planned activities can be eliminated. Therefore, several milestones are proposed to be revised or deleted.

The Phase II RFI/RI will be included within the IM/IRA document. This action will delete all Phase II RFI/RI milestones. An extension will be required for the IM/IRA DD due to its increased scope. The following IM/IRA DD proposed revised milestones are as follows:

Milestone

SUBMIT IM/IRA DECISION DOCUMENT
AGENCY APPROVAL IM/IRA DD
IM/IRA DD APPROVED

In addition, several milestones beyond the Phase II RFI/RI are proposed to be modified as a result of the IM/IRA DD.

Milestone

IM DESIGN WORK PLAN COMPLETE
SUBMIT DRAFT PHASE I IM/IRA IMPLEMENTATION DOCUMENT
SUBMIT TITLE II DESIGN
BEGIN CONSTRUCTION PROCESS

OPERABLE UNIT 7 IAG TABLE VI MILESTONES PROPOSED TO BE REVISED OR DELETED


<u>MILESTONE</u>	<u>POTENTIAL DISPOSITION</u>
SUBMIT DRAFT PHASE I RFV/RI REPORT	Deleted*
SUBMIT FINAL PHASE I RFV/RI REPORT	Deleted*
SUBMIT DRAFT PHASE I IM/IRA DD	Revised****
SUBMIT FINAL PHASE I IM/IRA DD	Revised****
SUBMIT IM/IRA RESPONSIVENESS SUMMARY	Revised****
SUBMIT FINAL PHASE I IM/IRA DD	Revised****
SUBMIT IM/DESIGN WORK PLAN	Revised***
SUBMIT PHASE I IM/IRA IMPLEMENTATION DOCUMENT	Revised***
SUBMIT TITLE II DESIGN	Revised***
BEGIN PHASE I IM/IRA CONSTRUCTION	Revised***
SUBMIT DRAFT PHASE II RFI/RI WORK PLAN	Deleted**
SUBMIT FINAL PHASE II RFI/RI WORK PLAN	Deleted**
SUBMIT DRAFT PHASE II RFV/RI REPORT	Deleted**
SUBMIT FINAL PHASE II RFV/RI REPORT	Deleted**
SUBMIT DRAFT PHASE II CMS/FS REPORT	Deleted**
SUBMIT FINAL PHASE II CMS/FS REPORT	Deleted**
SUBMIT DRAFT PHASE II PP	Deleted****
SUBMIT FINAL PHASE II PP	Deleted****
SUBMIT DRAFT PHASE II RESPONSIVENESS SUMMARY	Deleted****
SUBMIT FINAL PHASE II RESPONSIVENESS SUMMARY	Deleted****
SUBMIT DRAFT PHASE II CAD/FAD	Revised**
SUBMIT FINAL PHASE II CAD/FAD	Revised**
SUBMIT CD/RD WORK PLAN	Deleted***
SUBMIT DRAFT TITLE II DESIGN	Deleted***
SUBMIT TITLE II DESIGN	Deleted***
BEGIN CA/RA CONSTRUCTION	Deleted***

*Phase I requirement satisfied in revised FSP Tech Memo

**Integration of Phase I & Phase II requirements

*** Final Action will be significantly streamlined due to IM/IRA accomplishing closure

****Revised to incorporate Phase II RFI/RI Report requirements

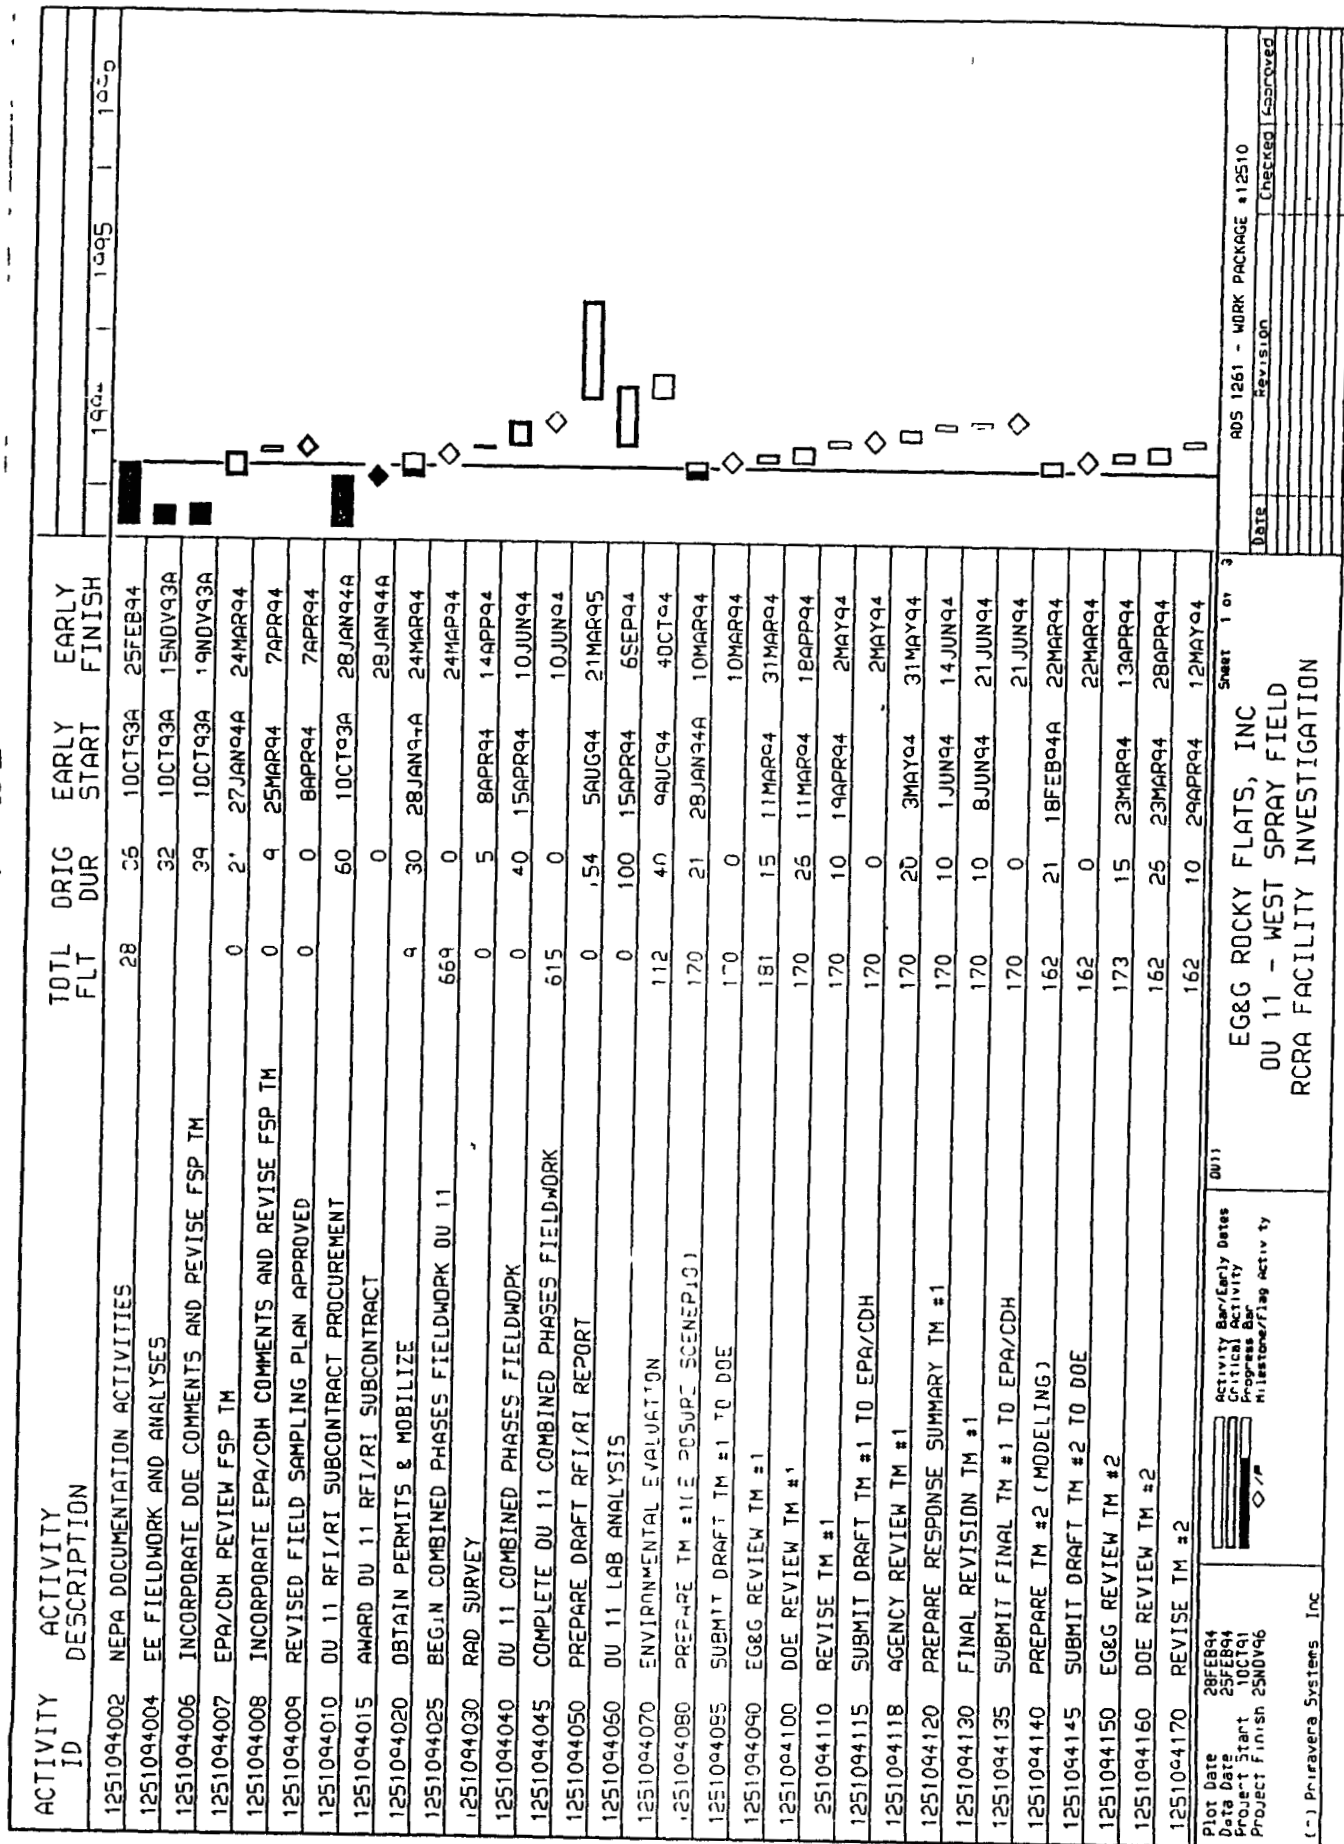

EG&G ROCKY FLATS, INC
OU 11 - WEST SPRAY FIELD
RCRA FACILITY INVESTIGATION

Activity Bar/Early Dates
Critical Activity
Progress Bar
Milestone/Flag Activity

Plot Date 28FEB94
Data Date 25FEB94
Project Start 10CT93
Project Finish 25NOV96

(-) Primavera Systems, Inc

DU11

Sheet 1 of 3

ADS 1261 - WORK PACKAGE #12510

Date Revision Checked Approved

ACTIVITY ID	ACTIVITY DESCRIPTION	TOTL FLT	ORIG DUP	EARLY START	EARLY FINISH
1251044175	SUBMIT DRAFT TM #2 TO EPA/CDH	162	0		12MAY94
1251044180	AGENCY REVIEW TM #2	162	20	13MAY94	10JUN94
1251044190	PREPARE RESPONSE SUMMARY TM #2	162	10	13JUN94	24JUN94
1251044200	FINAL REVISION TM #2	162	10	20JUN94	1JUL94
1251044205	SUBMIT FINAL TM #2 TO EPA/CDH	162	0		1JUL94
1251044210	PREPARE DRAFT TM #3	0	21	22AUG94	20SEP94
1251044215	SUBMIT DRAFT TM #3 TO DOE	36	0		20SEP94
1251044220	EG&G REVIEW TM #3	47	15	21SEP94	11OCT94
1251044230	DOE REVIEW TM #3	36	25	21SEP94	26OCT94
1251044240	REVISE TM #3	36	10	27OCT94	9NOV94
1251044245	SUBMIT DRAFT TM #3 TO EPA/CDH	36	0		9NOV94
1251044250	AGENCY REVIEW TM #3	36	20	10NOV94	9DEC94
1251044260	PREPARE RESPONSE SUMMARY TM #3	36	10	12DEC94	23DEC94
1251044270	FINAL REVISION TM #3	36	10	19DEC94	9JAN95
125105-275	SUBMIT FINAL TM #3 TO EPA/CDH	36	0		9JAN95
1251044280	PREPARE DRAFT TM #4 (TOXICITY)	0	21	21SEP94	19OCT94
1251044285	SUBMIT DRAFT TM #4 TO DOE	0	0		19OCT94
1251044290	EG&G REVIEW TM #4	11	15	20OCT94	9NOV94
1251044300	DOE REVIEW TM #4	0	26	20OCT94	28NOV94
1251044310	REVISE TM #4	0	10	29NOV94	12DEC94
1251044315	SUBMIT DRAFT TM #4 TO EPA/CDH	0	0		12DEC94
1251044320	AGENCY REVIEW TM #4	0	20	13DEC94	17JAN95
1251044330	PREPARE RESPONSE SUMMARY TM #4	0	10	18JAN95	31JAN95
1251044340	FINAL REVISION TM #4	0	10	25JAN95	7FEB95
1251044345	SUBMIT FINAL TM #4 TO EPA/CDH	0	0		7FEB95
1251044347	CONDUCT HHRA	0	15	8FEB95	28FEB95
1251044348	BASELINE RISK ASSESSMENT	0	15	1MAR95	21MAR95
1251044350	SUBMIT DRAFT RFI/RI REPORT TO DOE	0	0	22MAR95	21MAR95
1251044355	DOE REVIEW DRAFT RFI/RI REPORT	0	21	22MAR95	20APR95
1251044360	REVISE DRAFT RFI/PI REPORT	0	21	21APR95	19MAY95
1251044365	SUBMIT RFI/PI REPORT TO EPA/CDH	0	0	22MAY95	19MAY95

Sheet 2 of 3

EG&G ROCKY FLATS, INC
OU 11 - WEST SPRAY FIELD
RCRA FACILITY INVESTIGATION

Plot Date 29 FEB 94

Data Tag 0011

Project 0011

Project 0011

Activity Bar/Early Dates

Critical Activity

Progress Bar

Revision/Flag Act v Ty

AD5 1261 - WORK PACKAGE #12510

Revision

Checked

Approved

ACTIVITY ID	ACTIVITY DESCRIPTION	TOTL FLT	ORIG DUR	EARLY START	EARLY FINISH
1251094370	AGENCY REVIEW DRAFT RFI/RI REPORT	0	21	22MAY95	20JUN95
1251094375	REVISE DRAFT RFI/RI REPORT	0	21	21JUN95	20JUL95
1251094380	SUBMIT FINAL RFI/RI REPORT	0	0	21JUL95	20JUL95
1251094385	EPA/CDH REVIEW RFI/RI FOR FINAL APPROVAL	0	10	21JUL95	3AUG95
1251094387	RFI/RI REPORT APPROVED	0	0	4AUG95	3AUG95
1251094390	PREPARE DRAFT NO FURTHER ACTION JUSTIFICATION	0	42	4AUG95	30CT95
1251094400	SUBMIT DRAFT NO FURTHER ACTION JUSTIFICATION TO	0	0	40CT95	30CT95
1251094410	DOE REVIEW DRAFT NFAJD	0	21	40CT95	1NOV95
1251094420	REVISE DRAFT NFAJD	0	21	2NOV95	4DEC95
1251094430	SUBMIT DRAFT NFAJD TO EPA/CDH	0	0	5DEC95	4DEC95
1251094440	EPA/CDH REVIEW NFAJD	0	62	5DEC95	7MAR96
1251094450	REVISE NFAJD	0	41	8MAR96	6MAY96
1251094460	SUBMIT FINAL NFAJD TO EPA/CDH	0	0	7MAY96	6MAY96
1251094470	EPA/CDH REVIEW AND APPROVE NFAJD	0	21	7MAY96	5JUN96
1251094480	NO FURTHER ACTION JUSTIFICATION APPROVED	0	0	6JUN96	5JUN96
1251094490	PUBLIC COMMENT PERIOD	0	59	6JUN96	27AUG96
1251094500	PUBLIC COMMENT RESOLUTION	0	21	28AUG96	26SEP96
1251094510	PREPARE RECORD OF DECISION	0	42	27SEP96	25NOV96
1251094520	RECORD OF DECISION ISSUED	0	0	26NOV96	25NOV96

Plot Date 28FEB94
Data Date 25FEB94
Project Start 20CT91
Project Finish 25NOV96

(c) Primavera Systems, Inc

DU11

Activity Bar/Early Dates
Critical Activity
Progress Bar
Milestone/Flag Activity

Sheet 3 of 3

EG&G ROCKY FLATS, INC
DU 11 - WEST SPRAY FIELD
RCRA FACILITY INVESTIGATION

ADS 1261 - WORK PACKAGE #12510

Date Revision Checked Approved

ACTIVITY ID	ACTIVITY DESCRIPTION	REM DUP	EARLY START	EARLY FINISH
1230200010	AWARD SUBCONTRACT	0		21 JAN 94
1230200020	SUBCONTRACTOR PROJECT MANAGEMENT	528	21 JAN 94	9 APR 96
1230200030	PHASE I DATA ASSESSMENT	37	21 JAN 94	19 APR 94
1230200040	PHASE I DATA EVALUATION	32	21 JAN 94	12 APR 94
1230200050	PHASE I DATA PRESENTATION	5	13 APR 94	19 APR 94
1230200060	SCOPING MEETINGS/DQO DEVELOPMENT	3	28 JAN 94	1 MAR 94
1230200070	PHASE I RFI/RI WORKPLAN MODIFICATION	40	11 FEB 94	22 APR 94
1230200075	SUBMIT PHASE I WORKPLAN MOD TO DOE	0	25 APR 94	22 APR 94
1230200080	DOE REVIEW PHASE I WORKPLAN MOD	10	25 APR 94	6 MAY 94
1230200085	REVISE PHASE I WORKPLAN MOD PER DOE COMMENTS	10	9 MAY 94	20 MAY 94
1230200088	SUBMIT PHASE I WORK PLAN MOD TO EPA/CDH	0	23 MAY 94	20 MAY 94
1230200090	EPA/CDH REVIEW PHASE I WORKPLAN MOD	15	23 MAY 94	13 JUN 94
1230200095	REVISE PHASE I WORKPLAN MOD PER EPA/CDH COMMENTS	10	14 JUN 94	27 JUN 94
1230200100	DU 7 WORKPLAN MODIFICATION APPROVED	0	28 JUN 94	27 JUN 94
1230200110	WORKPLAN IMPLEMENTATION PLAN	21	23 JAN 94	25 MAR 94
1230200120	HEALTH AND SAFETY PLAN ADDENDUM	6	14 JUN 94	21 JUN 94
1230200130	TRAIN AND BADGE S/C PERSONNEL	21	28 MAR 94	26 APR 94
1230200140	OBTAIN PERMITS	10	28 MAR 94	11 APR 94
1230200150	READINESS REVIEW	5	28 JUN 94	5 JUL 94
1230200150	READINESS REVIEW COMPLETE	0	6 JUL 94	5 JUL 94
1230200170	RFI/RI IMPLEMENTATION OF TECH MEMO	60	6 JUL 94	28 SEP 94
1230200180	MOBILIZE	15	6 JUL 94	26 JUL 94
1230200190	MONITOR WELL/BORING INSTALLATION	35	27 JUL 94	14 SEP 94
1230200200	SOIL SAMPLING	21	27 JUL 94	24 AUG 94
1230200210	MONITOR WELL SAMPLING	21	10 AUG 94	8 SEP 94
1230200220	OTHER FIELD ACTIVITIES	42	6 JUL 94	15 SEP 94
1230200230	DE-MOBE	10	15 SEP 94	28 SEP 94
1230200240	FIELD WORK COMPLETE	0	29 SEP 94	28 SEP 94
1230200250	DATA MANAGEMENT/QA	63	6 JUL 94	30 OCT 94

ACTIVITY CLASSIFICATION SUMMARY Legend: ■ Approved □ Pending ○ Not Started		Activity Bar/Early Dates Critical Activity Progress Bar Milestone/Flag Activity		Sheet 1 of 4
Plot Date: 2 MAR 94 Data Date: 25 FEB 94 Project Start: 10 OCT 94 Project Finish: 10 FEB 01		EGG ROCKY FLATS ADS 1255 / DU 7 PRESENT LANDFILL		Date: Revisior: Project Approved:
(C) Priave-a Systems Inc				

ACTIVITY ID	ACTIVITY DESCRIPTION	REM DUR	EARLY START	EARLY FINISH	FY94 FY95 FY96 FY97 FY98			
					INTERIM MEASURE DECISION			
1230200260	ANALYTICAL	123	3AUG94	2FEB95				
1230200270	HOT SAMPLE ANALYSIS	90	3AUG94	9DEC94				
1230200280	COLD SAMPLE ANALYSIS	60	3AUG94	26OCT94				
1230200290	DATA VALIDATION	63	27OCT94	2FEB95				
1230200300	BASELINE RISK ASSESSMENT	84	27OCT94	3MAR95				
1230200310	PLF ASSESSMENT	42	27OCT94	4JAN95				
1230200320	ELP AREA SOILS ASSESSMENT	42	5JAN95	3MAR95				
1230200330	DU 7 GROUNDWATER ASSESSMENT	42	5JAN95	3MAR95				
1230200340	OUTYEAR PLANNING DOCUMENT	60	31JAN94A	20MAY94				
1230200350	IM/IRA DECISION DOCUMENT	487	31JAN94A	6FEB95				
1230200360	ARARS DEVELOPMENT	21	31JAN94A	30MAR94				
1230200370	REGULATORY SUPPORT	63	2MAR94	31MAY94				
1230200380	MODELING SUPPORT	15	13JAN95	2FEB95				
1230200390	CONCEPTUAL DESIGN	80	4OCT94	2FEB95				
1230200400	DATA EVALUATION	42	29NOV94	2FEB95				
1230200410	ENVIRONMENTAL ASSESSMENT (E4)	160	25FEB94	12OCT94				
1230200420	TECHNOLOGY LITERATURE RESEARCH	7	31JAN94A	7MAR94				
1230200430	OPTIONS ANALYSIS	42	4OCT94	2DEC94				
1230200440	PREPARE IM/IRA DRAFT DECISION DOCUMENT	42	5JAN95	3MAR95				
1230200445	SUBMIT DRAFT IM/IRA DECISION DOC TO DOE	0	6MAR95	3MAR95				
1230200450	DOE RFD/HQ REVIEW DRAFT IM/IRA DECISION DOC	21	6MAR95	3APR95				
1230200455	REVISE DRAFT IM/IRA DECISION DOC PER DOE COMMENT	21	4APR95	3MAY95				
1230200460	SUBMIT DRAFT IM/IRA DECISION DOCUMENT TO CDH/EPA	0	4MAY95	3MAY95				
1230200470	CDH/EPA REVIEW DRAFT IM/IRA DECISION DOC	21	4MAY95	2JUN95				
1230200475	REVISE IM/IRA DECISION DOC PER EPA/CDH COMMENTS	21	5JUN95	3JUL95				
1230200480	SUBMIT FINAL IM/IRA DECISION DOC TO CDH/EPA	0	5JUL95	3JUL95				
1230200490	IM/IRA PUBLIC RESPONSIVENESS SUMMARY	60	12JUL95	4OCT95				
1230200495	SUBMIT IM/IRA RESPONSIVENESS SUMMARY	0	5OCT95	4OCT95				
1230200500	IM/IRA DD COMMENT RESOLUTION/REVISION	42	5OCT95	5DEC95				

Activity Classification Summary 1230200430 OPTIONS ANALYSIS 1230200440 PREPARE IM/IRA DRAFT DECISION DOCUMENT 1230200445 SUBMIT DRAFT IM/IRA DECISION DOC TO DOE 1230200450 DOE RFD/HQ REVIEW DRAFT IM/IRA DECISION DOC 1230200455 REVISE DRAFT IM/IRA DECISION DOC PER DOE COMMENT 1230200460 SUBMIT DRAFT IM/IRA DECISION DOCUMENT TO CDH/EPA 1230200470 CDH/EPA REVIEW DRAFT IM/IRA DECISION DOC 1230200475 REVISE IM/IRA DECISION DOC PER EPA/CDH COMMENTS 1230200480 SUBMIT FINAL IM/IRA DECISION DOC TO CDH/EPA 1230200490 IM/IRA PUBLIC RESPONSIVENESS SUMMARY 1230200495 SUBMIT IM/IRA RESPONSIVENESS SUMMARY 1230200500 IM/IRA DD COMMENT RESOLUTION/REVISION		Activity Bar/Early Dates Critical Activity Progress Bar Milestone/Flag Activity		DU07 EG&G ROCKY FLATS ADS 1255 / DU 7 PRESENT LANDFILL		Sheet 2 of 4 Date Revision Checked Approved	
--	--	--	--	--	--	---	--

ACTIVITY ID	ACTIVITY DESCRIPTION	REM DUR	EARLY START	EARLY FINISH
1230200510	IM/IRA DD FINAL EPA/CDH/DOE REVIEW	42	6DEC95	9FEB96
1230200520	SUBMIT FINAL IM/IRA DD AND RESPONSIVENESS SUMM	0	12FEB96	9FEB96
1230200530	REMEDIAL DESIGN	397	4MAY95	3DEC96
1230200540	IM/DESIGN WORKPLAN	42	4MAY95	3JUL95
1230200545	SUBMIT IM/DESIGN WORKPLAN TO DOE	0	5JUL95	3JUL95
1230200550	DOE RFO/HQ REVIEW IM WORKPLAN	15	5JUL95	25JUL95
1230200555	REVISE IM WORKPLAN PER DOE COMMENTS	10	26JUL95	8AUG95
1230200558	SUBMIT IM DESIGN WORKPLAN TO CDH/EPA	0	9AUG95	8AUG95
1230200560	CDH/EPA REVIEW IM WORKPLAN	15	9AUG95	29AUG95
1230200565	REVISE IM WORKPLAN PER EPA/CDH COMMENTS	5	30AUG95	6SEP95
1230200570	IM DESIGN WORKPLAN COMPLETE	0	7SEP95	6SEP95
1230200580	PHASE I IM/IRA IMPLEMENTATION DDC/DRAFT ITL II)	100	7SEP95	5FEB96
1230200585	SUBMIT PHASE I IM/IRA IMP DOC TO DOE	0	6FEB96	5FEB96
1230200590	DOE RFO/HQ REVIEW IM/IRA IMPLEMENTATION DOC	21	6FEB96	5MAR96
1230200595	REVISE IM/IRA IMP DOC PER DOE COMMENTS	21	6MAR96	4APR96
1230200600	SUBMIT DRAFT PHASE I IM/IRA IMP DOC TO CDH/EPA	0	5APR96	4APR96
1230200610	CDH/EPA REVIEW DRAFT IM/IRA IMP DOC	42	5APR96	4JUN96
1230200620	REVISE IM/IRA IMPLEMENTATION DOCUMENT	63	5JUN96	3SEP96
1230200630	SUBMIT TITLE II DESIGN TO CDH/EPA	0	4SEP96	3SEP96
1230200640	CDH/EPA REVIEW/REVISION CYCLE	42	4SEP96	31OCT96
1230200650	FINAL TITLE II DESIGN W/CONSTRUCTION SCHEDULE	21	1NOV96	3DEC96
1232000660	BEGIN IM/IRA CONSTRUCTION PROCESS	0	6MAR96	5MAR96
1232000670	DAVIS BACON DETERMINATION	5	6MAR96	12MAR96
1232000680	DAVIS-BACON APPROVAL	0	13MAR96	12MAR96
1232000690	CONTRACT DEFINITION/ADVANCE NOTICE	60	13MAR96	6JUN96
1232000700	SUBCONTRACT BOILER PLATE (PROCUREMENT)	10	7JUN96	20JUN96
1232000710	SUBCONTRACT DIVISION	10	21JUN96	5JUL96
1232000720	HWCP DRAFT/F5 DRAFT TITLE II DESIGN)	10	8JUL96	19JUL96

ACTIVITY C ASSOCIATION SUMMARY

■ WORKBOOK

Plot Date 2MAR94
Data Date 25FEB94
Project Start 10C191
Project Finish 16FEB01

Activity Bar/Early Dates
Critical Activity
Progress Bar
Milestone/Flag Activity

0007

EG&G ROCKY FLATS

ADS 1255 / DU 7 PRESENT LANDFILL

SHEET 3 OF 4

ACTIVITY ID	ACTIVITY DESCRIPTION	PEM DUR	EARLY START	EARLY FINISH
1232000730	ISSUE RFP	35	22JUL96	9SEP96
1232000740	PRE-BID TOUR	1	10SEP96	10SEP96
1232000750	BID PROPOSAL RECEIVED	1	11SEP96	11SEP96
1232000760	BID PROPOSAL TECHNICAL REVIEW	10	12SEP96	25SEP96
1232000770	SUBCONTRACT AWARD	0	26SEP96	25SEP96
1232000780	NOTICE TO PROCEED	1	4DEC96	4DEC96
1232000790	RECEIVE SUBMITTALS	15	5DEC96	2JAN97
1232000800	APPROVE SUBMITTALS	10	3JAN97	16JAN97
1232000810	FINALIZE IWCP	10	17JAN97	30JAN97
1232000820	SUBCONTRACTOR TRAINING	15	31JAN97	20FEB97
1232000830	SUBCONTRACTOR MOBILIZATION	10	21FEB97	6MAR97
1232000840	CONSTRUCTION	230	7MAR97	9FEB98
1232000850	POST CONSTRUCTION	30	10FEB98	23MAR98
1230400000	POST CLOSURE PERFORMANCE MONITORING	747	18FEB98	16FEB01
1231109400	PROJECT SUPPORT & ADMINISTRATION	149	10C193A	27SEP94
1231109500	PROJECT SUPPORT & ADMINISTRATION	248	28SEP94	26SEP95
1231109600	PROJECT SUPPORT & ADMINISTRATION	249	27SEP95	25SEP96
1231109700	PROJECT SUPPORT & ADMINISTRATION	249	26SEP96	25SEP97
1231109800	PROJECT SUPPORT & ADMINISTRATION	249	26SEP97	25SEP98
1231109900	PROJECT SUPPORT & ADMINISTRATION	249	28SEP98	27SEP99
1231120000	PROJECT SUPPORT & ADMINISTRATION	249	28SEP99	26SEP00

CONSTRUCTION

PERFORMANCE MONITORING

PROJECT SUPPORT

EG&G ROCKY FLATS

ADS 1255 / DU 7 PRESENT LANDFILL

Activity Classification Summary

Project Date: 24Mar94

Project Name: EG&G ROCKY FLATS

Project Number: 1231109400

Activity Bar/Early Dates

Project Activity

Progress Bar

Milestone/Flag Activity

Sheet 4 of 4

DU07

Plotted Date: 24Mar94

Plotted By: J. B. A.

Plotted For: 1231109400

Checked: Approved
