

00977 RF 94

DUE
DATE

ACTION
DIST LTR ENC

BERMAN, H S		
CARNIVAL, G J		
COPP, R D		
CORDOVA, R C		
DAVIS, J G		
FERRERA, D W		
FRANZ, W A		
HANNI, B J		
HEALY, T J		
HEDAH, T G		
HILBIG, J G		
HUTCHINS, N M		
KELL, R E		
KIRBY, W A		
KUESTER, A W		
MAHAFFEY, J W		
MANN, H P		
MARX, G E		
McKENNA, F G		
MORGAN, R V		
PIZZUTO, V M		
POTTER, G L		
SANDLIN, N B		
SATTERWHITE, D G		
SCHUBERT, A L		
SETLOCK, G H		
STIGER, S G	XX	
SULLIVAN, M T		
SWANSON, E R		
WILKINSON, R B		
WILSON, J M		

O'Rourke T XX
Busby W XX
O'Neill K XX

CORRES CONTROL x x
ADMIN RECORD/080 x 2
PATS/T130G

Reviewed for Addressee
Corres Control RFP

3-11-94 C
DATE BY

Ref Ltr #

DOE ORDER # 5400 1

Department of Energy

ROCKY FLATS OFFICE
P O BOX 928
GOLDEN COLORADO 80402 0928



1 00023256

MAR 08 1994

94-DOE-02372

Mr Martin Hestmark
U S Environmental Protection Agency, Region VIII
ATTN Rocky Flats Project Manager, 8HWM-RI
999 18th Street, Suite 500, 8WM-C
Denver, Colorado 80202-2405

Mr Gary Baughman
Hazardous Waste Facilities Unit Leader
Colorado Department of Health
4300 Cherry Creek Drive South
Denver, Colorado 80222-1530

Gentlemen

Over the past several months, staff members from the Department of Energy (DOE), the Environmental Protection Agency, and the Colorado Department of Health have discussed methods to reduce costs and speed up the environmental cleanup at the Rocky Flats Plant. During these discussions, it was decided, in principle, to rescope the original schedules for Operable Units (OUs) 7 and 11, beginning with the Phase I Resource Conservation and Recovery Act Facility Investigation/Remedial Investigation (RFI/RI) Work Plans. As part of this rescoping, the original Phase I Work Plans for both OU-7 and 11 will be modified and several of the Table VI Milestones listed in the Interagency Agreement will be deleted or replaced by technical memorandums. In addition, we propose the transfer of Individual Hazardous Substance Sites 166 1, 166 2, 166 3, and 167 1 from OU-6 to OU-7.

The enclosure contains highlights of the proposed changes and new schedules. Your review, comments, and formal approval of the revised scopes of these OUs are requested.

The DOE would like to acknowledge the efforts of all parties in developing this rescoping strategy, a strategy that streamlines our regulatory and technical process to promote cleanup rather than paperwork. We look forward to continued cooperative efforts and the improvement of the overall performance of our environmental restoration effort.

ADMIN RECO

A-OU07-000271

M Hestmark & G Baughman
94-DOE-02372

2

MAR 08 1994

If you have any specific questions concerning the rescoping effort, please direct them to Jen Pepe at 966-2184, or Dave George at 966-5669

Sincerely,



Jessie Roberson
Acting Assistant Manager for
Environmental Restoration

Enclosure

cc w/Enclosure
F Lockhart, ER, RFO
S Stiger, AGMERM
D George, ER, RFO
T O'Rourke, EG&G
W Busby, EG&G
K O'Neill, EG&G

OPERABLE UNIT 11 PROPOSED RESCOPED ACTIVITIES

The following original IAG milestones were delivered as scheduled

SUBMIT DRAFT PHASE I RFI/RI WORK PLAN

JUNE 8, 1990

SUBMIT FINAL PHASE I RFI/RI WORK PLAN

JANUARY 2, 1992

The milestone SUBMIT DRAFT PHASE I RFI/RI REPORT has been increased in scope. The original milestone was scheduled for delivery on September 20, 1994. With the change in scope, the target date for completion is scheduled for at or near September 20, 1994.

Phase I and Phase II are proposed to be combined to a single phase to reduce the duration of closure.

The milestone SUBMIT DRAFT PHASE I PROPOSED IM/IRA DECISION DOCUMENT is assumed to include a Justification for No Further Action.

All of the milestones following are assumed to be deleted per the Justification for No Further Action.

OPERABLE UNIT 11 IAG TABLE VI MILESTONES PROPOSED TO BE REVISED OR DELETED

<u>MILESTONE</u>	<u>POTENTIAL DISPOSITION</u>
SUBMIT DRAFT PHASE I RFV/RI REPORT	Revised*
SUBMIT FINAL PHASE I RFV/RI REPORT	Revised*
SUBMIT DRAFT PHASE I PROPOSED IM/IRA DD	
SUBMIT FINAL PHASE I PROPOSED IM/IRA DD	
SUBMIT PHASE I IM/IRA RESPONSIVENESS SUMMARY	
SUBMIT PHASE I FINAL IM/IRA DECISION DOCUMENT AND FINAL RESPONSIVENESS SUMMARY	
SUBMIT IM DESIGN CD/RD WORK PLAN	Deleted**
SUBMIT PHASE I IM/IRA IMPLEMENTATION DOCUMENT	Deleted**
SUBMIT TITLE II DESIGN	Deleted**
BEGIN PHASE I IM/IRA CONSTRUCTION	Deleted**
SUBMIT DRAFT PHASE II RFI/RI WORK PLAN	Deleted*
SUBMIT FINAL PHASE II RFI/RI WORK PLAN	Deleted*
SUBMIT DRAFT PHASE II RFI/RI REPORT	Deleted*
SUBMIT FINAL PHASE II RFI/RI REPORT	Deleted*
SUBMIT DRAFT PHASE II CMS/FS REPORT	Deleted*
SUBMIT FINAL PHASE II CMS/FS REPORT	Deleted*
SUBMIT DRAFT PHASE II PP	Deleted*
SUBMIT FINAL PHASE II PP	Deleted*
SUBMIT DRAFT PHASE II RESPONSIVENESS SUMMARY	Deleted*
SUBMIT FINAL PHASE II RESPONSIVENESS SUMMARY	Deleted*
SUBMIT DRAFT PHASE II CAD/FAD	Revised**
SUBMIT FINAL PHASE II CAD/FAD	Revised**
SUBMIT CD/RD WORK PLAN	Revised**
SUBMIT DRAFT TITLE II DESIGN PLANS	Revised**
SUBMIT FINAL TITLE II DESIGN PLANS	Revised**
BEGIN PHASE II CA/RA CONSTRUCTION	Revised**

*Integration of Phase I & Phase II Requirements

** Assuming No Further Action Justification Per Integrated Phases RFI/RI Results

OPERABLE UNIT 7 PROPOSED RESCOPED ACTIVITIES

The following original IAG milestones were delivered as scheduled.

SUBMIT DRAFT PHASE I RFI/RI WORK PLAN
SUBMIT FINAL PHASE I RFI/RI WORK PLAN

JUNE 8, 1990
AUGUST 28, 1991

The following milestone was delayed due to a Stop Work Order

SUBMIT DRAFT PHASE I RFI/RI REPORT

OCTOBER 12, 1993

The remedial action necessary to close Operable Unit 7 is guided by the CHWA. In following the guidance of the CHWA, some previously planned activities can be eliminated. Therefore, several milestones are proposed to be revised or deleted.

The Phase II RFI/RI will be included within the IM/IRA document. This action will delete all Phase II RFI/RI milestones. An extension will be required for the IM/IRA DD due to its increased scope. The following IM/IRA DD proposed revised milestones are as follows:

Milestone

SUBMIT IM/IRA DECISION DOCUMENT
AGENCY APPROVAL IM/IRA DD
IM/IRA DD APPROVED

In addition, several milestones beyond the Phase II RFI/RI are proposed to be modified as a result of the IM/IRA DD.

Milestone

IM DESIGN WORK PLAN COMPLETE
SUBMIT DRAFT PHASE I IM/IRA IMPLEMENTATION DOCUMENT
SUBMIT TITLE II DESIGN
BEGIN CONSTRUCTION PROCESS

OPERABLE UNIT 7 IAG TABLE VI MILESTONES PROPOSED TO BE REVISED OR DELETED


<u>MILESTONE</u>	<u>POTENTIAL DISPOSITION</u>
SUBMIT DRAFT PHASE I RFV/RI REPORT	Deleted*
SUBMIT FINAL PHASE I RFV/RI REPORT	Deleted*
SUBMIT DRAFT PHASE I IM/IRA DD	Revised****
SUBMIT FINAL PHASE I IM/IRA DD	Revised****
SUBMIT IM/IRA RESPONSIVENESS SUMMARY	Revised****
SUBMIT FINAL PHASE I IM/IRA DD	Revised****
SUBMIT IM/DESIGN WORK PLAN	Revised***
SUBMIT PHASE I IM/IRA IMPLEMENTATION DOCUMENT	Revised***
SUBMIT TITLE II DESIGN	Revised***
BEGIN PHASE I IM/IRA CONSTRUCTION	Revised***
SUBMIT DRAFT PHASE II RFI/RI WORK PLAN	Deleted**
SUBMIT FINAL PHASE II RFI/RI WORK PLAN	Deleted**
SUBMIT DRAFT PHASE RFV/RI REPORT	Deleted**
SUBMIT FINAL PHASE RFV/RI REPORT	Deleted**
SUBMIT DRAFT PHASE II CMS/FS REPORT	Deleted**
SUBMIT FINAL PHASE II CMS/FS REPORT	Deleted**
SUBMIT DRAFT PHASE II PP	Deleted****
SUBMIT FINAL PHASE II PP	Deleted****
SUBMIT DRAFT PHASE II RESPONSIVENESS SUMMARY	Deleted****
SUBMIT FINAL PHASE II RESPONSIVENESS SUMMARY	Deleted****
SUBMIT DRAFT PHASE II CAD/FAD	Revised***
SUBMIT FINAL PHASE II CAD/FAD	Revised***
SUBMIT CD/RD WORK PLAN	Deleted***
SUBMIT DRAFT TITLE II DESIGN	Deleted***
SUBMIT TITLE II DESIGN	Deleted***
BEGIN CA/RA CONSTRUCTION	Deleted***

*Phase I requirement satisfied in revised FSP Tech Memo

**Integration of Phase I & Phase II requirements

*** Final Action will be significantly streamlined due to IM/IRA accomplishing closure

****Revised to incorporate Phase II RFI/RI Report requirements

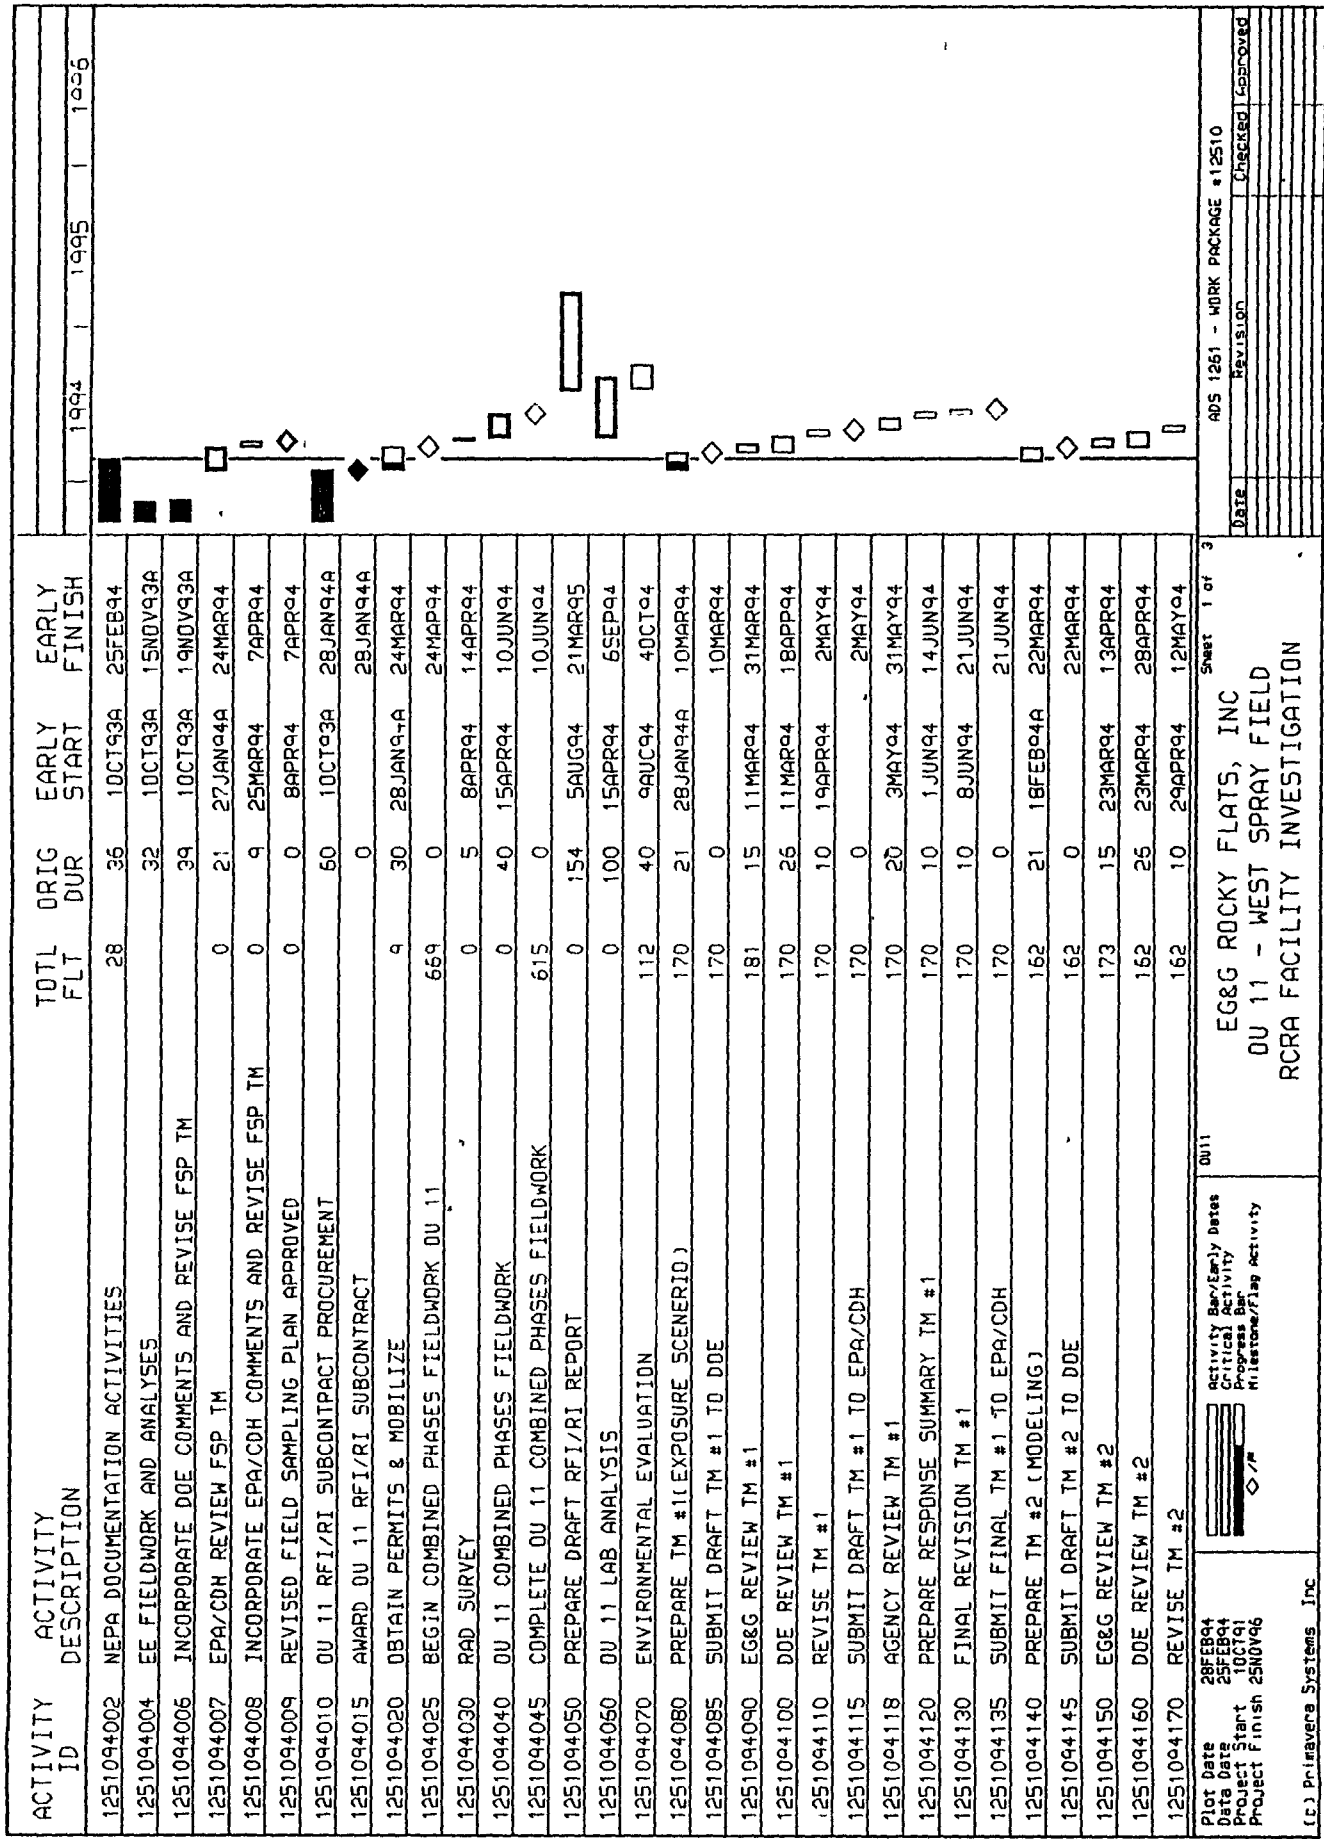

ACTIVITY ID	ACTIVITY DESCRIPTION	TOTL FLT	ORIG DUP	EARLY START	EARLY FINISH
1251094175	SUBMIT DRAFT TM #2 TO EPA/CDH	162	0		12MAY94
1251094180	AGENCY REVIEW TM #2	162	20	13MAY94	10JUN94
1251094190	PREPARE RESPONSE SUMMARY TM #2	162	10	13JUN94	24JUN94
1251094200	FINAL REVISION TM #2	162	10	20JUN94	1JUL94
1251094205	SUBMIT FINAL TM #2 TO EPA/CDH	162	0		1JUL94
1251094210	PREPARE DRAFT TM #3	0	21	22AUG94	20SEP94
1251094215	SUBMIT DRAFT TM #3 TO DOE	36	0		20SEP94
1251094220	EG&G REVIEW TM #3	47	15	21SEP94	11OCT94
1251094230	DOE REVIEW TM #3	36	26	21SEP94	26OCT94
1251094240	REVISE TM #3	36	10	27OCT94	9NOV94
1251094245	SUBMIT DRAFT TM #3 TO EPA/CDH	36	0		9NOV94
1251094250	AGENCY REVIEW TM #3	36	20	10NOV94	9DEC94
1251094260	PREPARE RESPONSE SUMMARY TM #3	36	10	12DEC94	23DEC94
1251094270	FINAL REVISION TM #3	36	10	19DEC94	9JAN95
1251094275	SUBMIT FINAL TM #3 TO EPA/CDH	36	0		9JAN95
1251094280	PREPARE DRAFT TM #4 (TOXICITY)	0	21	21SEP94	19OCT94
1251094285	SUBMIT DRAFT TM #4 TO DOE	0	0		19OCT94
1251094290	EG&G REVIEW TM #4	11	15	20OCT94	9NOV94
1251094300	DOE REVIEW TM #4	0	26	20OCT94	28NOV94
1251094310	REVISE TM #4	0	10	29NOV94	12DEC94
1251094315	SUBMIT DRAFT TM #4 TO EPA/CDH	0	0		12DEC94
1251094320	AGENCY REVIEW TM #4	0	20	13DEC94	17JAN95
1251094330	PREPARE RESPONSE SUMMARY TM #4	0	10	18JAN95	31JAN95
1251094340	FINAL REVISION TM #4	0	10	25JAN95	7FEB95
1251094345	SUBMIT FINAL TM #4 TO EPA/CDH	0	0		7FEB95
1251094347	CONDUCT HHRA	0	15	8FEB95	28FEB95
1251094348	BASELINE RISK ASSESSMENT	0	15	1MAR95	21MAR95
1251094350	SUBMIT DRAFT RFI/RI REPORT TO DOE	0	0	22MAR95	21MAR95
1251094355	DOE REVIEW DRAFT RFI/RI REPORT	0	21	22MAR95	20APR95
1251094360	REVISE DRAFT RFI/RI REPORT	0	21	21APR95	19MAY95
1251094365	SUBMIT RFI/RI REPORT TO EPA/CDH	0	0	22MAY95	19MAY95

Plot Date 28FEB94

Data Date 25FEB94

Project Start 10CT91

Project Finish 25NOV96

Activity Bar/Early Dates

Physical Activity

Milestone/Flag Activity

0011

Swat 2 of 3

EG&G ROCKY FLATS, INC

00 11 - WEST SPRAY FIELD

RCRA FACILITY INVESTIGATION

(c) Primavera Systems, Inc

AUS 1261 - WORK PACKAGE #12510

Revision

Checked

Approved

ACTIVITY ID	ACTIVITY DESCRIPTION	TOTL FLT	ORIG DUR	EARLY START	EARLY FINISH
1251094370	AGENCY REVIEW DRAFT RFI/RI REPORT	0	21	22MAY95	20JUN95
1251094375	REVISE DRAFT RFI/RI REPORT	0	21	21JUN95	20JUL95
1251094380	SUBMIT FINAL RFI/RI REPORT	0	0	21JUL95	20JUL95
1251094385	EPA/CDH REVIEW RFI/RI FOR FINAL APPROVAL	0	10	21JUL95	3AUG95
1251094387	RFI/RI REPORT APPROVED	0	0	4AUG95	3AUG95
1251094390	PREPARE DRAFT NO FURTHER ACTION JUSTIFICATION	0	42	4AUG95	30CT95
1251094400	SUBMIT DRAFT NO FURTHER ACTION JUSTIFICATION TO	0	0	40CT95	30CT95
1251094410	DOE REVIEW DRAFT NFAJD	0	21	40CT95	1NOV95
1251094420	REVISE DRAFT NFAJD	0	21	2NOV95	4DEC95
1251094430	SUBMIT DRAFT NFAJD TO EPA/CDH	0	0	5DEC95	4DEC95
1251094440	EPA/CDH REVIEW NFAJD	0	62	5DEC95	7MAR96
1251094450	REVISE NFAJD	0	41	8MAR96	6MAY96
1251094460	SUBMIT FINAL NFAJD TO EPA/CDH	0	0	7MAY96	6MAY96
1251094470	EPA/CDH REVIEW AND APPROVE NFAJD	0	21	7MAY96	5JUN96
1251094480	NO FURTHER ACTION JUSTIFICATION APPROVED	0	0	6JUN96	5JUN96
1251094490	PUBLIC COMMENT PERIOD	0	58	6JUN96	27AUG96
1251094500	PUBLIC COMMENT RESOLUTION	0	21	28AUG96	26SEP96
1251094510	PREPARE RECORD OF DECISION	0	42	27SEP96	25NOV96
1251094520	RECORD OF DECISION ISSUED	0	0	26NOV96	25NOV96

Plot Date 28FEB94	Activity Bar/Early Dates	<div> <div>DU11</div> <div>EG&G ROCKY FLATS, INC</div> <div>OU 11 - WEST SPRAY FIELD</div> <div>RCRA FACILITY INVESTIGATION</div> </div>	<div> <div>AD5 1261 - WORK PACKAGE #12510</div> <div>Checked</div> <div>Approved</div> </div>
Date Date 25FEB94	Activity Bar/Early Dates		
Project Start 10CT91	Activity Bar/Early Dates		
Project Finish 25NOV96	Activity Bar/Early Dates		
(c) Primavera Systems Inc			

ACTIVITY ID	ACTIVITY DESCRIPTION	REM DUP	EARLY START	EARLY FINISH
1230200010	AWARD SUBCONTRACT	0		21JAN94A
1230200020	SUBCONTRACTOR PROJECT MANAGEMENT	528	21JAN94A	9APR96
1230200030	PHASE I DATA ASSESSMENT	37	21JAN94A	19APR94
1230200040	PHASE I DATA EVALUATION	32	21JAN94A	12APR94
1230200050	PHASE I DATA PRESENTATION	5	13APR94	19APR94
1230200060	SCOPING MEETINGS/DQO DEVELOPMENT	3	28JAN94A	1MAR94
1230200070	PHASE I RFI/RI WORKPLAN MODIFICATION	40	11FEB94A	22APR94
1230200075	SUBMIT PHASE I WORKPLAN MOD TO DOE	0	25APR94	22APR94
1230200080	DOE REVIEW PHASE I WORKPLAN MOD	10	25APR94	6MAY94
1230200085	REVISE PHASE I WORKPLAN MOD PER DOE COMMENTS	10	9MAY94	20MAY94
1230200088	SUBMIT PHASE I WORK PLAN MOD TO EPA/CDH	0	23MAY94	20MAY94
1230200090	EPA/CDH REVIEW PHASE I WORKPLAN MOD	15	23MAY94	13JUN94
1230200095	REVISE PHASE I WORKPLAN MOD PER EPA/CDH COMMENTS	10	14JUN94	27JUN94
1230200100	OU 7 WORKPLAN MODIFICATION APPROVED	0	28JUN94	27JUN94
1230200110	WORKPLAN IMPLEMENTATION PLAN	21	23JAN94A	25MAP94
1230200120	HEALTH AND SAFETY PLAN ADDENDUM	6	14JUN94	21JUN94
1230200130	TRAIN AND BADGE S/C PERSONNEL	21	28MAR94	26APR94
1230200140	OBTAIN PERMITS	10	28MAR94	11APR94
1230200150	READINESS REVIEW	5	28JUN94	5JUL94
1230200160	READINESS REVIEW COMPLETE	0	6JUL94	5JUL94
1230200170	RFI/RI IMPLEMENTATION OF TECH MEMO	60	6JUL94	28SEP94
1230200180	MOBILIZE	15	6JUL94	26JUL94
1230200190	MONITOR WELL/BORING INSTALLATION	35	27JUL94	14SEP94
1230200200	SOIL SAMPLING	21	27JUL94	24AUG94
1230200210	MONITOR WELL SAMPLING	21	10AUG94	8SEP94
1230200220	OTHER FIELD ACTIVITIES	42	6JUL94	15EP94
1230200230	DE-MOBE	10	15SEP94	28SEP94
1230200240	FIELD WORK COMPLETE	0	29SEP94	28SEP94
1230200250	DATA MANAGEMENT/QA	63	6JUL94	30CT94

Plot Date 2MAR94

Data Date 25FEB94

Project Start 10C191

Project Finish 16FEB01

Activity Classification SUMMARY

NON-DOCK

Activity Bar/Early Dates

Critical Activity

Progress Update

Milestone/Flag Activity

0007

EG&G ROCKY FLATS

ADS 1255 / OU 7 PRESENT LANDFILL

Sheet 1 of 4

Revision

Checked/Approved

(c) Primavera Systems, Inc.

ACTIVITY ID	ACTIVITY DESCRIPTION	REM DUR	EARLY START	EARLY FINISH
1230200260	ANALYTICAL	123	3AUG94	2FEB95
1230200270	HOT SAMPLE ANALYSIS	90	3AUG94	9DEC94
1230200280	COLD SAMPLE ANALYSIS	60	3AUG94	26OCT94
1230200290	DATA VALIDATION	63	27OCT94	2FEB95
1230200300	BASELINE RISK ASSESSMENT	84	27OCT94	3MAR95
1230200310	PLF ASSESSMENT	42	27OCT94	4JAN95
1230200320	ELP AREA SOILS ASSESSMENT	42	5JAN95	3MAR95
1230200330	OU 7 GROUNDWATER ASSESSMENT	42	5JAN95	3MAR95
1230200340	OUTYEAR PLANNING DOCUMENT	60	31JAN94A	20MAY94
1230200350	IM/IRA DECISION DOCUMENT	487	31JAN94A	9FEB96
1230200360	ARARs DEVELOPMENT	21	31JAN94A	30MAR94
1230200370	REGULATORY SUPPORT	63	2MAR94	31MAY94
1230200380	MODELING SUPPORT	15	13JAN95	2FEB95
1230200390	CONCEPTUAL DESIGN	80	4OCT94	2FEB95
1230200400	DATA EVALUATION	42	29NOV94	2FEB95
1230200410	ENVIRONMENTAL ASSESSMENT(EA)	160	25FEB94	12OCT94
1230200420	TECHNOLOGY LITERATURE RESEARCH	7	31JAN94A	7MAR94
1230200430	OPTIONS ANALYSIS	42	4OCT94	2DEC94
1230200440	PREPARE IM/IRA DRAFT DECISION DOCUMENT	42	5JAN95	3MAR95
1230200445	SUBMIT DRAFT IM/IRA DECISION DOC TO DOE	0	6MAR95	3MAR95
1230200450	DOE RFO/HQ REVIEW DRAFT IM/IRA DECISION DOC	21	6MAR95	3APR95
1230200455	REVISE DRAFT IM/IRA DECISION DOC PER DOE COMMENT	21	4APR95	3MAY95
1230200460	SUBMIT DRAFT IM/IRA DECISION DOCUMENT TO CDH/EPA	0	4MAY95	3MAY95
1230200470	CDH/EPA REVIEW DRAFT IM/IRA DECISION DOC	21	4MAY95	2JUN95
1230200475	REVISE IM/IRA DECISION DOC PER EPA/CDH COMMENTS	21	5JUN95	3JUL95
1230200480	SUBMIT FINAL IM/IRA DECISION DOC TO CDH/EPA	0	5JUL95	3JUL95
1230200490	IM/IRA PUBLIC RESPONSIVENESS SUMMARY	60	12JUL95	4OCT95
1230200495	SUBMIT IM/IRA RESPONSIVENESS SUMMARY	0	5OCT95	4OCT95
1230200500	IM/IRA DD COMMENT RESOLUTION/REVISION	42	5OCT95	5DEC95

ACTIVITY ID

ACTIVITY DESCRIPTION

REM DUR

EARLY START

EARLY FINISH

1230200260

ANALYTICAL

123

3AUG94

2FEB95

1230200270

HOT SAMPLE ANALYSIS

90

3AUG94

9DEC94

1230200280

COLD SAMPLE ANALYSIS

60

3AUG94

26OCT94

1230200290

DATA VALIDATION

63

27OCT94

2FEB95

1230200300

BASELINE RISK ASSESSMENT

84

27OCT94

3MAR95

1230200310

PLF ASSESSMENT

42

27OCT94

4JAN95

1230200320

ELP AREA SOILS ASSESSMENT

42

5JAN95

3MAR95

1230200330

OU 7 GROUNDWATER ASSESSMENT

42

5JAN95

3MAR95

1230200340

OUTYEAR PLANNING DOCUMENT

60

31JAN94A

20MAY94

1230200350

IM/IRA DECISION DOCUMENT

487

31JAN94A

9FEB96

1230200360

ARARs DEVELOPMENT

21

31JAN94A

30MAR94

1230200370

REGULATORY SUPPORT

63

2MAR94

31MAY94

1230200380

MODELING SUPPORT

15

13JAN95

2FEB95

1230200390

CONCEPTUAL DESIGN

80

4OCT94

2FEB95

1230200400

DATA EVALUATION

42

29NOV94

2FEB95

1230200410

ENVIRONMENTAL ASSESSMENT(EA)

160

25FEB94

12OCT94

1230200420

TECHNOLOGY LITERATURE RESEARCH

7

31JAN94A

7MAR94

1230200430

OPTIONS ANALYSIS

42

4OCT94

2DEC94

1230200440

PREPARE IM/IRA DRAFT DECISION DOCUMENT

42

5JAN95

3MAR95

1230200445

SUBMIT DRAFT IM/IRA DECISION DOC TO DOE

0

6MAR95

3MAR95

1230200450

DOE RFO/HQ REVIEW DRAFT IM/IRA DECISION DOC

21

6MAR95

3APR95

1230200455

REVISE DRAFT IM/IRA DECISION DOC PER DOE COMMENT

21

4APR95

3MAY95

1230200460

SUBMIT DRAFT IM/IRA DECISION DOCUMENT TO CDH/EPA

0

4MAY95

3MAY95

1230200470

CDH/EPA REVIEW DRAFT IM/IRA DECISION DOC

21

4MAY95

2JUN95

1230200475

REVISE IM/IRA DECISION DOC PER EPA/CDH COMMENTS

21

5JUN95

3JUL95

1230200480

SUBMIT FINAL IM/IRA DECISION DOC TO CDH/EPA

0

5JUL95

3JUL95

1230200490

IM/IRA PUBLIC RESPONSIVENESS SUMMARY

60

12JUL95

4OCT95

1230200495

SUBMIT IM/IRA RESPONSIVENESS SUMMARY

0

5OCT95

4OCT95

1230200500

IM/IRA DD COMMENT RESOLUTION/REVISION

42

5OCT95

ACTIVITY ID	ACTIVITY DESCRIPTION	REM DUR	EARLY START	EARLY FINISH
1230200510	IM/IRA DD FINAL EPA/CDH/DOE REVIEW	42	6DEC95	9FEB96
1230200520	SUBMIT FINAL IM/IRA DD AND RESPONSIVENESS SUMM	0	12FEB96	9FEB96
1230200530	REMEDIAL DESIGN	397	4MAY95	3DEC96
1230200540	IM/DESIGN WORKPLAN	42	4MAY95	3JUL95
1230200545	SUBMIT IM/DESIGN WORKPLAN TO DOE	0	5JUL95	3JUL95
1230200550	DOE RFO/HQ REVIEW IM WORKPLAN	15	5JUL95	25JUL95
1230200555	REVISE IM WORKPLAN PER DOE COMMENTS	10	26JUL95	8AUG95
1230200558	SUBMIT IM DESIGN WORKPLAN TO CDH/EPA	0	9AUG95	8AUG95
1230200560	CDH/EPA REVIEW IM WORKPLAN	15	9AUG95	29AUG95
1230200565	REVISE IM WORKPLAN PER EPA/CDH COMMENTS	5	30AUG95	6SEP95
1230200570	IM DESIGN WORKPLAN COMPLETE	0	7SEP95	6SEP95
1230200580	PHASE I IM/IRA IMPLEMENTATION DOC(DRAFT TTL II)	100	7SEP95	5FEB96
1230200585	SUBMIT PHASE I IM/IRA IMP DOC TO DOE	0	6FEB96	5FEB96
1230200590	DOE RFO/HQ REVIEW IM/IRA IMPLEMENTATION DOC	21	6FEB96	5MAR96
1230200595	REVISE IM/IRA IMP DOC PER DOE COMMENTS	21	6MAR96	4APR96
1230200600	SUBMIT DRAFT PHASE I IM/IRA IMP DOC TO CDH/EPA	0	5APR96	4APR96
1230200610	CDH/EPA REVIEW DRAFT IM/IRA IMP DOC	42	5APR96	4JUN96
1230200620	REVISE IM/IRA IMPLEMENTATION DOCUMENT	63	5JUN96	3SEP96
1230200630	SUBMIT TITLE II DESIGN TO CDH/EPA	0	4SEP96	3SEP96
1230200640	CDH/EPA REVIEW/REVISION CYCLE	42	4SEP96	31OCT96
1230200650	FINAL TITLE II DESIGN W/CONSTRUCTION SCHEDULE	21	1NOV96	3DEC96
1232000660	BEGIN IM/IRA CONSTRUCTION PROCESS	0	6MAR96	5MAR96
1232000670	DAVIS BACON DETERMINATION	5	6MAR96	12MAR96
1232000680	DAVIS-BACON APPROVAL	0	13MAR96	12MAR96
1232000690	CONTRACT DEFINITION/ADVANCE NOTICE	60	13MAR96	6JUN96
1232000700	SUBCONTRACT BOILER PLATE(PROCUREMENT)	10	7JUN96	20JUN96
1232000710	SUBCONTRACT DIVISION	10	21JUN96	5JUL96
1232000720	INCP DRAFT(FS DRAFT TITLE II DESIGN)	10	8JUL96	19JUL96

Plot Date 2MAR94

Data Date 2FEB94

Project Start 1DEC91

Project Finish 18FEB01

Activity Classification Summary

Activity Bar/Early Dates

Critical Activity

Progress

Milestone/Flag Activity

0007

EG&G ROCKY FLATS

ADS 1255 / DU 7 PRESENT LANDFILL

Sheet 3 of 4

Checked

Approved

ACTIVITY ID	ACTIVITY DESCRIPTION	REM DUR	EARLY S-ART	EARLY FINISH	FY94	FY95	FY-6	FY97	FY98
1232000730	ISSUE RFP	35	22JUL96	9SEP96					
1232000740	PRE-BID TOUR	1	10SEP96	10SEP96					
1232000750	BID PROPOSAL RECIEVED	1	11SEP96	11SEP96					
1232000760	BID PROPOSAL TECHNICAL REVIEW	10	12SEP96	25SEP96					
1232000770	SUBCONTRACT AWARD	0	26SEP96	25SEP96					
1232000780	NOTICE TO PROCEED	1	4DEC96	4DEC96					
1232000790	RECEIVE SUBMITTALS	15	5DEC96	2JAN97					
1232000800	APPROVE SUBMITTALS	10	3JAN97	16JAN97					
1232000810	FINALIZE IMCP	10	17JAN97	30JAN97					
1232000820	SUBCONTRACTOR TRAINING	15	31JAN97	20FEB97					
1232000830	SUBCONTRACTOR MOBILIZATION	10	21FEB97	6MAR97					
1232000840	CONSTRUCTION	230	7MAR97	9FEB98					
1232000850	POST CONSTRUCTION	30	10FEB98	23MAR98					
1230400000	POST CLOSURE PERFORMANCE MONITORING	747	18FEB98	16FEB01					
1231109400	PROJECT SUPPORT & ADMINISTRATION	149	10CT93A	27SEP94					
1231109500	PROJECT SUPPORT & ADMINISTRATION	248	28SEP94	26SEP95					
1231109600	PROJECT SUPPORT & ADMINISTRATION	249	27SEP95	25SEP96					
1231109700	PROJECT SUPPORT & ADMINISTRATION	249	26SEP96	25SEP97					
1231109800	PROJECT SUPPORT & ADMINISTRATION	249	26SEP97	25SEP98					
1231109900	PROJECT SUPPORT & ADMINISTRATION	249	28SEP98	27SEP99					
1231120000	PROJECT SUPPORT & ADMINISTRATION	249	28SEP99	26SEP00					

CONSTRUCTION

PERFORMANCE MONITORING

PROJECT SUPPORT

EG&G ROCKY FLATS

ADS 1255 / DU 7 PRESENT LANDFILL

Activity Classification: SUPPORT

Plot Date: 2MAR94

Data Date: 25FEB94

Project Start: 10CT93

Project Finish: 16FEB01

Activity Bar/Early Dates

Critical Activity

Progress Bar

Milestone/Flag Activity

0007

EG&G ROCKY FLATS

ADS 1255 / DU 7 PRESENT LANDFILL

Sheet 4 of 4

Legend

Activity Bar/Early Dates

Critical Activity

Progress Bar

Milestone/Flag Activity

Legend

Activity Bar/Early Dates

Critical Activity

Progress Bar

Milestone/Flag Activity

Legend

Activity Bar/Early Dates

Critical Activity

Progress Bar

Milestone/Flag Activity

(c) Primavera Systems Inc

Legend

Activity Bar/Early Dates

Critical Activity

Progress Bar

Milestone/Flag Activity

Legend

Activity Bar/Early Dates

Critical Activity

Progress Bar

Milestone/Flag Activity
