



Rocky Mountain
Remediation Services, L.L.C.
... protecting the environment

RF/RMRS-99-437.UN

Closeout Radiological Survey Report

For Building 779, Administration Building

Rocky Mountain Remediation Services, L.L.C.

Millennium Services Inc.

Revision 0

October 1999



ADMIN RECCRD

REVIEWED FOR CLASSIFICATION UCN
By [Signature]
Date 10/13/99

B779-A-000148


1/129

**CLOSEOUT RADIOLOGICAL SURVEY REPORT
FOR BUILDING 779, Administration Building**


REVISION 0


OCTOBER, 99


This Closeout Radiological Survey Report was prepared by:



Michael Grube, Final Survey Radiological Engineer, B779 (GTS DURATEK) 10/12/99
Date


**This Closeout Radiological Survey Report has been reviewed and approved
by:**



Sarah Roberts, Radiological Engineer, B779 (ARCADIA) 10/13/99
Date

 FOR
Mark Brooks, Quality Assurance Manager (RMRS) 10/14/99
Date


Mark Hickman, Integration Manager, B779 (RMRS) 10/13/99
Date


Jeff Barroso, Radiological Safety Manager, B779 (RMRS) 10/13/99
Date


Terry Vaughn, Radiological Safety Director (RMRS) 10/14/99
Date


Thomas Dieter, Project Manager, B779 (RMRS) 10/13/99
Date


Brian Mathis, Manager D&D Projects (K-H) 10/14/99
Date

Table of Contents

List of Acronyms	2
Abstract	3
1.0 Introduction	3
1.1 Survey Unit Descriptions	4
1.2 Overview Maps	5
2.0 Scope of Work	7
2.1 Paint/Surface Media Samples	7
2.2 Removable Surface Contamination Survey	7
2.3 Total Surface Activity Survey	7
2.4 Scan Surveys	8
2.4.1 SCM/SIMS Scan Surveys	8
2.4.2 NE Electra Scan Surveys	9
3.0 DCGLs	10
4.0 Background	10
5.0 Quality Assurance/Quality Control	11
5.1 Paint/Surface Media Samples	11
5.2 Removable Surface Contamination Surveys	11
5.3 Total Surface Activity Surveys	11
5.4 Scan Surveys	11
5.4.1 SCM/SIMS Scan Surveys	11
5.4.2 NE Electra Scan Surveys	12
6.0 Investigation Methodology	12
7.0 Survey Results	13
7.1 Paint/Surface Media Samples	13
7.2 Removable Surface Contamination Surveys	14
7.3 Total Surface Activity Surveys	15
7.4 Scan Surveys	15
7.4.1 Survey Unit 77909 Scan and Investigation Data Summary	16
7.4.2 Survey Unit 77914 Scan and Investigation Data Summary	20
7.4.3 Survey Unit 77915 Scan and Investigation Data Summary	21
7.4.4 Survey Unit 77916 Scan and Investigation Data Summary	24
7.4.5 Survey Unit 77917 Scan and Investigation Data Summary	25
7.4.6 Survey Unit 77918 Scan and Investigation Data Summary	29
7.4.7 Survey Unit 77920 Scan and Investigation Data Summary	31
8.0 Conclusion	37

Attachments

Attachment A Survey Unit Overlay Maps	
Attachment B Survey Unit 77909 Data Summary	
Attachment C Survey Unit 77915 Data Summary	
Attachment D Survey Unit 77916 Data Summary	
Attachment E Survey Unit 77917 Data Summary	
Attachment F Survey Unit 77918 Data Summary	
Attachment G Survey Unit 77920 Data Summary	
Attachment H Survey Unit 77914 Data Summary	
Attachment I SCM/SIMS Quality Control Charts	
Attachment J Data Quality Assessment	
Attachment K Sample/Survey Measurement Location Maps	

Acronyms

cpm	Counts Per Minute
CRSP	Closeout Radiological Survey Plan
D&D	Decontamination and Decommissioning
DCGL _W	Derived Concentration Guideline Level – Wilcoxon Rank Sum test
DCGL _{EMC}	Derived Concentration Guideline Level – Elevated Measurement Comparison
DOE	U.S. Department of Energy
dpm	Disintegration Per Minute
DQA	Data Quality Assessment
DQO	Data Quality Objectives
FSS	Final Status Survey
FSSP	Final Status Survey Plan
FSSR	Final Status Survey Report
HSA	Historical Site Assessment
LBGR	Lower Bound of the Gray Region
MARSSIM	Multi-Agency Radiation Survey and Site Investigation Manual
MDA	Minimum Detectable Activity
MDC	Minimum Detectable Concentration
NIST	National Institute of Standards & Technology
NORM	Naturally Occurring Radioactive Material
PRE	Project Radiological Engineer
PSPC	Position Sensitive Proportional Counter
QA	Quality Assurance
QA/QC	Quality Assurance/Quality Control
QC	Quality Control
RCT	Radiological Control Technician
RE	Radiological Engineer
REFS	Radiological Engineering Field Services
RESS	Radiological Engineering Support Services
RFETS	Rocky Flats Environmental Technology Site
SCM/SIMS	Surface Contamination Monitor/Survey Information Management System
SRA	Shonka Research Associates
TSA (TSC)	Total Surface Activity (or Total Surface Contamination)
V&V	Verification and Validation

Abstract

Total and removable surface contamination surveys, paint/surface media samples (survey units 77909 and 77920 only), and scan surveys were performed in each Administration Building survey unit. The number/frequency of surveys/samples collected in each survey unit was based on the guidance provided in the Multi-Agency Radiation Survey and Site Investigation Manual (MARSSIM).

All survey/sample results presented in this report meet the DCGLs as defined by the Closeout Radiological Survey Plan for the 779 Cluster.

1.0 Introduction

Building 779 was originally constructed in 1965, with additions in 1968 and 1973. The mission of Building 779 was primarily as a nuclear weapons research and development center, and an analytical laboratory in support of Plutonium Operations. This report documents the final survey results of the Administration Building portion of 779 (including the Administration building exterior). The final surveys for other portions of Building 779 and the Building 779 cluster will be documented in separate stand-alone reports.

The Administration Building is a two-level structure that is connected to the east side of Building 779 and has approximate dimensions of 100 ft. long x 60 ft wide x 27 ft high. The exterior walls of the Administration Building are concrete block.

An addition to the existing containment structure was built on the roof of Building 779 to support the removal of contaminated ducting during D&D. The entire containment is outside the scope of final survey, and will be evaluated and released per a Property Release Evaluation (PRE) in accordance with 3-PRO-141-RSP-09.01, *Unrestricted Release of Property, Material, Equipment, and Waste*, prior to building demolition. The material will remain on the building during demolition, and will be segregated from building rubble after demolition.

Contamination originating from the duct pipe removed from the roof of 779 was identified on the roof surface outside of the containment on 9/8/99. Previously performed radiological operations surveys indicated that the contamination did not exist on the roof prior to this date. Several square meters of gravel from the ballast layer on the roof were removed. The tar beneath the gravel was surveyed to assure that all contamination was identified and removed. In addition, total surface contamination measurements were collected around the perimeter of the cleared area to assure that the contamination was appropriately bounded and removed. These surveys, though not included as part of the final survey data, are included in survey package 77909 for information purposes.

As a final verification, a statistically-based number of total and removable surface contamination measurements were collected on the affected areas of the roof (including survey units 77905 and 77909) to assure that contamination had not migrated to unidentified locations. This data is reported in sections 7.2 and 7.3.

The upper and lower levels of Administration Building were utilized as office space. The area was completely stripped of radiologically contaminated process piping prior to the performance of final surveys. "Clean" pipe and systems still remain, and will be released via PREs for the elevator (#990921-00779-002) and all conduit, electrical panels, fire protection pipe, etc. (#991007-00779-001). The elevator, piping and conduit will remain in the building during demolition, and will be segregated from building rubble after demolition.

Based on process history and characterization and in-process surveys, the areas were classified in accordance with MARSSIM and the Building 779 Cluster Closeout Radiological Survey Plan (CRSP) described in Section 1.1.

The Administration Building consisted of three survey areas that were further broken down into seven survey units. Three of the seven survey units were classified as Class 3. An explanation of the Class 1 and Class 2 survey units is provided below.

A spill occurred on the floor of room 208 (survey unit 77916) on 6/25/99. The total alpha contamination levels were as high as 2000 dpm/100 cm². Decontamination was successfully performed on all of the spots of contamination prior to final survey. However, due to the potential for contamination above the DCGL_w, the floor was classified as Class 1 (walls and ceiling were Class 3). No media samples were required from 77916 due to complete scabbling of the floor media.

The Administration Building exterior (survey unit 77909) is considered Class 2 due to the potential spread of contamination from outside areas (solar ponds, Building 776 fire). Rooms 115 and 115A had a history of fixed contamination that was potentially painted over. In addition, potentially contaminated zone one ventilation was located in the overhead (exhaust duct tower). However, it was not anticipated that residual contamination above the DCGL_w existed. Therefore the area was classified as Class 2.

The floors in both hallways were reclassified as Class 1 and re-designated as Survey Unit 77914. The reason for the reclassification was that contamination was detected in the hallway on the first floor in front of the elevator. Refer to Section 6.0 Investigation methodology for an additional discussion regarding this classification.

1.1 Survey Unit Descriptions

The Administration Building consists of all rooms on the first and second floor, the associated hallways and stairwells, the exhaust duct tower (to ground level), and the building exterior (north, south, and east wall and roof). A brief description and the classification of each of the seven Administration Building survey units are described below:

- 77909 – Administration Building Exterior (Class 2)
- 77915 – Second Floor Office Areas & Stairwell (201, 201A, 201B, 202, 202A, 203, 204, 204A, 204B, 205, 206, 207, 207A, 207B, 207C, 208 (walls and ceiling), 210, 210A, 211, 212, 212A, 213, 214) (Class 3)
- 77916 – Room 208 Floor (Class 1)
- 77917 – First Floor Office Areas and hallway (105, 106, 107, 108, 109, 110, 110A, 111, 113) (Class 3)
- 77918 – Rooms 100, 101, 101A, 104, 116, 116A, 116B, 117, (Class 3)
- 77920 – Rooms 114, 115, 115A, Exhaust Duct Tower (to ground level) (Class 2)
- 77914 – Administration Building Hallway Floor Surfaces (First and Second Floor) (Class 1)

1.2 Overview Maps

Figures 1.1 and 1.2 depict the location of the Administration Building in the 779 Cluster, and an interior view of the Administration Building, respectively.

Figure 1.1
Administration Building Exterior Overview Map

779 CLUSTER EXTERIOR SURVEY UNIT OVERVIEW



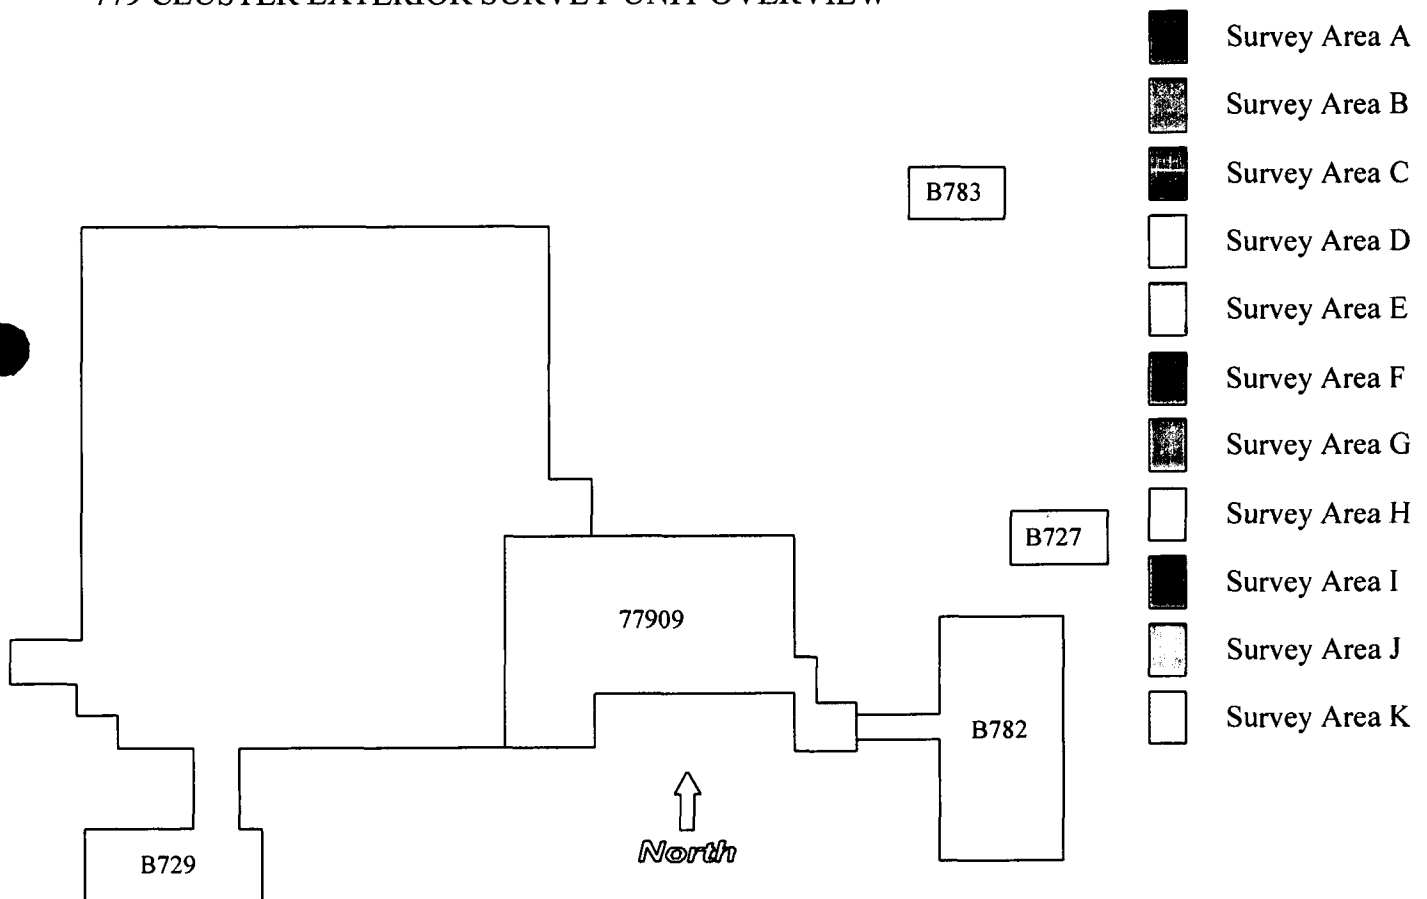


Figure 1.2 Administration Building Interior Overview Maps

779 FIRST FLOOR ADMIN INTERIOR SURVEY UNIT OVERVIEW

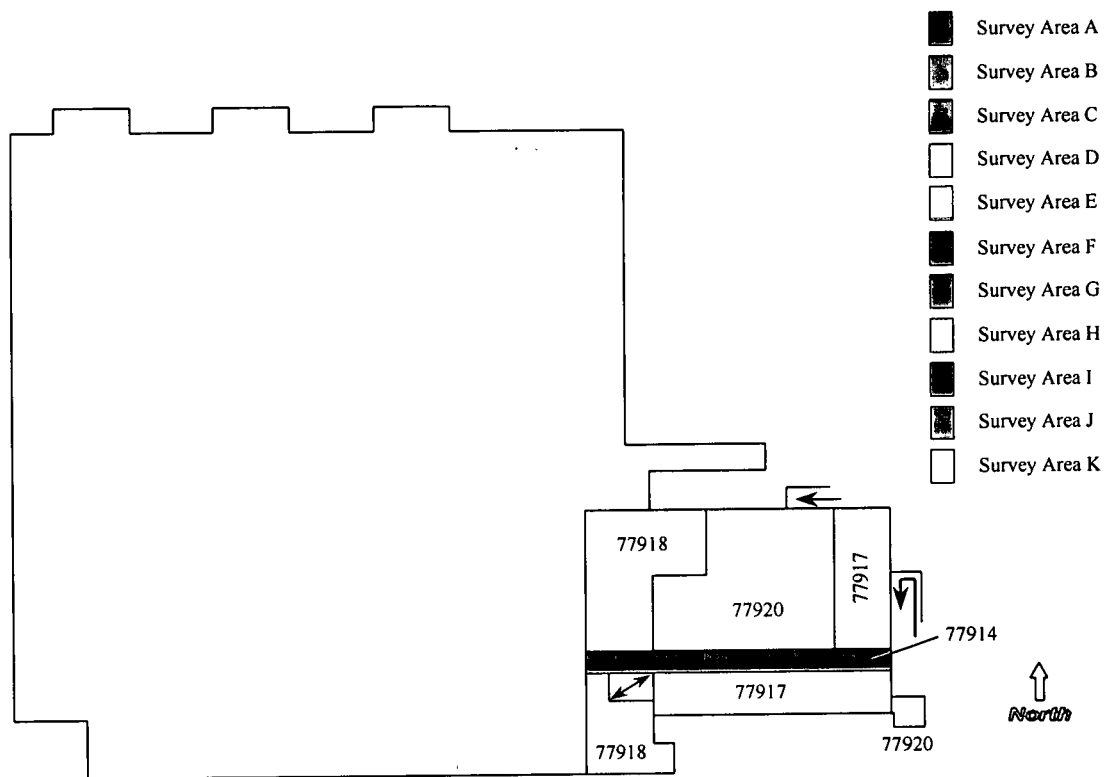

779 SECOND FLOOR ADMIN INTERIOR SURVEY UNIT OVERVIEW

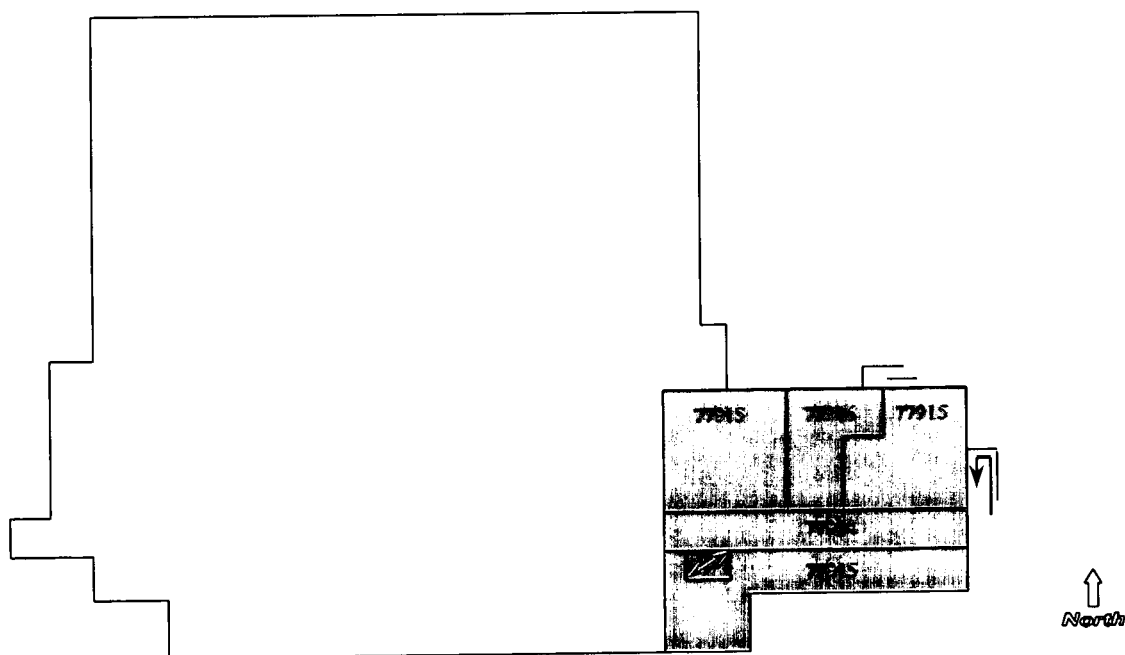

2.0 Scope of Work

2.1 Paint/Surface Media Samples

Paint/surface media samples were obtained in 77909 and 77920 (Class 2 survey units) to ensure average contamination did not exist below painted surfaces or other forms of surface media such as roofing material, floor adhesive, or within the paint or roofing/adhesive material itself. No samples were collected from 77914 or 77916 (Class 1) because the paint or surface media was removed prior to final survey. In addition, no media samples were collected from Class 3 areas (not required per the CRSP).

Due to the fact that there was no evidence (as discovered during the historical site assessment, characterization, and final status surveys) that contamination had migrated into cinder block, concrete, or any other base material and disappeared from the surface, total surface activity measurements and surface media sampling were utilized as the detection methods for any contamination that occurred on building surfaces. Therefore, no volumetric samples were collected.

The sample collection method for coated surfaces (paint or adhesive) involved the collection of cover material to a depth where the underlying base material was exposed.

The quantity of samples was determined based on MARSSIM statistical calculations to satisfy Impacted Class 2 survey requirements. The calculation methodology for the number of media samples is presented in the Closeout Radiological Survey Plan for the 779 Cluster (Section 5.2.6.2). Based on the calculations included in each survey package, 15 paint/surface media samples were required for each survey unit (refer to Building 779 project files).

Instrument calibration, maintenance, source check requirements, data reduction and MDC equations are controlled per applicable Kaiser Hill Analytical Services Division procedures.

2.2 Removable Surface Contamination Surveys

Removable surface contamination surveys were obtained in each survey unit to ensure that removable contamination did not exist above the Building 779 Cluster DCGL_{WS}. The quantity of removable contamination measurements was determined based on MARSSIM statistical calculations as presented in the Closeout Radiological Survey Plan for the 779 Cluster, RF/RMRS-97-123.UN (Section 5.2.6.2). Based on calculations included in each survey package, a minimum of 15 removable contamination measurements were required for each survey unit (refer to Building 779 project files).

Smears were counted on a SAC-4. Instrument calibration, maintenance, source check requirements, data reduction and MDC equations are provided in 3-PRO-112-RSP-02.01, Revision 1, "Radiological Instrumentation".

2.3 Total Surface Activity Surveys

Total surface activity surveys were obtained in each survey unit to ensure the average total activity levels did not exist above the Building 779 Cluster DCGL_{WS}. The number of total surface activity surveys was also determined based on MARSSIM statistical calculations as presented in the Closeout Radiological Survey Plan for the 779 Cluster (Section 5.2.6.2). Based on the calculations included in each survey package, 15 total surface activity measurements were required for each survey unit (refer to Building 779 project files).

The surveys were performed with an NE Electra with the 100 cm² DP6 detector. The survey count time was ninety seconds. Local area background determinations are discussed in Section 4.0. Instrument calibration, maintenance, source check requirements, as well as data reduction and MDC equations are provided in 3-PRO-112-RSP-02.01, Revision 1, "Radiological Instrumentation".

The Electra MDC is verified in a radiological engineering site operations technical basis document entitled "Methods to Demonstrate Compliance with Performance Requirements for Swipe Counting and Portable Contamination Survey Instrumentation used to Evaluate Property and Waste for Unrestricted Release", dated June 7, 1995.

2.4 Scan Surveys

Surface scans were conducted in each survey unit per two methods 1) with the position-sensitive SCM system and 2) with conventional hand-held NE Electra dual scintillation detectors. The two methods are described in the following sections.

2.4.1 SCM/SIMS Scan Surveys

The majority of the surface scans were conducted using the Surface Contamination Monitor/Survey Information Management System (SCM/SIMS) developed by Shonka Research Associates, Inc. (SRA). The SCM/SIMS system consists of a position sensitive proportional counter (PSPC) coupled to a computerized data acquisition system. The PSPC is a long detector that acts as an array of many small radiation detectors. This allows the instrument to measure more area per unit time than a smaller detector and still separate out localized areas of contamination. The PSPC is typically mounted to a motor driven cart. The drive motor provides speed control for the unit, and a precision wheel encoder, affixed to the cart, provides travel distance input to the computer. Counts are accumulated in each 5 cm channel every 5 cm travel by the system. The result is data retained in 5 cm x 5 cm (25 cm²) pixels, available for analysis and presentation via the SIMS software. Surveys were conducted at a speed of 0.4 to 0.8 inch/sec. A recount detector was employed for all surveys performed with the cart-mounted detectors. Recount detectors perform a second survey of the area surveyed by the primary detector. The main purpose of the recount detector is to reduce the number of false positive results due to the low DCGL_w for alpha emitting isotopes, the low and variable background, and the short count time. A few background counts occurring in a small area can result in an indication of elevated activity. The probability of background affecting both the primary and the recount detector is greatly reduced, thus reducing the need to perform verification surveys.

SCM/SIMS detector surface areas are 900 cm² and 1800 cm². Choice of detector was based on the floor space available and the interferences in the area. To complete surveys in areas that were not accessible with the standard cart mounted detectors, either corner detectors were employed or hand-held instruments were utilized (refer to section 2.4.2). The corner detector is a similar PSPC used in a static count mode with data binned in 5 cm increments. The corner detector accumulates data for eight seconds. The longer count time eliminated the need for recount. The output of the corner detector is integrated into the SIMS software.

Wall surveys were performed by mounting the detectors vertically to the side of the SCM cart. All other aspects of the survey were consistent with floor monitoring. The drive wheel maintained speed control, and position sensitivity was established through the wheel encoder. The height above grade was identified on the survey maps.

Surveys were conducted in accordance with equipment operation and calibration procedures developed by SRA and incorporated in the Millennium Services, Inc. Quality Assurance Plan. Detector efficiencies were determined with a NIST traceable Plutonium-238 source with an active area of approximately 50 cm² and an alpha energy of 5.5 MeV. The energy of the source is similar to the 5.1 MeV of Plutonium-239, the principle isotope of the primary suspected contaminant. Periodic quality control checks were performed for each detector in use, and used to establish the efficiency for the detectors based on data that spanned the use of that detector during the survey (Refer to Section 4.0). All quality control checks were performed under the same operating and environmental conditions as the surveys in accordance with applicable Radiological Safety Procedures.

The SCM/SIMS sensitivity for the surveys performed in the Administration Building is documented in the B779 project file. The Minimum Detectable Concentration for alpha surveys for 100 cm² areas is 128 dpm (refer to "Evaluation of Surface Contamination Monitor/Survey Information Management (SCM/SIMS) for the identification of contamination against the DCGL_{EMC} for the 779 Closure Project at the Rocky Flats Environmental Technology Site"). All RFETS-specified instrument performance requirements are satisfied with SCM/SIMS survey methodology based on data discussion provided in Appendix 5 of the CRSR for Building 729, RF/RMRS-99-358.UN.

2.4.2 NE Electra Scan Surveys

Areas that were not scanned with the SCM/SIMS were scanned with the hand-held NE Electra with 100 cm² DP6 probes, or NE Electra Plus with 600 cm² DP8 probes.

The scan rate for the DP6 was established as 1.5 inches per second in order to comply with the recommendations for probabilities of detection provided in ANSI N13.12, *Draft American National Standards: Control of Radioactive Surface Contamination on Materials, Equipment, and Facilities to be Released for Uncontrolled Use*. Scanned areas in excess of 225 dpm/100 cm² were flagged. If no flags were identified during the scan, the scan result was recorded as <225 dpm/100 cm² (refer to Tables 7.5 to 7.11).

Areas scanned with the DP8 detectors consisted of eight-second static counts. In the event that the eight-second count exceeded 225 dpm/100 cm², two additional measurements were performed at the same location. If one of the two additional measurements exceeded 225 dpm/100 cm², an investigation was performed.

Differentiation between SCM and handheld instrument surveys is captured within each individual survey package that is maintained in the project files.

3.0 DCGLs

The surface contamination criteria from DOE Order 5400.5 were used as the DCGLs for the final survey. The applicable transuranic DCGL_w for removable contamination, and total surface activity measured by direct surface emission are as follows:

Category	DCGL _w Removable Alpha (dpm/100 cm ²)	DCGL _w Total Alpha (dpm/100 cm ²)	DCGL _{EMC} Total Alpha (dpm/100 cm ²)
Transuranic	20	100	300
Uranium	N/A	5000	15,000

The applicable transuranic DCGL_w for paint/surface media samples is 100 dpm/100 cm².

4.0 Background

Final radiological surveys of the Administration Building were focussed on alpha emitting isotopes, principally Plutonium-239, and Plutonium-240. Natural activity present in construction materials was not expected to contribute a significant amount to the field measurements. Historical data from other RFETS building indicates that surface emission rates from concrete, typically the material containing the highest quantities of naturally-occurring alpha-emitting isotopes, would contribute negligible activity when compared to the DCGL_{EMC}. Therefore, no material background subtract was performed for alpha surface scan measurements, and results were compared directly to the applicable DCGL_{EMC} defined in Section 3.0.

For total surface activity data collected with the NE Electra, a ninety-second background measurement was collected at each total surface activity location. The average of these measurements was calculated, and the mean value subtracted from total surface activity measurements to obtain the net total surface activity results.

Paint/Surface media samples were analyzed by alpha spectroscopy methods. Individual isotopic data results are contained in Attachments B through G. Transuranic isotopes are not present in natural radioactivity; therefore no background concerns exist. Uranium isotopes, though present in nature, are not expected to exist in significant quantities in paint/surface media samples. As in surface activity measurements, total reported activity from paint/surface media sample analyses was evaluated against the applicable uranium or transuranic DCGL_w defined in Section 3.0.

Other than instrument background, which is quantified prior to analysis, background is not a factor during performance of removable contamination surveys. Reported values from the removable contamination surveys were evaluated against the applicable DCGL_w defined in Section 3.0.

5.0 Quality Assurance/Quality Control

Quality control for each type of instrument utilized in the Administration Building survey is discussed in the sections below. Additional quality control elements include the Software Quality Control Checklist Verification of Calculations sheets, which were generated for each survey unit (refer to Building 779 Project files) to verify the calculations contained in the spreadsheets; and a data quality assessment (DQA) document, which was generated to discuss the acceptance of data for final status survey (refer to Attachment J).

5.1 Paint/Surface Media Samples

Measures of laboratory precision and accuracy were assessed per applicable laboratory procedures. All QA data indicated that sample results were valid (refer to Attachment J, Data Quality Assessment).

5.2 Removable Surface Contamination Surveys

The instruments utilized for removable surface contamination analysis (Eberline SAC-4) were calibrated with NIST-traceable sources. A daily background and QC check was also performed. All background and QC checks were within required tolerances as delineated in the Building 779 CRSP RF/RMRS-97-123.UN (also refer to Attachment J, Data Quality Assessment).

5.3 Total Surface Activity Surveys

An additional 5% of total surface activity measurements were obtained for quality control purposes (refer to Attachments B through H). The results from these measurements were compared to the applicable $DCGL_W$ to ensure survey compliance (i.e., all QC measurements were less than $DCGL_W$). All QC measurements were less than $DCGL_W$ (refer to Attachment J, Data Quality Assessment).

5.4 Scan Surveys

5.4.1 SCM/SIMS Scan Surveys

Quality control surveys for SCM/SIMS scans were performed with a NIST traceable Plutonium-238 source with an activity of 194,400 dpm. The source, RFETS ID# RS3911, Manufacturer's ID ER716, is a 71 mm x 71 mm (approximately 50 cm²) plated source. The source manufacturer's certificate is in the 779 Closure Project file. Quality control surveys consisted of a minimum of three measurements of the source by the detector in the configuration used in the actual survey. SCM quality control surveys were performed with the source on the floor or wall and the detector assembly moving at the appropriate survey speed (i.e., 0.4 to 0.8 inches/sec). Corner detector quality control surveys consisted of measurements of the source placed on a surface and the data acquisition set for the survey time (i.e., 8 to 10 seconds).

A quality control survey was performed at the beginning and end of each detector use each day and periodically during the surveys. The response of the detector over the duration of its use became the basis for the detector's efficiency. Additionally, each survey was evaluated to ensure that it was bracketed by acceptable quality control surveys. At least two of the three measurements must fall within the specified tolerance (within 20% of the mean of all quality control surveys for each specific detector) in order for the data to be considered valid. The above criteria were satisfied. Therefore, the detector results were considered valid.

Source checks were conducted daily prior to start of survey, whenever the detector configuration was changed, and whenever any other electronic adjustments or maintenance was performed. The mean of the valid quality control surveys, determined from all acceptable results over the duration of the survey, was used to establish the efficiency for a specific detector. Attachment H includes the quality control charts for the SCM/SIMS detectors used during the survey.

5.4.2 NE Electra Scan Surveys

Performance checks were performed on the NE Electra prior to field use. The results were required to fall within the established range ($\pm 20\%$ in accordance with the applicable Radiological Safety Procedures) in order for the instrument and the associated data to be considered valid (refer to Attachment J, Data Quality Assessment).

6.0 Investigation Methodology

Follow up investigations were conducted for each scan result in excess of 75% of the DCGL_{EMC} (225 dpm/100cm²) by performing a survey of the flagged area with a hand held instrument, the NE Electra with a DP6 probe.

Investigation surveys utilizing the NE Electra were performed by first scanning the surrounding suspect area to determine if any elevated activity areas could be identified. Following the scan, a shielded local area background measurement (one minute count) and an unshielded direct measurement (one minute count) were obtained in the area of highest activity identified during the scan.

Remediation and a follow-up survey were performed at each confirmed location that produced an NE Electra result in excess of 225 dpm/100 cm² (as described in Tables 7.5 to 7.10).

Each investigation measurement was documented on an investigation form. In some cases, more than one investigation result was documented for a given grid. All scan investigation results are presented in Tables 7.5 to 7.10.

Investigations of each paint/media result in excess of 75% of the DCGL_w (100 dpm/100 cm²) were performed by evaluating other media sample results to assure that a pattern of contamination did not exist. If no pattern was identified, the data was deemed acceptable, due to the fact that the sample represented a small-area source term that would not result in a contamination level in excess of 100 dpm/100 cm² when averaged over the survey unit.

For the single case where the $DCGL_w$ was exceeded for a media sample result (77909), the media sample was bounded by eight additional samples within the affected m^2 to ensure the $DCGL_w$ for that m^2 was not exceeded. The average uranium and transuranic values for the eight additional media samples and the one original media sample is less than 75% of the applicable $DCGL_w$. In addition, the sign test was performed to assure that the mean concentration did not exceed the $DCGL_w$ over the survey unit. The sign test passed (i.e. the null hypothesis was rejected), thus the area was deemed acceptable (refer to Attachment B).

The initial survey of a small area of the Administration Building Hallway first floor (directly outside the entrance into the Radiological Boundary Area (RBA)), indicated the presence of total surface contamination in excess of 75% of the $DCGL_w$. The activity was attributed to the movement of radiological waste crates through the hallway (from the RBA), due to the fact that the remainder of the Administration Building hallway surveys (performed previously) did not indicate any contamination in excess of this action level.

In order to assure that contamination had not been tracked to other areas of the Administration Building hallway, an additional Class 1 survey unit (77914) was established. This survey unit consists of the floor surfaces of the first and second level hallways, which served as transport routes for radiological waste crates.

In addition, investigation surveys were performed in additional access/egress areas, and adjacent to all doorways in the Administration Building, to assure that the movement of personnel through these areas did not contribute to the spread of contamination.

The results for survey unit 77914 are presented in Section 7.0.

7.0 Survey Results

7.1 Paint/Surface Media Samples

Paint/surface media samples were obtained at each grid location where paint/surface media existed in accordance with approved instructions in each survey package, ensuring that the minimum required paint/surface media samples were obtained for survey units 77909 and 77920. Attachments B and G present results and a data summary of paint/surface media sample analyses for this survey unit. Alpha spectroscopy was performed to determine the activity of Uranium-233/234, Uranium-235, Uranium-238, Plutonium-239/240, and Americium-241. Values for each isotope(s) are reported separately. The data for the two survey units was below the applicable total uranium and total transuranic $DCGL_w$. The number of media samples obtained was verified to be adequate by re-calculating the required number of samples with the actual survey unit sample standard deviation (refer to the "Post Survey Paint/Media Sample Summary Statistics Calculation Verification Worksheet" in the Building 779 project files, for each applicable survey unit). Tables 7.1 and 7.2 summarize the results of the paint/surface media samples.

Table 7.1
Paint/Surface Media Summary Results for Transuranics

Survey Unit	Minimum (dpm/100 cm^2)	Maximum (dpm/100 cm^2)	Mean (dpm/100 cm^2)	Std. Dev. (dpm/100 cm^2)	$DCGL_w$
77909	5.5	85.4*	22.3	28.6	100
77920	0.0	5.7	2.1	1.7	

* An investigation was performed for each paint/media result in excess of 75% of the $DCGL_w$ (100 dpm/100 cm^2) by evaluating other media sample results to assure that a pattern of contamination did not exist. If no pattern was identified, the data was deemed acceptable.

Table 7.2
Paint/Surface Media Summary Results for Uranium

Survey Unit	Minimum (dpm/100 cm ²)	Maximum (dpm/100 cm ²)	Mean (dpm/100 cm ²)	Std. Dev. (dpm/100 cm ²)	DCGL _w
77909	4.5	88.3	42.9	27.3	5000
77920	21.3	169.0	68.8	40.0	

Detailed sampling instructions and paint/surface media sample results are on file in the Building 779 project files.

7.2 Removable Surface Contamination Surveys

Removable contamination measurements were obtained at each accessible grid location in accordance with approved instructions in each survey package. The minimum required removable contamination measurements were obtained for each survey unit. Removable contamination results for each survey unit are presented in Attachments B through H (except for roof investigation data). Surveys were performed at each location from which paint/surface media samples were obtained, ensuring that the minimum required number of smears was collected for each survey unit. For those points, measurements were obtained prior to and after the media sample. For those areas from which no paint/media sample was obtained, a single removable contamination measurement was obtained. The results of all smears show that the removable contamination levels met the DCGL_w described in Section 3.0. The number of removable activity measurements obtained was verified to be adequate by re-calculating the required number of measurements with the actual survey unit measurement standard (refer to the "Post Survey Removable Contamination Summary Statistics Calculation Verification Worksheet" in the Building 779 project files, for each survey unit). Table 7.3 summarizes the results of removable surface contamination surveys.

Table 7.3
Removable Surface Contamination Summary Results

Survey Unit	Minimum (dpm/100 cm ²)	Maximum (dpm/100 cm ²)	Mean (dpm/100 cm ²)	Std. Dev. (dpm/100 cm ²)	DCGL _w
77909	-2	10	2	3	20
Roof Investigation	-0.6	4.2	0.3	1.3	
77915	-0.6	2.4	0.7	1.0	
77916	-0.6	3.9	0.6	1.5	
77917	-0.3	2.7	0.9	1.1	
77918	-0.9	3.6	0.5	1.5	
77920	-0.6	3.9	1.3	1.3	
77914	-0.6	4.5	0.2	1.0	

Detailed survey instructions and removable surface contamination results are on file in the Building 779 project files.

7.3 Total Surface Activity Surveys

Total surface activity measurements were obtained in accordance with approved instructions in each survey package, at each accessible grid location, ensuring that the minimum required total surface activity measurements were obtained for each survey unit. Total surface activity survey results for each survey unit are presented in Attachments B through H (except for roof investigation data). Total surface activity surveys were performed at each location where paint/surface media samples were obtained. For those areas where no media sample was obtained, a single total surface activity measurement was obtained. The results of all surveys showed that all total surface activity levels were less than the DCGL_w described in Section 3.0. The number of total surface activity measurements obtained was verified to be adequate by recalculating the required number of measurements with the actual survey unit standard deviation (refer to the "Post Survey Total Surface Activity Summary Statistics Calculation Verification Worksheet" in the Building 779 project files, for each survey unit). Table 7.4 summarizes the total surface contamination survey results.

Table 7.4
Total Surface Contamination Summary Results

Survey Unit	Minimum (dpm/100 cm ²)	Maximum (dpm/100 cm ²)	Mean (dpm/100 cm ²)	Std. Dev. (dpm/100 cm ²)	DCGL _w
77909	-0.9	56.6	22.5	15.5	100
Roof Investigation	-5.5	57.4	19.6	16.3	
77915	-6.3	60.2	19.0	17.6	
77916	0.0	45.6	15.2	11.3	
77917	-7.7	43.7	9.8	13.6	
77918	-4.5	29.1	8.5	8.8	
77920	-6.2	30.5	10.1	9.8	
77914	-14.4	35.3	9.4	10.9	

Detailed survey instructions and total surface contamination results are on file in the Building 779 project files.

7.4 Scan Surveys

Scan surveys were performed at the required density in accordance with approved instructions in each survey package. The scan results are presented in Tables 7.5 through 7.11. Survey results are grouped by survey unit. Each survey unit is divided into a number of subunits, which is typically represented by a single surface (e.g. floor, wall < 2 meters, wall > 2 meters, ceiling, etc.). Within each subunit, survey(s) are performed. For SCM scan surveys, a report is automatically generated. For the NE Electra scan surveys, the results are reported as < 225 dpm/100 cm² (given that no areas are flagged for investigation). For both scan methods, survey information is documented on survey forms and maps. A consistent numbering system (per the survey unit numbers outlined in the Final Survey Breakdown Structure, Rev 2) is used to identify the survey unit, subunit, survey number, and type of detector used.

The scan survey overlay maps (refer to Attachment A) delineate the subunit locations so that all surveys can be traced to the location surveyed. The yellow-shaded areas represent areas requiring 100% scan. The green-shaded areas represent requiring 50% scans. The blue-shaded areas represent areas requiring 10% scan. The required scan frequency for each survey unit, per the Closeout Radiological Survey Plan for the 779 Cluster was verified.

Due to the low expected count rate and the random nature of radioactivity, a low occurrence of individual 100 cm² area false positive results are expected. This phenomenon is amplified when using the SCM/SIMS system due to the large amounts of data generated (i.e. a result is recorded for each 25 cm² area scanned). The utilization of a recount detector allows for a rapid evaluation of an area that indicates a higher than normal value. If one detector indicates a slightly elevated reading but the event is not confirmed by the second detector, the measurement is likely a false positive. Readings that approach an investigation level with either detector are averaged with the results from the other detector. An average value in excess of 225 dpm/100 cm² requires an investigation.

Surveys taken with the SCM operating in the timer mode are presented as a single survey. Survey time for those detectors have been increased to minimize the probability of false positives. Timer mode surveys are performed when the cart mounted, motor driven SCM can not physically access an area due to area size, interference, or accessibility. The timer mode setting was 10 seconds, providing the same surface area measurement as the time measured by both the primary and recount operating at 1cm/sec.

7.4.1 Survey Unit 77909 Scan and Investigation Data Summary

Table 7.5 summarizes the SCM/SIMS and NE Electra scans and follow-up investigations conducted in survey unit 77909:

Table 7.5
Survey Unit 77909 Scan Data Summary

Final Scan Survey Number ⁽¹⁾	Scan Survey Date	Max. Result (dpm/100cm ²) ⁽²⁾	Investigation Survey Number	SCM value >75% of EMC (dpm/100cm ²)	Electra Investigation Result (dpm/100cm ²)	Decon required (y/n)	Final Investigation Value (dpm/100cm ²)
00920100	7/21/99	193	n/a	n/a	n/a	No	n/a
00920200	7/21/99	232	00920290	232	48	No	n/a
00920300	7/21/99	270	00920390	229	52	No	n/a
				270	52	No	n/a
00920400	7/21/99	387	00920490	232	60	No	n/a
				256	80	No	n/a
				270	40	No	n/a
				387	52	No	n/a
				271	56	No	n/a
				232	48	No	n/a
				232	56	No	n/a
				232	60	No	n/a
				270	40	No	n/a
				232	52	No	n/a

CLOSEOUT RADIOLOGICAL SURVEY REPORT
FOR BUILDING 779, ADMINISTRATION BUILDING

RF/RMRS-99-437.UN
Rev. 0 Page 17 of 37

Final Scan Survey Number ⁽¹⁾	Scan Survey Date	Max. Result (dpm/100cm ²) ⁽²⁾	Investigation Survey Number	SCM value >75% of EMC (dpm/100cm ²)	Electra Investigation Result (dpm/100cm ²)	Decon required (y/n)	Final Investigation Value (dpm/100cm ²)
00920500	7/21/99	270	00920590	232	16	No	n/a
				258	40	No	n/a
				270	80	No	n/a
00920600	7/21/99	270	00920690	232	32	No	n/a
				232	36	No	n/a
				270	8	No	n/a
				259	24	No	n/a
00920700	7/21/99	194	n/a	n/a	n/a	No	n/a
00920800	7/21/99	309	00920890	309	48	No	n/a
				232	4	No	n/a
				291	16	No	n/a
00920900	7/21/99	309	00920990	232	22	No	n/a
				270	46	No	n/a
				226	38	No	n/a
				295	34	No	n/a
				232	18	No	n/a
				253	54	No	n/a
				309	58	No	n/a
00921000	7/21/99	309	00921090	271	24	No	n/a
				308	32	No	n/a
				309	52	No	n/a
				270	48	No	n/a
				270	32	No	n/a
00921100	7/21/99	270	00921190	270	44	No	n/a
				232	36	No	n/a
00921200	7/21/99	271	00921290	232	60	No	n/a
				232	36	No	n/a
00921200	7/21/99	271	00921290	231	80	No	n/a
				232	64	No	n/a
				271	36	No	n/a
00921300	7/21/99	252	00921390	252	24	No	n/a
00921400	7/21/99	309	00921490	232	36	No	n/a
				309	32	No	n/a
				232	28	No	n/a
				268	40	No	n/a
				238	88	No	n/a
				270	36	No	n/a
				231	12	No	n/a
00921500	7/21/99	298	00921590	232	32	No	n/a
				232	68	No	n/a
				270	20	No	n/a
				232	4	No	n/a
				232	24	No	n/a
				232	24	No	n/a
				232	12	No	n/a
				298	56	No	n/a

CLOSEOUT RADIOLOGICAL SURVEY REPORT
FOR BUILDING 779, ADMINISTRATION BUILDING

RF/RMRS-99-437.UN
Rev. 0 Page 18 of 37

Final Scan Survey Number ⁽¹⁾	Scan Survey Date	Max. Result (dpm/100cm ²) ⁽²⁾	Investigation Survey Number	SCM value >75% of EMC (dpm/100cm ²)	Electra Investigation Result (dpm/100cm ²)	Decon required (y/n)	Final Investigation Value (dpm/100cm ²)
00921600	7/22/99	309	00921690	257	20	No	n/a
				271	40	No	n/a
				232	28	No	n/a
				309	60	No	n/a
				270	28	No	n/a
				309	40	No	n/a
00921601	8/24/99	203	n/a	n/a	n/a	No	n/a
00921700	7/22/99	348	00921790	232	68	No	n/a
				232	32	No	n/a
				309	28	No	n/a
				271	36	No	n/a
				232	40	No	n/a
				232	32	No	n/a
				232	60	No	n/a
				348	4	No	n/a
				309	40	No	n/a
				232	8	No	n/a
				232	40	No	n/a
				243	40	No	n/a
				309	16	No	n/a
				232	72	No	n/a
00921800	7/22/99	318	00921890	309	80	No	n/a
				271	68	No	n/a
				232	76	No	n/a
				232	100	No	n/a
				318	68	No	n/a
00921800	7/22/99	318	00921890	271	56	No	n/a
				292	52	No	n/a
				231	36	No	n/a
				227	64	No	n/a
				309	48	No	n/a
				309	52	No	n/a
				270	20	No	n/a
00921900	7/22/99	270	00921990	270	20	No	n/a
00922000	7/22/99	309	00922090	309	68	No	n/a
				232	64	No	n/a
				232	60	No	n/a
				232	12	No	n/a
				232	28	No	n/a
				245	48	No	n/a
00922100	7/20/99	232	00922190	232	32	No	n/a
				232	4	No	n/a
				232	32	No	n/a
				232	44	No	n/a
00922200	7/20/99	243	00922290	243	32	No	n/a
00922300	7/20/99	232	00922390	232	8	No	n/a
00965300	8/24/99	135	n/a	n/a	n/a	No	n/a

CLOSEOUT RADIOLOGICAL SURVEY REPORT
FOR BUILDING 779, ADMINISTRATION BUILDING

RF/RMRS-99-437.UN
Rev. 0 Page 19 of 37

Final Scan Survey Number ⁽¹⁾	Scan Survey Date	Max. Result (dpm/100cm ²) ⁽²⁾	Investigation Survey Number	SCM value >75% of EMC (dpm/100cm ²)	Electra Investigation Result (dpm/100cm ²)	Decon required (y/n)	Final Investigation Value (dpm/100cm ²)
00965400	8/24/99	203	n/a	n/a	n/a	No	n/a
00965501	8/24/99	270	00965590	270	40	No	n/a
00965503	9/30/99	154	n/a	n/a	n/a	No	n/a
00965600	7/27/99	194	n/a	n/a	n/a	No	n/a
00965601	8/24/99	102	n/a	n/a	n/a	No	n/a
00965700	7/27/99	270	00965790	270	24	No	n/a
00965701	8/24/99	135	n/a	n/a	n/a	No	n/a
00965800	7/27/99	194	n/a	n/a	n/a	No	n/a
00965801	8/24/99	101	n/a	n/a	n/a	No	n/a
00965900	8/24/99	169	n/a	n/a	n/a	No	n/a
00966000	7/23/99	461	00966090	270	12	No	n/a
				461	36	No	n/a
00966001	8/24/99	203	n/a	n/a	n/a	No	n/a
00966100	7/23/99	257	00966190	242	20	No	n/a
				232	24	No	n/a
				257	24	No	n/a
00966101	8/24/99	237	00966191	237	36	No	n/a
00966200	7/23/99	232	00966290	229	28	No	n/a
				232	24	No	n/a
00966201	8/24/99	169	n/a	n/a	n/a	No	n/a
00966300	7/23/99	232	00966390	232	28	No	n/a
00966400	7/23/99	503	00966490	503	40	No	n/a
				309	36	No	n/a
00966400	7/23/99	503	00966490	309	40	No	n/a
00966500	8/24/99	372	00966590	372	20	No	n/a
00966600	8/24/99	135	n/a	n/a	n/a	No	n/a
00966800	8/24/99	270	00966890	270	60	No	n/a
				270	84	No	n/a
00967000	7/22/99	194	n/a	n/a	n/a	No	n/a
00967001	8/24/99	169	n/a	n/a	n/a	No	n/a
00967100	7/23/99	309	00967190	309	76	No	n/a
00967201	7/23/99	380	00967290	380	44	No	n/a
				232	52	No	n/a

- (1) The first six characters represent the survey subunit number. The last two numbers represent the detector type.
- (2) NE Electra scan results are reported as < 225 dpm/100 cm² when no areas are flagged.
- (3) One-square meter averages are verified as less than 75 dpm/100 cm² when individual measurements in excess of 100 dpm/100 cm² are present.

Detailed scan survey instructions and results are on file in the Building 779 project file.

7.4.2 Survey Unit 77914 Scan and Investigation Data Summary

Table 7.6 summarizes the SCM/SIMS and NE Electra scans and follow-up investigations conducted in survey unit 77914:

Table 7.6
Survey Unit 77914 Scan Data Summary

Final Scan Survey Number ⁽¹⁾	Scan Survey Date	Max. Result (dpm/100cm ²) ⁽²⁾	Investigation Survey Number	SCM value >75% of EMC (dpm/100cm ²)	Electra Investigation Result (dpm/100cm ²)	Decon required (y/n)	Final Investigation Value (dpm/100cm ²)
01400100	9/30/99	2477	01400190	2477	2400	Yes	28
				619	712	Yes	24
01400200	9/30/99	2884	01400291	232	36	No	n/a
				232	-8	No	n/a
				2884	232	Yes	12
				232	40	No	n/a
01400290	10/4/99	<225	n/a	n/a	n/a	No	n/a
01400300	9/30/99	1019	01400391	232	16	No	n/a
				232	40	No	n/a
				1019	56	No	n/a
				232	28	No	n/a
01400390	10/4/99	<225	n/a	n/a	n/a	No	n/a
01400400	9/30/99	1200	01400491	1200	0	No	n/a
				252	244	Yes	20
				271	28	No	n/a
01400490	10/4/99	<225	n/a	n/a	n/a	No	n/a
01400500	9/30/99	232	01400591	232	8	No	n/a
01400590	10/6/99	<225	n/a	n/a	n/a	No	n/a
01400600	9/30/99	194	n/a	n/a	n/a	No	n/a
01400690	10/6/99	<225	n/a	n/a	n/a	No	n/a
01400701	10/2/99	557	01400790	557	412	Yes	12
01400791	10/6/99	<225	n/a	n/a	n/a	No	n/a
01400801	10/2/99	213	n/a	n/a	n/a	No	n/a
01400890	10/6/99	<225	n/a	n/a	n/a	No	n/a
01400900	9/30/99	1316	01400991	1316	28	No	n/a
				309	-4	No	n/a
01400990	10/6/99	<225	n/a	n/a	n/a	No	n/a
01401000	9/30/99	541	01401090	541	524	Yes	16
				270	28	No	n/a
01401100	9/30/99	193	n/a	n/a	n/a	No	n/a
01401190	10/6/99	<225	n/a	n/a	n/a	No	n/a
01401290	10/9/99	<225	n/a	n/a	n/a	No	n/a
01401200	10/8/99	193	n/a	n/a	n/a	No	n/a

- (1) The first six characters represent the survey subunit number. The last two numbers represent the detector type.
 (2) NE Electra scan results are reported as < 225 dpm/100 cm² when no areas are flagged.
 (3) One-square meter averages are verified as less than 75 dpm/100 cm² when individual measurements in excess of 100 dpm/100 cm² are present.

Detailed scan survey instructions and results are on file in the Building 779 project file.

7.4.3 Survey Unit 77915 Scan and Investigation Data Summary

Table 7.7 summarizes the SCM/SIMS and NE Electra scans and follow-up investigations conducted in survey unit 77915:

Table 7.7
Survey Unit 77915 Scan Data Summary

Final Scan Survey Number ⁽¹⁾	Scan Survey Date	Max. Result (dpm/100cm ²) ⁽²⁾	Investigation Survey Number	SCM value >75% of EMC (dpm/100cm ²)	Electra Investigation Result (dpm/100cm ²)	Decon required (y/n)	Final Investigation Value (dpm/100cm ²)
01500100	8/16/99	251	01500191	251	0	No	n/a
01500300	8/17/99	251	01500391	251	32	No	n/a
01500430	7/14/99	349	01500490	238	60	No	n/a
				227	40	No	n/a
				237	8	No	n/a
				349	16	No	n/a
01500430	7/14/99	349	01500490	225	4	No	n/a
				226	24	No	n/a
				232	16	No	n/a
01500530	7/13/99	254	01500590	254	36	No	n/a
01500600	7/17/99	208	n/a	n/a	n/a	No	n/a
01500700	8/17/99	349	01500791	349	8	No	n/a
				301	4	No	n/a
				251	40	No	n/a
				251	16	No	n/a
01500900	7/17/99	348	01500990	270	16	No	n/a
				232	0	No	n/a
				232	12	No	n/a
				348	20	No	n/a
				310	8	No	n/a
01501000	7/17/99	271	01501090	271	32	No	n/a
				256	28	No	n/a
01501190	8/9/99	254	n/a	254	n/a	Yes	36
01501400	8/17/99	301	01501491	251	12	No	n/a
				240	28	No	n/a
				251	8	No	n/a
				251	40	No	n/a
				298	24	No	n/a
				301	24	No	n/a
				226	40	No	n/a
				251	8	No	n/a
01501500	8/16/99	301	01501591	301	28	No	n/a
				301	12	No	n/a
				251	8	No	n/a
				251	12	No	n/a
				251	24	No	n/a

CLOSEOUT RADIOLOGICAL SURVEY REPORT
FOR BUILDING 779, ADMINISTRATION BUILDING

RF/RMRS-99-437.UN
Rev. 0 Page 22 of 37

Final Scan Survey Number ⁽¹⁾	Scan Survey Date	Max. Result (dpm/100cm ²) ⁽²⁾	Investigation Survey Number	SCM value >75% of EMC (dpm/100cm ²)	Electra Investigation Result (dpm/100cm ²)	Decon required (y/n)	Final Investigation Value (dpm/100cm ²)
01501630	7/15/99	231	01501690	231	20	No	n/a
01501730	8/12/99	241	01501790	241	-4	No	n/a
				241	20	No	n/a
01501832	8/12/99	229	01501890	229	16	No	n/a
01501931	8/12/99	211	n/a	n/a	n/a	No	n/a
01502031	8/12/99	519	01502090	519	0	No	n/a
01502600	8/16/99	276	01502690	276	2	No	n/a
				243	4	No	n/a
01520100	8/17/99	270	01520190	270	-8	No	n/a
01520200	8/17/99	169	n/a	n/a	n/a	No	n/a
01520300	8/17/99	203	n/a	n/a	n/a	No	n/a
01520400	8/17/99	203	n/a	n/a	n/a	No	n/a
01520500	8/17/99	101	n/a	n/a	n/a	No	n/a
01520630	7/12/99	114	n/a	n/a	n/a	No	n/a
01520700	8/17/99	135	n/a	n/a	n/a	No	n/a
01520830	7/12/99	163	n/a	n/a	n/a	No	n/a
01520900	8/17/99	201	n/a	n/a	n/a	No	n/a
01521090	7/15/99	<225	n/a	n/a	n/a	No	n/a
01521100	8/17/99	150	n/a	n/a	n/a	No	n/a
01521190	7/15/99	<225	n/a	n/a	n/a	No	n/a
01521200	8/17/99	251	01521290	251	24	No	n/a
01521300	8/17/99	169	n/a	n/a	n/a	No	n/a
01521400	8/17/99	135	n/a	n/a	n/a	No	n/a
01521500	8/17/99	169	n/a	n/a	n/a	No	n/a
01521600	8/17/99	169	n/a	n/a	n/a	No	n/a
01521700	8/17/99	135	n/a	n/a	n/a	No	n/a
01521800	8/17/99	135	n/a	n/a	n/a	No	n/a
01521900	8/17/99	169	n/a	n/a	n/a	No	n/a
01522000	8/17/99	169	n/a	n/a	n/a	No	n/a
01522591	8/20/99	<225	n/a	n/a	n/a	No	n/a
01522690	8/20/99	<225	n/a	n/a	n/a	No	n/a
01522891	8/20/99	<225	n/a	n/a	n/a	No	n/a
01523000	7/14/99	154	n/a	n/a	n/a	No	n/a
01523200	7/14/99	154	n/a	n/a	n/a	No	n/a
01523491	8/20/99	<225	n/a	n/a	n/a	No	n/a
01523591	8/18/99	<225	n/a	n/a	n/a	No	n/a
01523691	8/20/99	<225	n/a	n/a	n/a	No	n/a
01523901	10/2/99	135	n/a	n/a	n/a	No	n/a
01524001	10/2/99	116	n/a	n/a	n/a	No	n/a
01524200	7/15/99	270	01524290	270	4	No	n/a
				240	8	No	n/a
01524400	7/15/99	193	n/a	n/a	n/a	No	n/a
01524501	8/17/99	203	n/a	n/a	n/a	No	n/a
01524630	7/23/99	536	01524690	308	12	No	n/a
				233	12	No	n/a
				536	12	No	n/a

CLOSEOUT RADIOLOGICAL SURVEY REPORT
FOR BUILDING 779, ADMINISTRATION BUILDING

RF/RMRS-99-437.UN
Rev. 0 Page 23 of 37

Final Scan Survey Number ⁽¹⁾	Scan Survey Date	Max. Result (dpm/100cm ²) ⁽²⁾	Investigation Survey Number	SCM value >75% of EMC (dpm/100cm ²)	Electra Investigation Result (dpm/100cm ²)	Decon required (y/n)	Final Investigation Value (dpm/100cm ²)
01524800	7/27/99	193	n/a	n/a	n/a	No	n/a
01524830	7/23/99	372	01524890	372	-4	No	n/a
01524901	8/25/99	169	n/a	n/a	n/a	No	n/a
01524930	7/23/99	211	n/a	n/a	n/a	No	n/a
01525030	7/23/99	284	01525090	284	0	No	n/a
				243	-8	No	n/a
01525130	7/23/99	245	01525190	245	8	No	n/a
01525230	7/23/99	276	01525290	230	12	No	n/a
				276	20	No	n/a
				271	0	No	n/a
				227	4	No	n/a
				228	4	No	n/a
01525230	7/23/99	276	01525290	255	15	No	n/a
01525300	8/17/99	201	n/a	n/a	n/a	No	n/a
01525400	8/17/99	176	n/a	n/a	n/a	No	n/a
01525500	8/17/99	176	n/a	n/a	n/a	No	n/a
01525600	8/17/99	201	n/a	n/a	n/a	No	n/a
01525701	10/2/99	194	n/a	n/a	n/a	No	n/a
01525730	7/16/99	104	n/a	n/a	n/a	No	n/a
01525800	8/17/99	201	n/a	n/a	n/a	No	n/a
01525900	8/17/99	201	n/a	n/a	n/a	No	n/a
01526000	8/17/99	151	n/a	n/a	n/a	No	n/a
01526100	7/17/99	116	n/a	n/a	n/a	No	n/a
01526200	7/17/99	116	n/a	n/a	n/a	No	n/a
01526300	7/17/99	154	n/a	n/a	n/a	No	n/a
01526400	7/17/99	154	n/a	n/a	n/a	No	n/a
01526501	8/16/99	304	01526591	304	8	No	n/a
01526601	8/16/99	135	n/a	n/a	n/a	No	n/a
01526701	8/16/99	203	n/a	n/a	n/a	No	n/a
01526801	8/16/99	135	n/a	n/a	n/a	No	n/a
01526901	8/16/99	135	n/a	n/a	n/a	No	n/a
01527001	8/16/99	135	n/a	n/a	n/a	No	n/a
01527101	8/16/99	135	n/a	n/a	n/a	No	n/a
01527201	8/16/99	135	n/a	n/a	n/a	No	n/a
01527301	8/17/99	135	n/a	n/a	n/a	No	n/a
01527401	8/17/99	135	n/a	n/a	n/a	No	n/a
01527501	8/17/99	135	n/a	n/a	n/a	No	n/a
01527601	8/17/99	135	n/a	n/a	n/a	No	n/a
01527700	8/17/99	201	n/a	n/a	n/a	No	n/a
01527800	8/17/99	150	n/a	n/a	n/a	No	n/a
01528100	8/17/99	201	n/a	n/a	n/a	No	n/a
01528190	7/14/99	<225	n/a	n/a	n/a	No	n/a
01528290	7/14/99	<225	n/a	n/a	n/a	No	n/a
01528300	8/17/99	150	n/a	n/a	n/a	No	n/a
01528390	7/14/99	<225	n/a	n/a	n/a	No	n/a
01528490	7/14/99	<225	n/a	n/a	n/a	No	n/a

CLOSEOUT RADIOLOGICAL SURVEY REPORT
FOR BUILDING 779, ADMINISTRATION BUILDING

RF/RMRS-99-437.UN
Rev. 0 Page 24 of 37

Final Scan Survey Number ⁽¹⁾	Scan Survey Date	Max. Result (dpm/100cm ²) ⁽²⁾	Investigation Survey Number	SCM value >75% of EMC (dpm/100cm ²)	Electra Investigation Result (dpm/100cm ²)	Decon required (y/n)	Final Investigation Value (dpm/100cm ²)
01565400	7/13/99	232	01565490	232	20	No	n/a
01565700	7/13/99	77	n/a	n/a	n/a	No	n/a
01565900	7/12/99	227	01565990	227	40	No	n/a
01566300	7/13/99	193	n/a	n/a	n/a	No	n/a
01566900	7/13/99	193	n/a	n/a	n/a	No	n/a
01567300	7/14/99	193	n/a	n/a	n/a	No	n/a
01567500	7/17/99	889	01567590	889	16	No	n/a
01568000	7/14/99	116	n/a	n/a	n/a	No	n/a
01570300	7/17/99	116	n/a	n/a	n/a	No	n/a
01570700	7/18/99	154	n/a	n/a	n/a	No	n/a
01585100	7/27/99	193	n/a	n/a	n/a	No	n/a

- (1) The first six characters represent the survey subunit number. The last two numbers represent the detector type.
(2) NE Electra scan results are reported as < 225 dpm/100 cm² when no areas are flagged.
(3) One-square meter averages are verified as less than 75 dpm/100 cm² when individual measurements in excess of 100 dpm/100 cm² are present.

Detailed scan survey instructions and results are on file in the Building 779 project file.

7.4.4 Survey Unit 77916 Scan and Investigation Data Summary

Table 7.8 summarizes the SCM/SIMS and NE Electra scans and follow-up investigations conducted in survey unit 77916:

Table 7.8
Survey Unit 77916 Scan Data Summary

Final Scan Survey Number ⁽¹⁾	Scan Survey Date	Max. Result (dpm/100cm ²) ⁽²⁾	Investigation Survey Number	SCM value >75% of EMC (dpm/100cm ²)	Electra Investigation Result (dpm/100cm ²)	Decon required (y/n)	Final Investigation Value (dpm/100cm ²)
01602600	7/27/99	193	n/a	n/a	n/a	No	n/a
01602601	8/27/99	348	01602691	348	48	No	n/a
01602690	8/24/99	<225	n/a	n/a	n/a	No	n/a
01602700	7/27/99	193	n/a	n/a	n/a	No	n/a
01602701	8/27/99	193	n/a	n/a	n/a	No	n/a
01602790	8/24/99	<225	n/a	n/a	n/a	No	n/a

- (1) The first six characters represent the survey subunit number. The last two numbers represent the detector type.
(2) NE Electra scan results are reported as < 225 dpm/100 cm² when no areas are flagged.
(3) One-square meter averages are verified as less than 75 dpm/100 cm² when individual measurements in excess of 100 dpm/100 cm² are present.

Detailed scan survey instructions and results are on file in the Building 779 project file.

7.4.5 Survey Unit 77917 Scan and Investigation Data Summary

Table 7.9 summarizes the SCM/SIMS and NE Electra scans and follow-up investigations conducted in survey unit 77917:

Table 7.9
Survey Unit 77917 Scan Data Summary

Final Scan Survey Number ⁽¹⁾	Scan Survey Date	Max. Result (dpm/100cm ²) ⁽²⁾	Investigation Survey Number	SCM value >75% of EMC (dpm/100cm ²)	Electra Investigation Result (dpm/100cm ²)	Decon required (y/n)	Final Investigation Value (dpm/100cm ²)
01700134	8/11/99	291	01700193	244	16	No	n/a
				264	36	No	n/a
				226	20	No	n/a
				240	52	No	n/a
				239	28	No	n/a
01700134	8/11/99	291	01700193	226	0	No	n/a
				291	18	No	n/a
				226	16	No	n/a
				225	24	No	n/a
01700232	8/11/99	341	01700291	249	-4	No	n/a
				236	0	No	n/a
				235	-4	No	n/a
				264	0	No	n/a
				230	6	No	n/a
				304	-10	No	n/a
				258	-12	No	n/a
				229	4	No	n/a
				252	4	No	n/a
				247	-4	No	n/a
				225	-4	No	n/a
				341	-4	No	n/a
				269	16	No	n/a
				259	12	No	n/a
01700300	8/23/99	503	01700392	503	24	No	n/a
				251	12	No	n/a
				251	0	No	n/a
				251	36	No	n/a
				251	16	No	n/a
				251	16	No	n/a
				226	-4	No	n/a
				251	12	No	n/a
				251	64	No	n/a
				245	16	No	n/a
				226	20	No	n/a
				301	32	No	n/a
				226	80	No	n/a
				251	0	No	n/a
01700400	8/2/99	309	01700490	276	16	No	n/a
				228	28	No	n/a
				270	28	No	n/a
				309	24	No	n/a

CLOSEOUT RADIOLOGICAL SURVEY REPORT
FOR BUILDING 779, ADMINISTRATION BUILDING

RF/RMRS-99-437.UN
Rev. 0 Page 26 of 37

Final Scan Survey Number ⁽¹⁾	Scan Survey Date	Max. Result (dpm/100cm ²) ⁽²⁾	Investigation Survey Number	SCM value >75% of EMC (dpm/100cm ²)	Electra Investigation Result (dpm/100cm ²)	Decon required (y/n)	Final Investigation Value (dpm/100cm ²)
01700400	8/2/99	309	01700490	270	52	No	n/a
				227	20	No	n/a
01700830	8/11/99	289	01700890	227	-6	No	n/a
				290	30	No	n/a
				229	18	No	n/a
				231	12	No	n/a
				247	6	No	n/a
				284	14	No	n/a
01700830	8/11/99	289	01700890	234	-6	No	n/a
				251	30	No	n/a
				227	6	No	n/a
				254	24	No	n/a
				282	36	No	n/a
				271	12	No	n/a
				257	20	No	n/a
				244	12	No	n/a
01700930	8/11/99	267	01700990	237	8	No	n/a
				267	36	No	n/a
				230	24	No	n/a
				225	40	No	n/a
				231	20	No	n/a
01701030	8/11/99	444	01701090	444	32	No	n/a
				236	56	No	n/a
				247	32	No	n/a
				335	24	No	n/a
				288	12	No	n/a
				243	40	No	n/a
				265	28	No	n/a
				230	52	No	n/a
01701130	8/11/99	314	01701190	314	-8	No	n/a
				228	12	No	n/a
				239	-4	No	n/a
				238	-24	No	n/a
				228	4	No	n/a
				237	12	No	n/a
01720230	7/26/99	157	n/a	n/a	n/a	No	n/a
01720430	7/26/99	270	01720490	270	28	No	n/a
				245	20	No	n/a
				243	100	No	n/a
				242	28	No	n/a
				249	8	No	n/a
01720530	7/26/99	337	01720590	337	16	No	n/a
				292	32	No	n/a
				279	16	No	n/a
01720530	7/26/99	337	01720590	285	8	No	n/a

CLOSEOUT RADIOLOGICAL SURVEY REPORT
FOR BUILDING 779, ADMINISTRATION BUILDING

RF/RMRS-99-437.UN
Rev. 0 Page 27 of 37

Final Scan Survey Number ⁽¹⁾	Scan Survey Date	Max. Result (dpm/100cm ²) ⁽²⁾	Investigation Survey Number	SCM value >75% of EMC (dpm/100cm ²)	Electra Investigation Result (dpm/100cm ²)	Decon required (y/n)	Final Investigation Value (dpm/100cm ²)
01720630	7/26/99	408	01720690	288	-8	No	n/a
				280	4	No	n/a
				260	0	No	n/a
				256	-8	No	n/a
				236	0	No	n/a
				263	4	No	n/a
				242	0	No	n/a
				334	24	No	n/a
				251	4	No	n/a
				236	12	No	n/a
				408	4	No	n/a
				241	-4	No	n/a
				259	16	No	n/a
				264	-4	No	n/a
				258	-8	No	n/a
01720730	7/26/99	284	01720791	225	0	No	n/a
				230	12	No	n/a
				226	-4	No	n/a
				284	4	No	n/a
01720830	7/26/99	322	01720890	266	20	No	n/a
				322	28	No	n/a
				317	16	No	n/a
				254	16	No	n/a
				273	-8	No	n/a
				241	32	No	n/a
				322	24	No	n/a
				306	24	No	n/a
				273	28	No	n/a
				315	4	No	n/a
				254	4	No	n/a
				310	16	No	n/a
01720902	8/12/99	169	n/a	249	4	No	n/a
				n/a	n/a	No	n/a
01721001	8/12/99	304	01721090	304	-4	No	n/a
01721101	8/12/99	304	01721191	304	12	No	n/a
01721201	8/12/99	169	n/a	n/a	n/a	No	n/a
01721400	8/2/99	309	01721490	290	4	No	n/a
				232	-16	No	n/a
				230	4	No	n/a
				309	8	No	n/a
				232	16	No	n/a
				232	0	No	n/a
01721600	8/2/99	270	01721690	270	12	No	n/a
01721600	8/2/99	270	01721690	232	8	No	n/a
				232	0	No	n/a
				232	8	No	n/a
				253	4	No	n/a
				270	0	No	n/a

CLOSEOUT RADIOLOGICAL SURVEY REPORT
FOR BUILDING 779, ADMINISTRATION BUILDING

RF/RMRS-99-437.UN
Rev. 0 Page 28 of 37

Final Scan Survey Number ⁽¹⁾	Scan Survey Date	Max. Result (dpm/100cm ²) ⁽²⁾	Investigation Survey Number	SCM value >75% of EMC (dpm/100cm ²)	Electra Investigation Result (dpm/100cm ²)	Decon required (y/n)	Final Investigation Value (dpm/100cm ²)
01721700	8/16/99	169	n/a	n/a	n/a	No	n/a
01721800	8/16/99	169	n/a	n/a	n/a	No	n/a
01721900	8/16/99	169	n/a	n/a	n/a	No	n/a
01722000	8/16/99	135	n/a	n/a	n/a	No	n/a
01722101	8/16/99	135	n/a	n/a	n/a	No	n/a
01722201	8/16/99	169	n/a	n/a	n/a	No	n/a
01722301	8/16/99	135	n/a	n/a	n/a	No	n/a
01722401	8/16/99	169	n/a	n/a	n/a	No	n/a
01722530	8/10/99	191	n/a	n/a	n/a	No	n/a
01722630	8/10/99	361	01722690	361	12	No	n/a
				267	-4	No	n/a
01722730	8/10/99	205	n/a	n/a	n/a	No	n/a
01722830	8/10/99	260	01722890	229	28	No	n/a
				260	4	No	n/a
				246	0	No	n/a
01722930	8/10/99	244	01722990	244	18	No	n/a
01723030	8/10/99	361	01723090	361	16	No	n/a
				231	16	No	n/a
				273	24	No	n/a
01723130	8/10/99	445	01723190	258	20	No	n/a
				270	28	No	n/a
				232	40	No	n/a
				282	68	No	n/a
				445	28	No	n/a
01723230	8/10/99	376	01723290	376	40	No	n/a
				295	0	No	n/a
				258	36	No	n/a
				245	4	No	n/a
				273	12	No	n/a
				238	8	No	n/a
				249	28	No	n/a
01723330	8/10/99	282	01723390	263	12	No	n/a
				282	0	No	n/a
				225	4	No	n/a
01723430	8/10/99	231	01723490	231	12	No	n/a
01765900	8/2/99	387	01765990	387	36	No	n/a
				267	24	No	n/a
				227	32	No	n/a
				260	48	No	n/a
01765900	8/2/99	387	01765990	271	28	No	n/a
01766100	8/2/99	271	01766190	232	48	No	n/a
				232	16	No	n/a
				232	12	No	n/a
				271	36	No	n/a
				232	28	No	n/a
				271	24	No	n/a

CLOSEOUT RADIOLOGICAL SURVEY REPORT
FOR BUILDING 779, ADMINISTRATION BUILDING

RF/RMRS-99-437.UN
Rev. 0 Page 29 of 37

Final Scan Survey Number ⁽¹⁾	Scan Survey Date	Max. Result (dpm/100cm ²) ⁽²⁾	Investigation Survey Number	SCM value >75% of EMC (dpm/100cm ²)	Electra Investigation Result (dpm/100cm ²)	Decon required (y/n)	Final Investigation Value (dpm/100cm ²)
01766500	8/2/99	232	01766590	232	-12	No	n/a
01766500	8/2/99	232	01766590	232	24	No	n/a
				232	32	No	n/a

- (1) The first six characters represent the survey subunit number. The last two numbers represent the detector type.
 (2) NE Electra scan results are reported as < 225 dpm/100 cm² when no areas are flagged.
 (3) One-square meter averages are verified as less than 75 dpm/100 cm² when individual measurements in excess of 100 dpm/100 cm² are present.

Detailed scan survey instructions and results are on file in the Building 779 project file.

7.4.6 Survey Unit 77918 Scan and Investigation Data Summary

Table 7.10 summarizes the SCM/SIMS and NE Electra scans and follow-up investigations conducted in survey unit 77918:

Table 7.10
Survey Unit 77918 Scan Data Summary

Final Scan	Scan	Max. Result	Investigation	SCM value	Electra	Decon	Final
01800100	8/4/99	309	01800190	264	16	No	n/a
				271	28	No	n/a
				309	12	No	n/a
				232	8	No	n/a
01800200	8/4/99	348	01800290	348	20	No	n/a
01800790	9/11/99	<225	n/a	n/a	n/a	No	n/a
01800791	10/4/99	<225	n/a	n/a	n/a	No	n/a
01800890	9/13/99	<225	n/a	n/a	n/a	No	n/a
01800891	10/7/99	<225	n/a	n/a	n/a	No	n/a
01800990	9/11/99	<225	n/a	n/a	n/a	No	n/a
01800991	10/4/99	<225	n/a	n/a	n/a	No	n/a
01801090	9/11/99	<225	n/a	n/a	n/a	No	n/a
01801091	10/4/99	<225	n/a	n/a	n/a	No	n/a
01801190	10/7/99	<225	n/a	n/a	n/a	No	n/a
01801191	10/7/99	<225	n/a	n/a	n/a	No	n/a
01801200	9/10/99	301	01801290	251	0	No	n/a
				301	4	No	n/a
				251	36	No	n/a
01801300	9/10/99	302	01801390	252	8	No	n/a
				302	-12	No	n/a
				226	8	No	n/a
				250	12	No	n/a
				302	16	No	n/a
				226	-12	No	n/a
				252	16	No	n/a
				277	24	No	n/a
				226	-15	No	n/a
				252	-4	No	n/a

CLOSEOUT RADIOLOGICAL SURVEY REPORT
FOR BUILDING 779, ADMINISTRATION BUILDING

RF/RMRS-99-437.UN
Rev. 0 Page 30 of 37

Final Scan	Scan	Max. Result	Investigation	SCM value	Electra	Decon	Final
01801400	9/10/99	335	01801490	251	0	No	n/a
				252	-20	No	n/a
				252	4	No	n/a
				277	0	No	n/a
				302	0	No	n/a
				252	16	No	n/a
				302	8	No	n/a
				352	8	No	n/a
				302	20	No	n/a
				335	4	No	n/a
				252	4	No	n/a
				252	-8	No	n/a
				277	20	No	n/a
				252	44	No	n/a
				252	4	No	n/a
				302	20	No	n/a
				226	12	No	n/a
				277	0	No	n/a
				252	0	No	n/a
				247	0	No	n/a
				226	4	No	n/a
				252	-8	No	n/a
				252	-4	No	n/a
01801590	10/9/99	<225	n/a	n/a	n/a	No	n/a
01820100	8/4/99	194	n/a	n/a	n/a	No	n/a
01820200	8/4/99	194	n/a	n/a	n/a	No	n/a
01820300	8/4/99	232	01820390	232	-12	No	n/a
01820400	8/4/99	270	01820490	270	4	No	n/a
01820500	10/8/99	150	n/a	n/a	n/a	No	n/a
01820590	10/4/99	<225	n/a	n/a	n/a	No	n/a
01820600	10/4/99	116	n/a	n/a	n/a	No	n/a
01820700	9/7/99	154	n/a	n/a	n/a	No	n/a
01820701	9/10/99	201	n/a	n/a	n/a	No	n/a
01820800	9/7/99	153	n/a	n/a	n/a	No	n/a
01820801	9/9/99	213	n/a	n/a	n/a	No	n/a
01820802	9/10/99	201	n/a	n/a	n/a	No	n/a
01820901	9/9/99	116	n/a	n/a	n/a	No	n/a
01820902	9/10/99	251	01820990	251	28	No	n/a
01821000	10/8/99	232	01821091	232	20	No	n/a
01821090	10/4/99	<225	n/a	n/a	n/a	No	n/a
01821100	9/8/99	152	n/a	n/a	n/a	No	n/a
01821200	9/8/99	155	n/a	n/a	n/a	No	n/a
01821300	9/8/99	188	n/a	n/a	n/a	No	n/a
01821400	9/8/99	116	n/a	n/a	n/a	No	n/a
01821500	9/8/99	116	n/a	n/a	n/a	No	n/a
01821600	9/8/99	116	n/a	n/a	n/a	No	n/a
01821700	9/8/99	174	n/a	n/a	n/a	No	n/a
01821800	9/8/99	116	n/a	n/a	n/a	No	n/a
01821900	9/8/99	116	n/a	n/a	n/a	No	n/a
01822000	9/8/99	116	n/a	n/a	n/a	No	n/a
01822100	9/8/99	97	n/a	n/a	n/a	No	n/a
01822300	9/10/99	251	01822390	251	12	No	n/a
01822400	9/10/99	201	n/a	n/a	n/a	No	n/a

CLOSEOUT RADIOLOGICAL SURVEY REPORT
FOR BUILDING 779, ADMINISTRATION BUILDING

RF/RMRS-99-437.UN
Rev. 0 Page 31 of 37

Final Scan	Scan	Max. Result	Investigation	SCM value	Electra	Decon	Final
01822500	9/10/99	150	n/a	n/a	n/a	No	n/a
01822700	9/10/99	251	01822790	251	16	No	n/a
01823500	9/30/99	193	n/a	n/a	n/a	No	n/a
01823590	10/4/99	<225	n/a	n/a	n/a	No	n/a
01823600	9/30/99	174	n/a	n/a	n/a	No	n/a
01823690	10/4/99	<225	n/a	n/a	n/a	No	n/a
01823700	10/2/99	116	n/a	n/a	n/a	No	n/a
01823790	10/4/99	<225	n/a	n/a	n/a	No	n/a
01823800	9/30/99	483	01823891	483	220	No	n/a
01823890	10/4/99	<225	n/a	n/a	n/a	No	n/a
01823900	10/8/99	96	n/a	n/a	n/a	No	n/a
01823990	10/9/99	<225	n/a	n/a	n/a	No	n/a
01865100	8/4/99	194	n/a	n/a	n/a	No	n/a
01865200	1/8/99	96	n/a	n/a	n/a	No	n/a
01865290	10/4/99	<225	n/a	n/a	n/a	No	n/a
01865400	9/8/99	77	n/a	n/a	n/a	No	n/a
01865500	9/8/99	116	n/a	n/a	n/a	No	n/a
01865600	9/8/99	116	n/a	n/a	n/a	No	n/a
01865800	9/8/99	116	n/a	n/a	n/a	No	n/a
01865900	9/8/99	112	n/a	n/a	n/a	No	n/a
01866000	9/8/99	77	n/a	n/a	n/a	No	n/a
01866100	9/9/99	154	n/a	n/a	n/a	No	n/a
01866400	9/9/99	154	n/a	n/a	n/a	No	n/a
01867000	9/30/99	116	n/a	n/a	n/a	No	n/a
01867090	10/4/99	<225	n/a	n/a	n/a	No	n/a
01867100	10/8/99	150	n/a	n/a	n/a	No	n/a
01867190	10/9/99	<225	n/a	n/a	n/a	No	n/a
01885100	8/4/99	232	01885190	232	56	No	n/a
01885500	9/9/99	193	n/a	n/a	n/a	No	n/a

- (1) The first six characters represent the survey subunit number. The last two numbers represent the detector type.
- (2) NE Electra scan results are reported as < 225 dpm/100 cm² when no areas are flagged.
- (3) One-square meter averages are verified as less than 75 dpm/100 cm² when individual measurements in excess of 100 dpm/100 cm² are present.

Detailed scan survey instructions and results are on file in the Building 779 project file.

7.4.7 Survey Unit 77920 Scan and Investigation Data Summary

Table 7.11 summarizes the SCM/SIMS and NE Electra scans and follow-up investigations conducted in survey unit 77920:

Table 7.11
Survey Unit 77920 Scan Data Summary

Final Scan Survey Number ⁽¹⁾	Scan Survey Date	Max. Result (dpm/100cm ²) ⁽²⁾	Investigation Survey Number	SCM value >75% of EMC (dpm/100cm ²)	Electra Investigation Result (dpm/100cm ²)	Decon required (y/n)	Final Investigation Value (dpm/100cm ²)
02000101	7/27/99	301	02000190	251	20	No	n/a
				301	4	No	n/a
02000103	8/16/99	264	02000192	264	40	No	n/a
				264	12	No	n/a
02000202	8/16/99	264	02000292	264	48	No	n/a
				264	24	No	n/a
02000293	8/26/99	<225	n/a	n/a	n/a	No	n/a
02000302	8/16/99	257	02000391	251	40	No	n/a
				248	48	No	n/a
				257	20	No	n/a
02000401	8/16/99	201	n/a	n/a	n/a	No	n/a
02000500	7/27/99	301	02000591	301	16	No	n/a
02000532	8/12/99	539	02000590	539	24	No	n/a
				260	24	No	n/a
				294	28	No	n/a
02000600	7/27/99	201	n/a	n/a	n/a	No	n/a
02000632	8/12/99	301	02000690	301	20	No	n/a
				242	24	No	n/a
02000700	7/27/99	234	02000790	234	20	No	n/a
02000702	8/24/99	402	02000791	226	44	No	n/a
				402	72	No	n/a
				301	8	No	n/a
				251	20	No	n/a
				301	28	No	n/a
				226	12	No	n/a
				251	28	No	n/a
				246	52	No	n/a
				226	12	No	n/a
				226	32	No	n/a
				251	28	No	n/a
				299	28	No	n/a
				251	40	No	n/a
				251	44	No	n/a
				251	48	No	n/a
				247	28	No	n/a
				251	24	No	n/a
				251	16	No	n/a
				251	48	No	n/a
				251	32	No	n/a
				251	16	No	n/a
				251	4	No	n/a
				251	16	No	n/a
				247	40	No	n/a

CLOSEOUT RADIOLOGICAL SURVEY REPORT
FOR BUILDING 779, ADMINISTRATION BUILDING

RF/RMRS-99-437.UN
Rev. 0 Page 33 of 37

Final Scan Survey Number ⁽¹⁾	Scan Survey Date	Max. Result (dpm/100cm ²) ⁽²⁾	Investigation Survey Number	SCM value >75% of EMC (dpm/100cm ²)	Electra Investigation Result (dpm/100cm ²)	Decon required (y/n)	Final Investigation Value (dpm/100cm ²)
02000890	10/3/99	<225	n/a	n/a	n/a	No	n/a
02000990	10/3/99	<225	n/a	n/a	n/a	No	n/a
02020100	7/26/99	553	02020190	268	96	No	n/a
				251	180	No	n/a
				553	170	No	n/a
				251	52	No	n/a
02020130	7/26/99	278	02020191	278	12	No	n/a
				225	0	No	n/a
				225	20	No	n/a
				278	4	No	n/a
02020192	8/25/99	<225	n/a	n/a	n/a	No	n/a
02020200	7/26/99	452	02020290	452	336	Yes	40
				301	24	No	n/a
				251	12	No	n/a
02020230	7/26/99	652	02020292	302	n/a	Yes	wall removed
				364	n/a	Yes	wall removed
				257	20	No	n/a
02020230	7/26/99	652	02020292	252	-4	No	n/a
				243	16	No	n/a
				273	0	No	n/a
				250	16	No	n/a
				244	20	No	n/a
				244	12	No	n/a
				259	12	No	n/a
				652	n/a	Yes	wall removed
02020300	7/26/99	301	02020390	301	28	No	n/a
				301	8	No	n/a
				231	16	No	n/a
				251	16	No	n/a
02020330	7/26/99	253	02020391	253	12	No	n/a
				230	12	No	n/a
				247	12	No	n/a
				245	4	No	n/a
				248	0	No	n/a
02020392	8/26/99	<225	n/a	n/a	n/a	No	n/a
02020400	7/26/99	402	02020490	402	92	No	n/a
				281	16	No	n/a
				251	4	No	n/a
02020430	7/26/99	280	02020491	280	0	No	n/a
				238	8	No	n/a
				237	20	No	n/a
				280	0	No	n/a
				238	24	No	n/a
				237	0	No	n/a
				260	0	No	n/a
				249	20	No	n/a

CLOSEOUT RADIOLOGICAL SURVEY REPORT
FOR BUILDING 779, ADMINISTRATION BUILDING

RF/RMRS-99-437.UN
Rev. 0 Page 34 of 37

Final Scan Survey Number ⁽¹⁾	Scan Survey Date	Max. Result (dpm/100cm ²) ⁽²⁾	Investigation Survey Number	SCM value >75% of EMC (dpm/100cm ²)	Electra Investigation Result (dpm/100cm ²)	Decon required (y/n)	Final Investigation Value (dpm/100cm ²)
02020493	8/25/99	<225	n/a	n/a	n/a	No	n/a
02020500	7/26/99	347	02020590	347	24	No	n/a
				301	44	No	n/a
				239	-4	No	n/a
02020530	7/26/99	350	02020591	284	8	No	n/a
				242	20	No	n/a
				298	36	No	n/a
				294	20	No	n/a
				345	32	No	n/a
				288	12	No	n/a
				269	20	No	n/a
				260	12	No	n/a
				315	20	No	n/a
				350	32	No	n/a
				293	8	No	n/a
				245	12	No	n/a
02020530	7/26/99	350	02020591	260	32	No	n/a
02020600	7/26/99	352	02020690	251	36	No	n/a
				275	36	No	n/a
				352	276	Yes	176
				301	0	No	n/a
				251	20	No	n/a
02020630	7/26/99	244	02020691	227	8	No	n/a
				244	8	No	n/a
				236	24	No	n/a
				234	28	No	n/a
				231	8	No	n/a
02020692	8/23/99	<225	n/a	n/a	n/a	No	n/a
02020700	7/26/99	201	n/a	n/a	n/a	No	n/a
02020730	7/26/99	294	02020791	261	8	No	n/a
				226	12	No	n/a
				227	8	No	n/a
				233	12	No	n/a
				243	20	No	n/a
				294	32	No	n/a
				242	20	No	n/a
				239	20	No	n/a
				270	20	No	n/a
				234	12	No	n/a
				268	16	No	n/a
02020800	7/26/99	236	02020890	236	16	No	n/a

CLOSEOUT RADIOLOGICAL SURVEY REPORT
FOR BUILDING 779, ADMINISTRATION BUILDING

RF/RMRS-99-437.UN
Rev. 0 Page 35 of 37

Final Scan Survey Number ⁽¹⁾	Scan Survey Date	Max. Result (dpm/100cm ²) ⁽²⁾	Investigation Survey Number	SCM value >75% of EMC (dpm/100cm ²)	Electra Investigation Result (dpm/100cm ²)	Decon required (y/n)	Final Investigation Value (dpm/100cm ²)
02020830	7/26/99	363	02020891	279	0	No	n/a
				290	12	No	n/a
				237	12	No	n/a
				263	12	No	n/a
				363	4	No	n/a
				352	20	No	n/a
				263	16	No	n/a
				266	8	No	n/a
				288	12	No	n/a
				244	4	No	n/a
				244	4	No	n/a
02020892	8/26/99	<225	n/a	n/a	n/a	No	n/a
02020900	7/26/99	594	02020991	325	16	No	n/a
				594	60	No	n/a
				251	76	No	n/a
				238	24	No	n/a
				427	32	No	n/a
02020930	7/26/99	377	02020990	257	20	No	n/a
02020930	7/26/99	377	02020990	242	16	No	n/a
				267	8	No	n/a
				255	20	No	n/a
				255	24	No	n/a
				241	24	No	n/a
				229	20	No	n/a
				317	10	No	n/a
				233	0	No	n/a
				232	36	No	n/a
				240	12	No	n/a
				228	0	No	n/a
				377	16	No	n/a
				272	8	No	n/a
				264	20	No	n/a
				272	12	No	n/a
				248	24	No	n/a
02021000	7/26/99	339	02021090	247	20	No	n/a
				301	12	No	n/a
				232	20	No	n/a
				251	20	No	n/a
				339	12	No	n/a
				251	4	No	n/a
02021030	7/26/99	288	02021091	230	4	No	n/a
				288	20	No	n/a
				275	12	No	n/a
				237	4	No	n/a
				247	8	No	n/a

CLOSEOUT RADIOLOGICAL SURVEY REPORT
FOR BUILDING 779, ADMINISTRATION BUILDING

RF/RMRS-99-437.UN
Rev. 0 Page 36 of 37

Final Scan Survey Number ⁽¹⁾	Scan Survey Date	Max. Result (dpm/100cm ²) ⁽²⁾	Investigation Survey Number	SCM value >75% of EMC (dpm/100cm ²)	Electra Investigation Result (dpm/100cm ²)	Decon required (y/n)	Final Investigation Value (dpm/100cm ²)
02021100	7/26/99	352	02021190	251	12	No	n/a
				352	4	No	n/a
				301	20	No	n/a
02021130	7/26/99	424	02021191	236	24	No	n/a
				230	12	No	n/a
				424	12	No	n/a
				231	20	No	n/a
				274	40	No	n/a
				286	32	No	n/a
				274	156	No	n/a
				235	28	No	n/a
				255	8	No	n/a
02021192	8/25/99	<225	n/a	n/a	n/a	No	n/a
02021200	7/26/99	402	02021290	402	332	Yes	68
				251	6	No	n/a
				251	24	No	n/a
				251	22	No	n/a
02021230	7/26/99	385	02021391	346	44	No	n/a
				234	4	No	n/a
				385	28	No	n/a
				235	28	No	n/a
				272	8	No	n/a
				267	16	No	n/a
02021390	10/3/99	<225	n/a	n/a	n/a	No	n/a
02021490	10/3/99	<225	n/a	n/a	n/a	No	n/a
02021590	10/3/99	<225	n/a	n/a	n/a	No	n/a
02021690	10/3/99	<225	n/a	n/a	n/a	No	n/a
02021790	10/3/99	<225	n/a	n/a	n/a	No	n/a
02021890	10/3/99	<225	n/a	n/a	n/a	No	n/a
02021990	10/3/99	<225	n/a	n/a	n/a	No	n/a
02022090	10/3/99	<225	n/a	n/a	n/a	No	n/a
02065100	7/26/99	151	n/a	n/a	n/a	No	n/a
02065101	8/24/99	101	n/a	n/a	n/a	No	n/a
02065200	7/26/99	704	02065290	704	n/a	Yes	wall removed
02065201	8/24/99	338	02065291	338	0	No	n/a
02065300	7/26/99	251	02065390	251	-4	No	n/a
				251	8	No	n/a
02065301	8/24/99	135	n/a	n/a	n/a	No	n/a
02065400	7/26/99	201	n/a	n/a	n/a	No	n/a
02065401	8/24/99	101	n/a	n/a	n/a	No	n/a
02065500	7/26/99	287	02065590	251	0	No	n/a
				287	4	No	n/a
02065600	7/26/99	251	02065690	251	16	No	n/a
02065800	7/26/99	201	n/a	n/a	n/a	No	n/a
02065900	7/26/99	201	n/a	n/a	n/a	No	n/a

CLOSEOUT RADIOLOGICAL SURVEY REPORT
FOR BUILDING 779, ADMINISTRATION BUILDING

RF/RMRS-99-437.UN
Rev. 0 Page 37 of 37

Final Scan Survey Number ⁽¹⁾	Scan Survey Date	Max. Result (dpm/100cm ²) ⁽²⁾	Investigation Survey Number	SCM value >75% of EMC (dpm/100cm ²)	Electra Investigation Result (dpm/100cm ²)	Decon required (y/n)	Final Investigation Value (dpm/100cm ²)
02066200	7/26/99	251	02066290	251	40	No	n/a
				251	28	No	n/a
02066390	10/3/99	<225	n/a	n/a	n/a	No	n/a
02066490	10/3/99	<225	n/a	n/a	n/a	No	n/a
02066590	10/3/99	<225	n/a	n/a	n/a	No	n/a
02066690	10/3/99	<225	n/a	n/a	n/a	No	n/a
02085200	8/23/99	169	n/a	n/a	n/a	No	n/a
02085490	10/4/99	<225	n/a	n/a	n/a	No	n/a

(1) The first six characters represent the survey subunit number. The last two numbers represent the detector type.

(2) NE Electra scan results are reported as < 225 dpm/100 cm² when no areas are flagged.

(3) One-square meter averages are verified as less than 75 dpm/100 cm² when individual measurements in excess of 100 dpm/100 cm² are present.

Detailed scan survey instructions and results are on file in the Building 779 project file.


8.0 Conclusion

All survey/sample data collected from the B779 Administration Building interior and exterior surfaces were collected in accordance with the Closeout Radiological Survey Plan for the 779 Cluster and approved survey instructions. All data was verified and validated as described in Attachment I) and therefore is considered acceptable to demonstrate compliance with release criteria.


All survey/sample results presented in this report meet the DCGLs as defined by the Closeout Radiological Survey Plan for the 779 Cluster.

ATTACHMENT A
Survey Unit Overlay Maps

Survey Unit: 77909
B779 Exterior Walls & Exhaust Duct Tower (Exterior)
Map 1 of 2

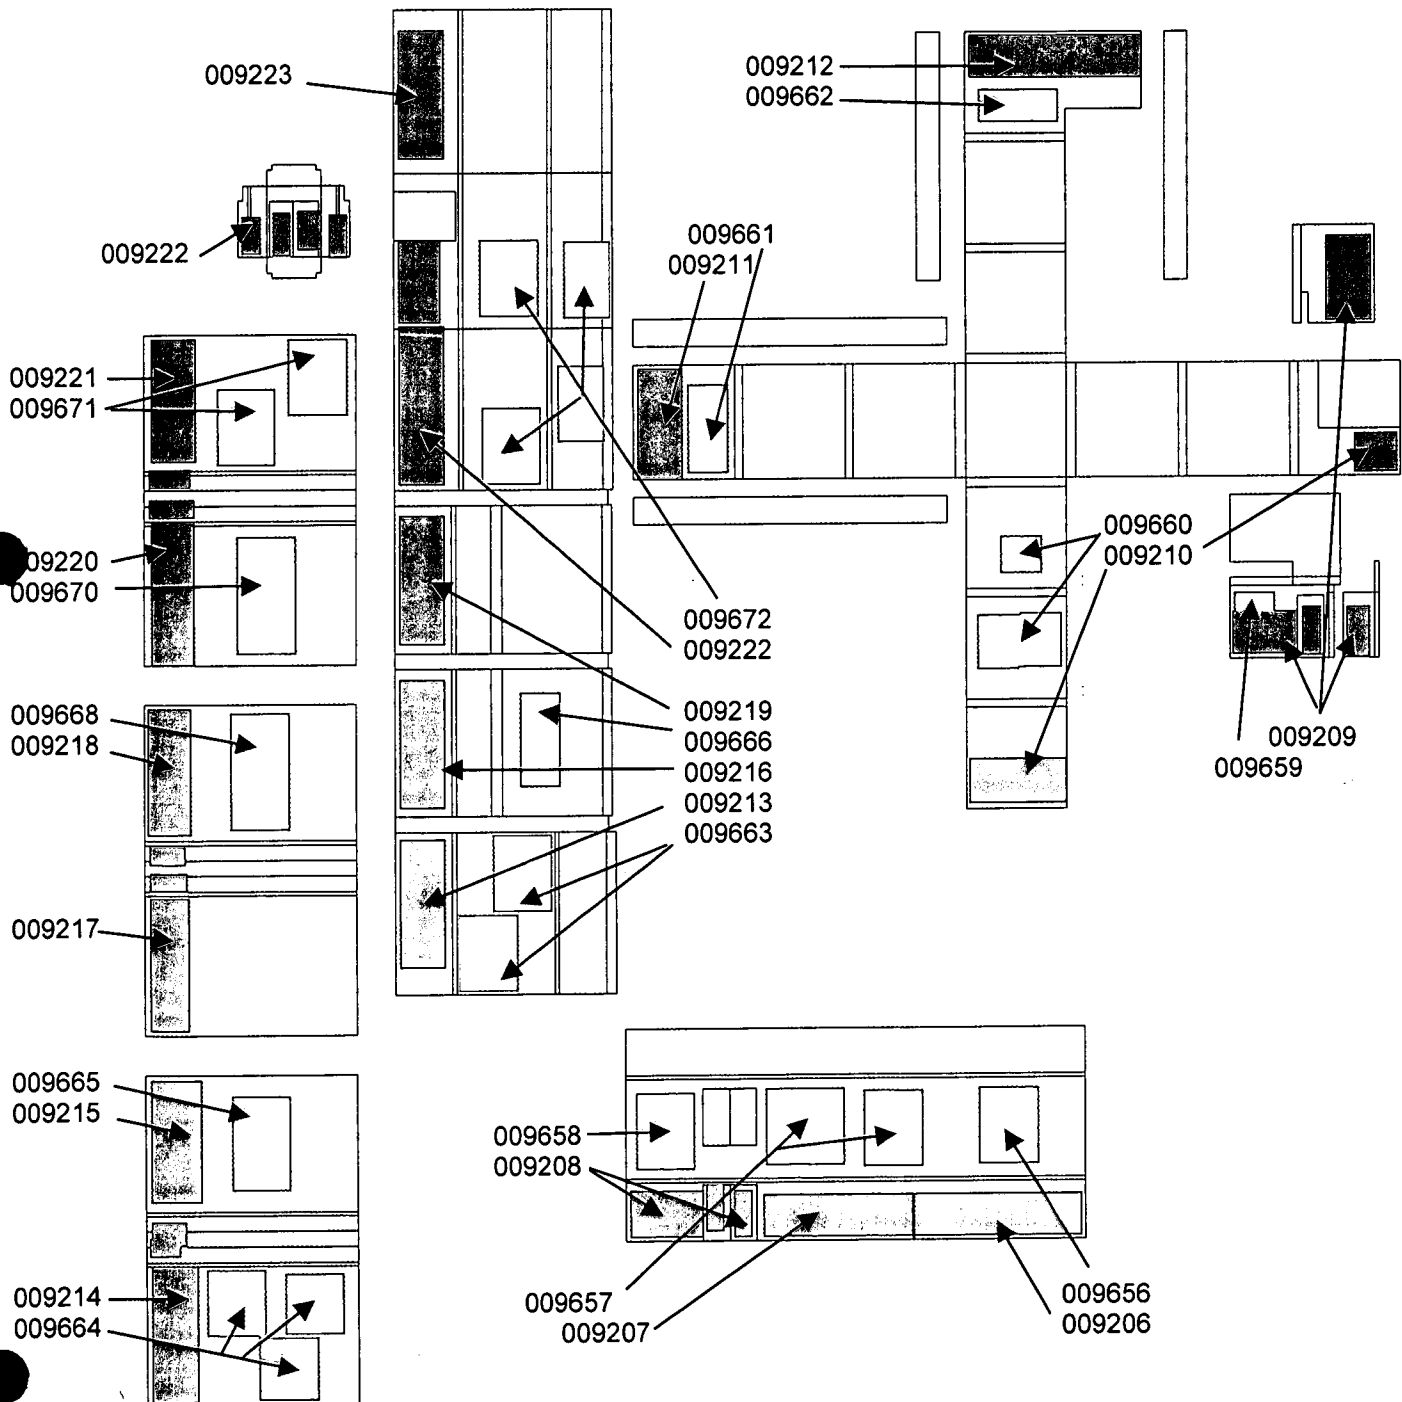


Survey Unit: 77909
B779 North Exterior Walls
Map 2 of 2

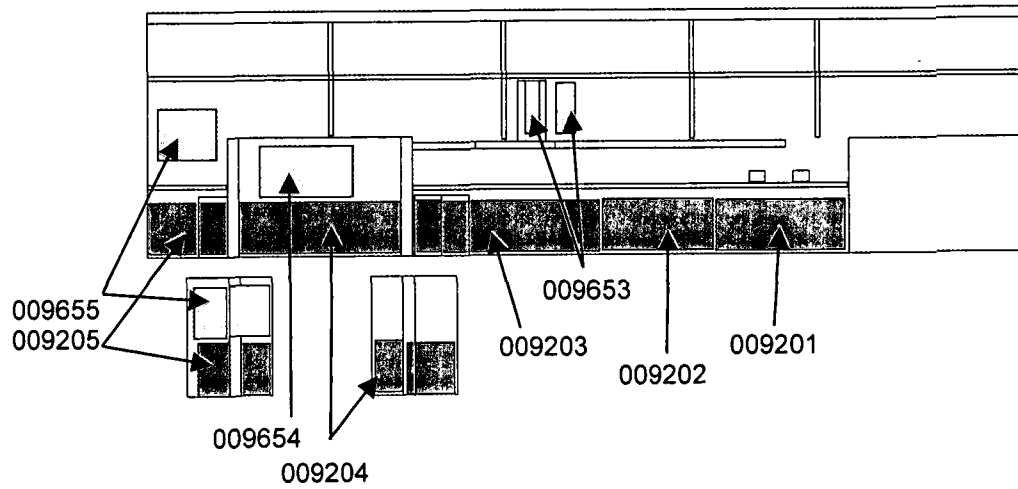


Survey Unit: 77914
B779 First and second Floor
Admin Bldg Hallways
Map 1 of 1


1st Floor Hallways




2nd Floor Hallway

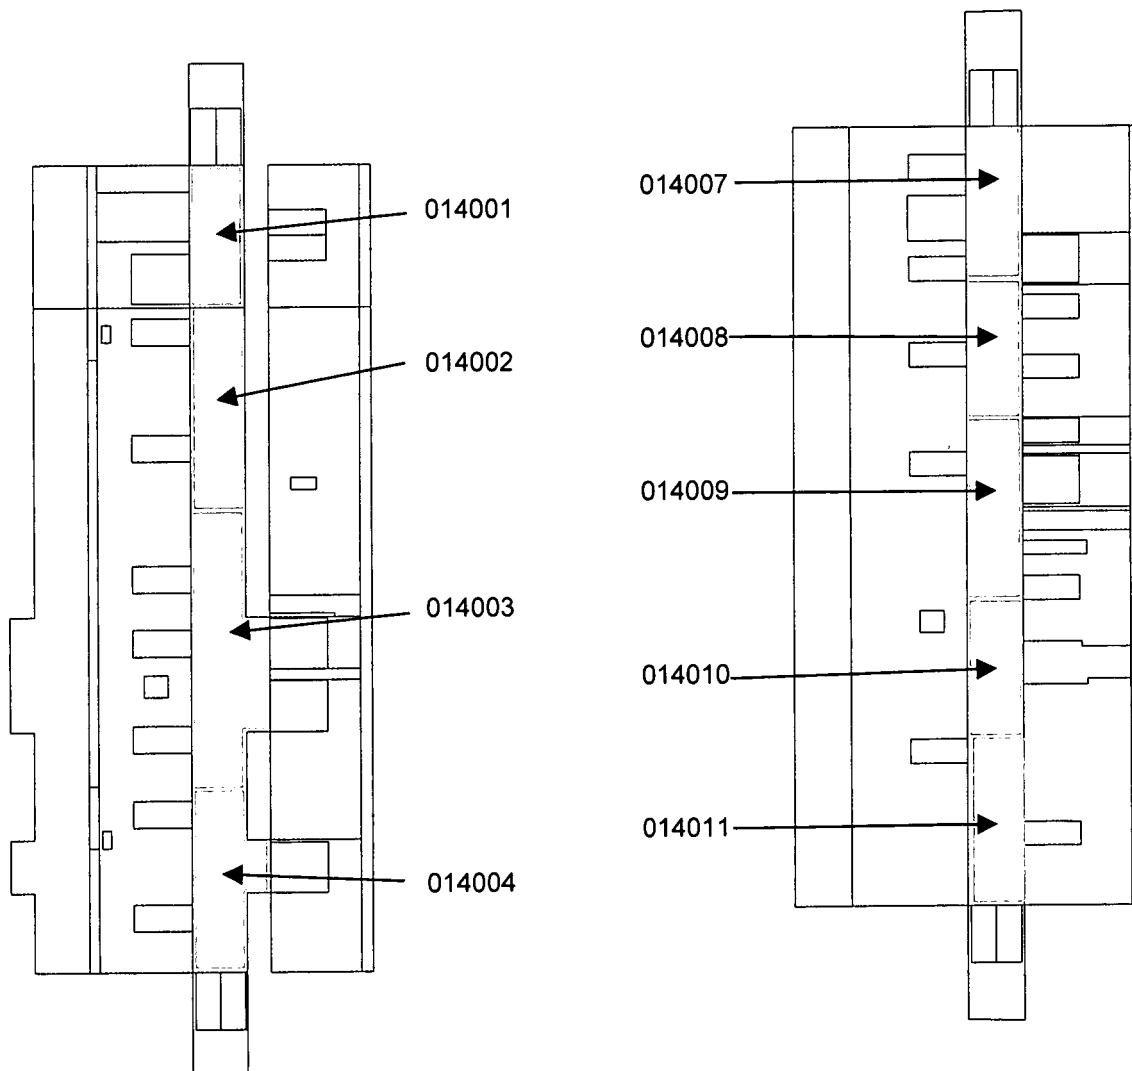


Survey Unit: 77915
B779 Second Floor Admin Area
Map 1 of 4

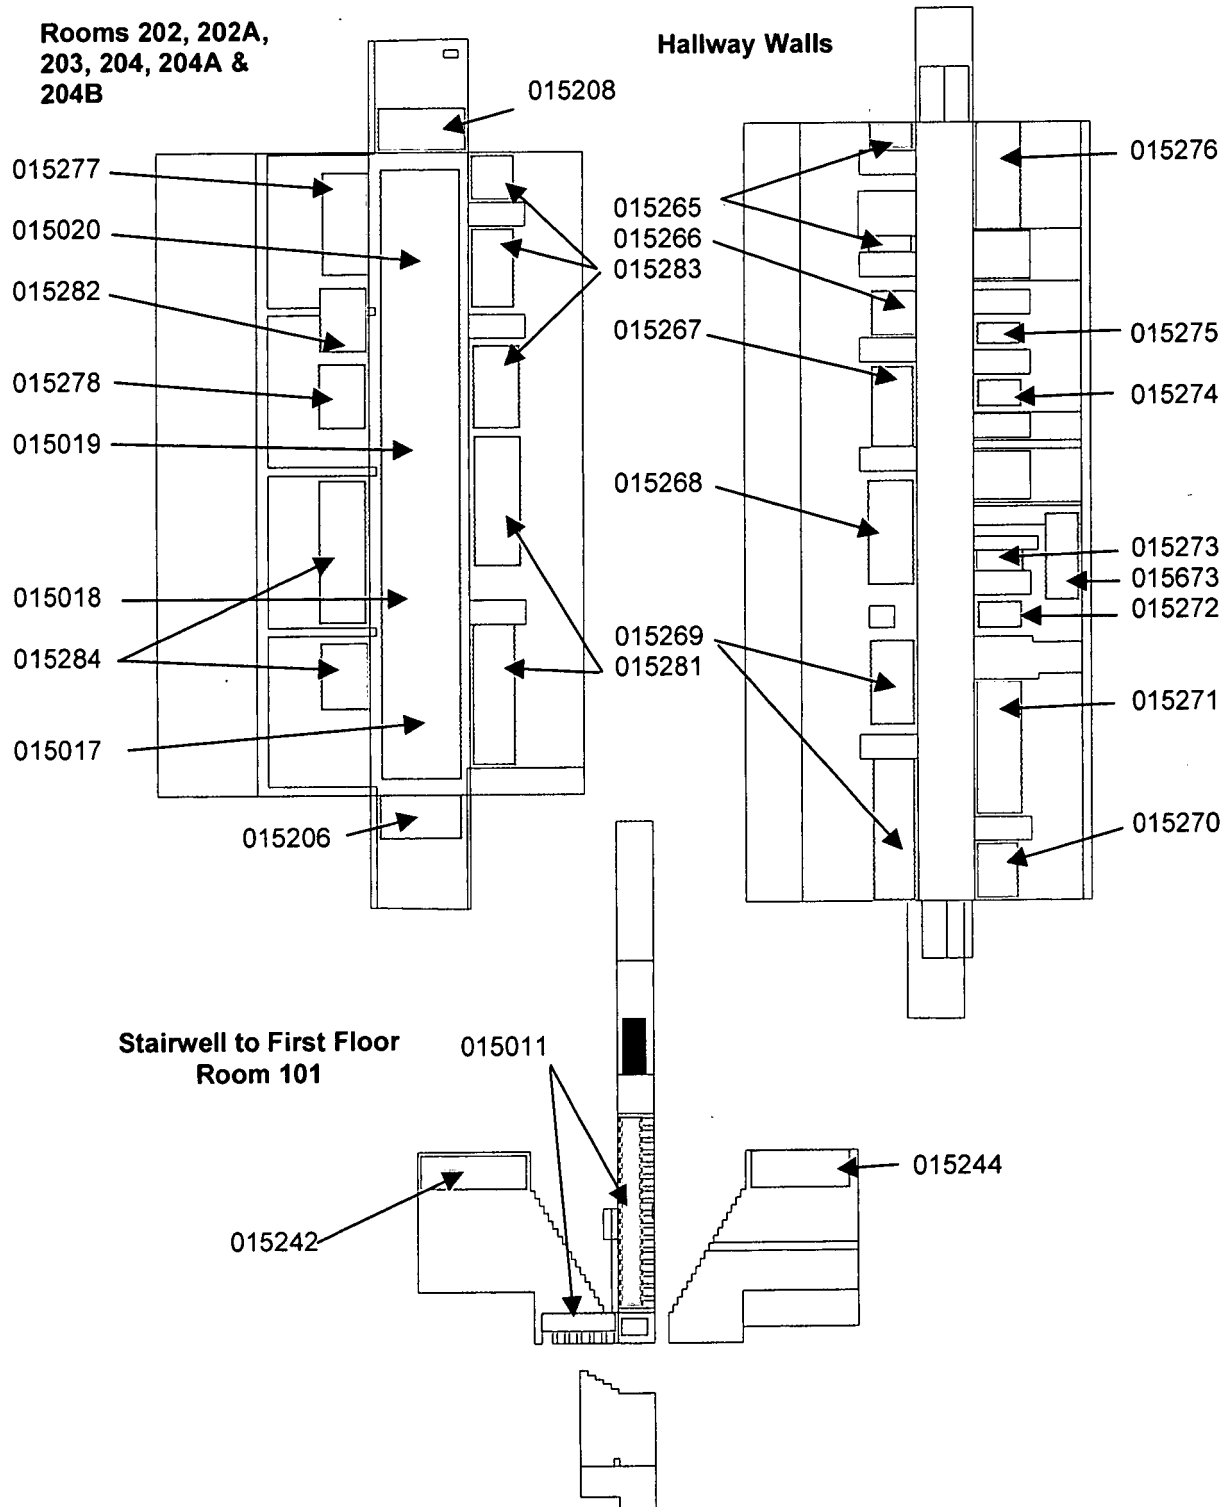

Survey Unit: 77915
B779 Second Floor Admin Area
Map 2 of 4

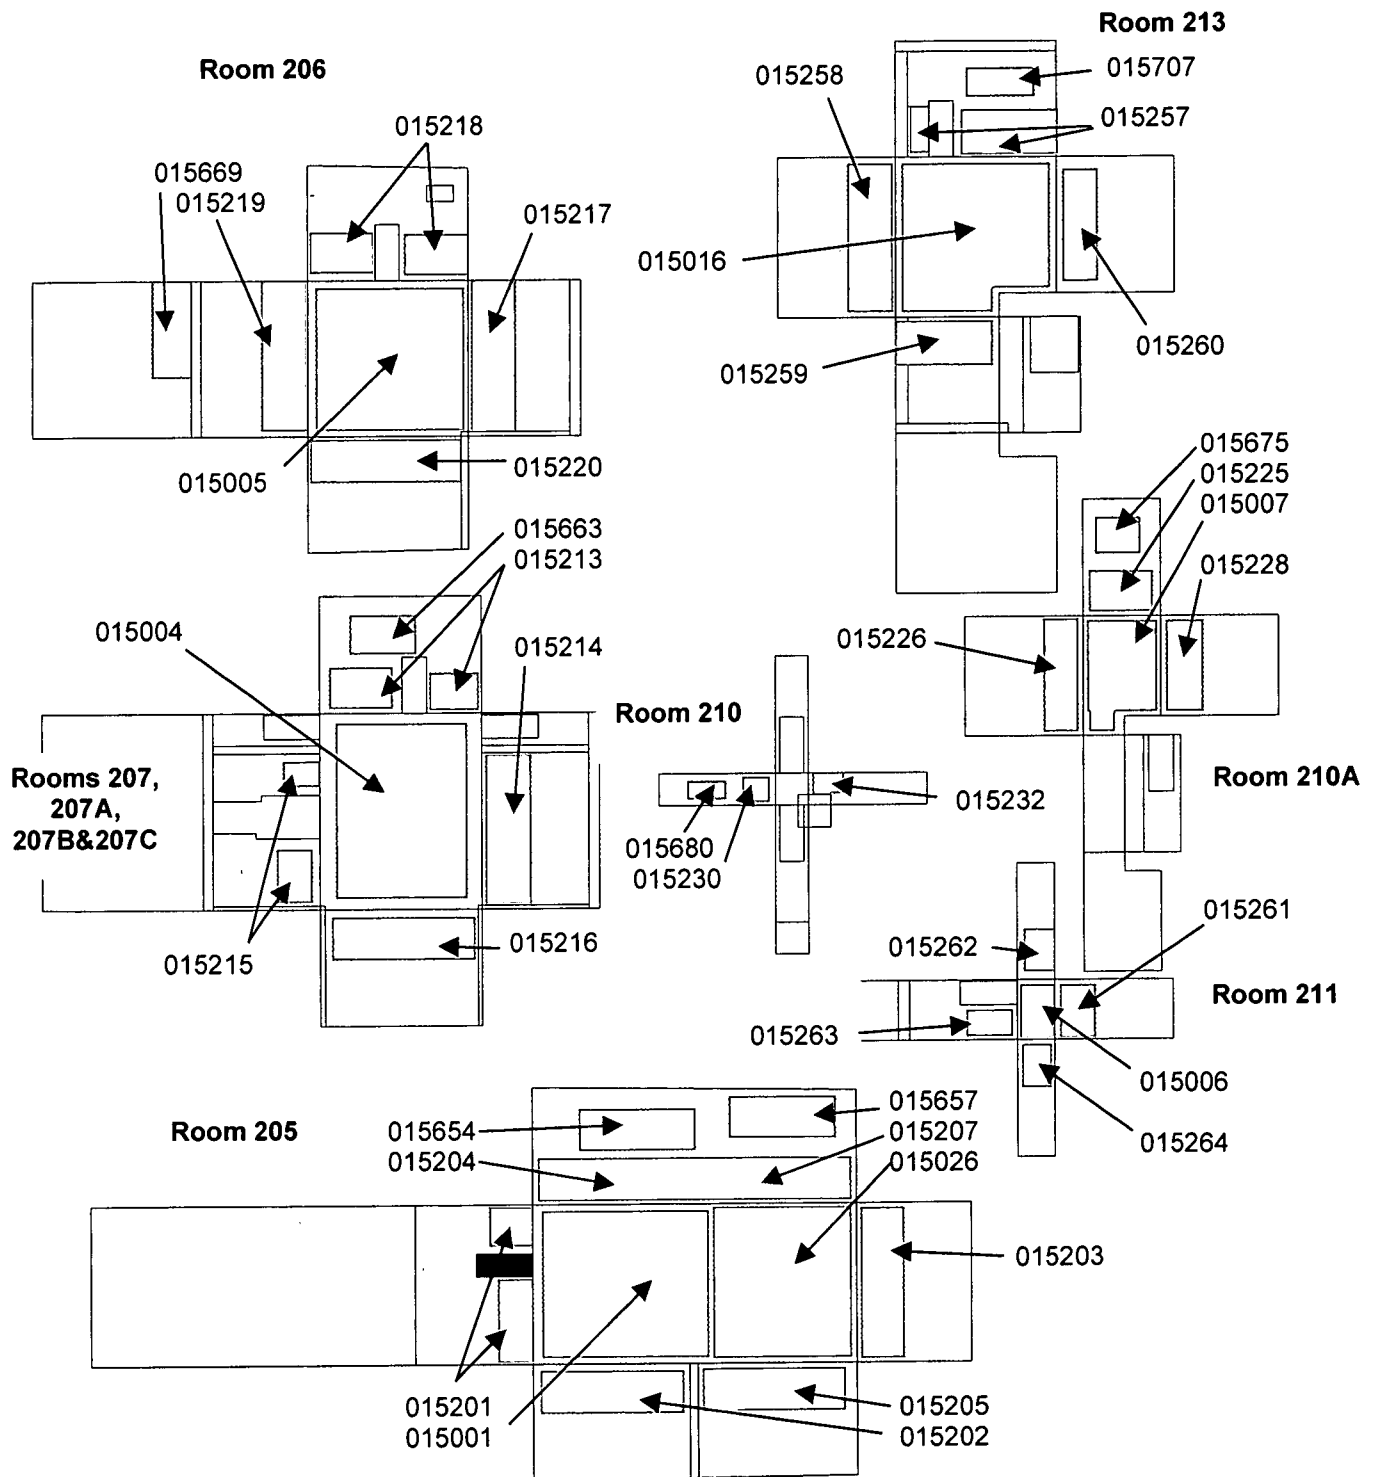


Survey Unit: 77915
B779 Second Floor Admin Area
Map 3 of 4

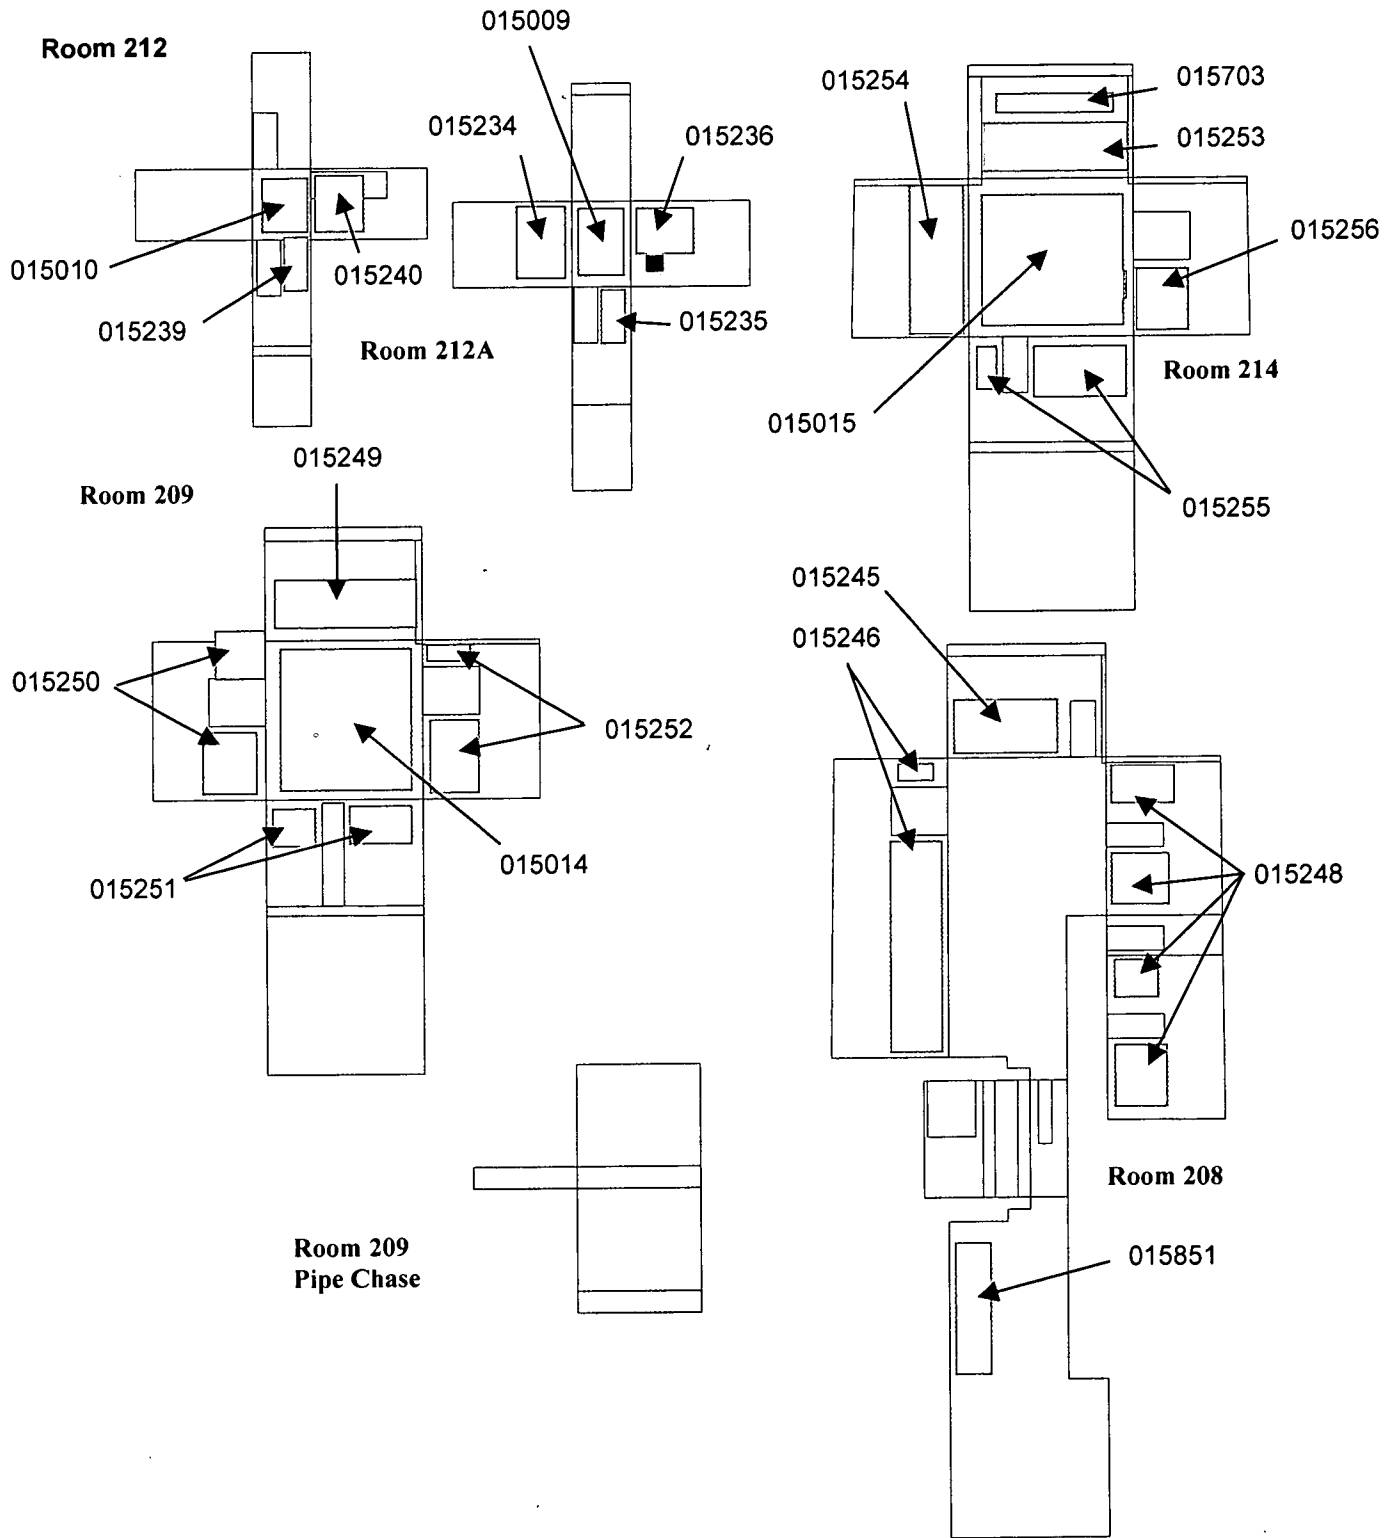

46


Survey Unit: 77915
B779 Second Floor Admin Area
Map 4 of 4

Rooms 201, 201A & 201B

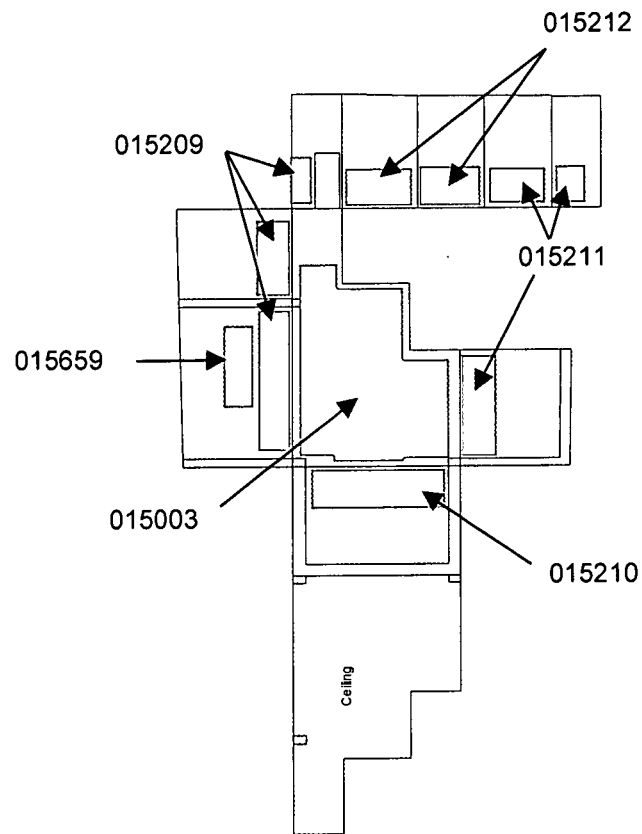


Survey Unit: 77916
B779 Second Floor Admin Area
Map 1 of 1


ROOM 208

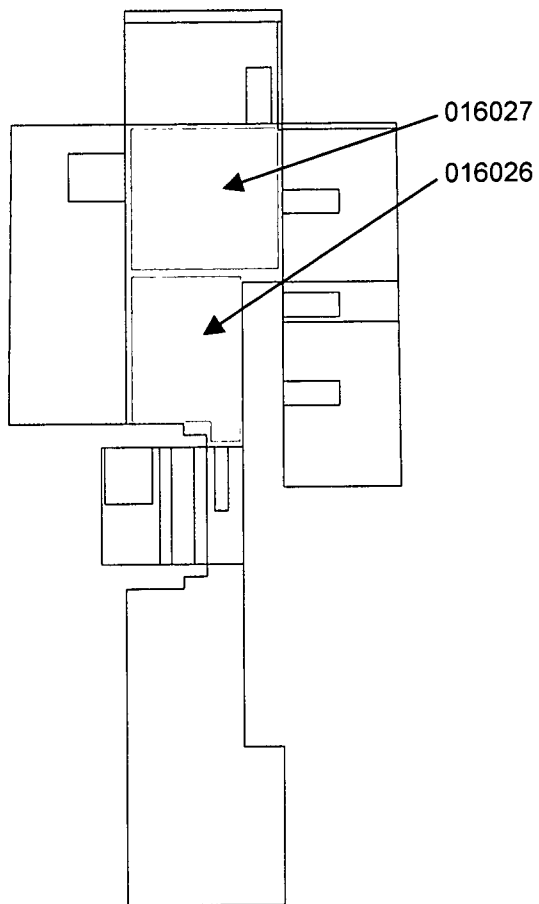


Survey Unit: 77917
B779 First Floor Office Areas (Rooms & Hallway)
Map 1 of 2

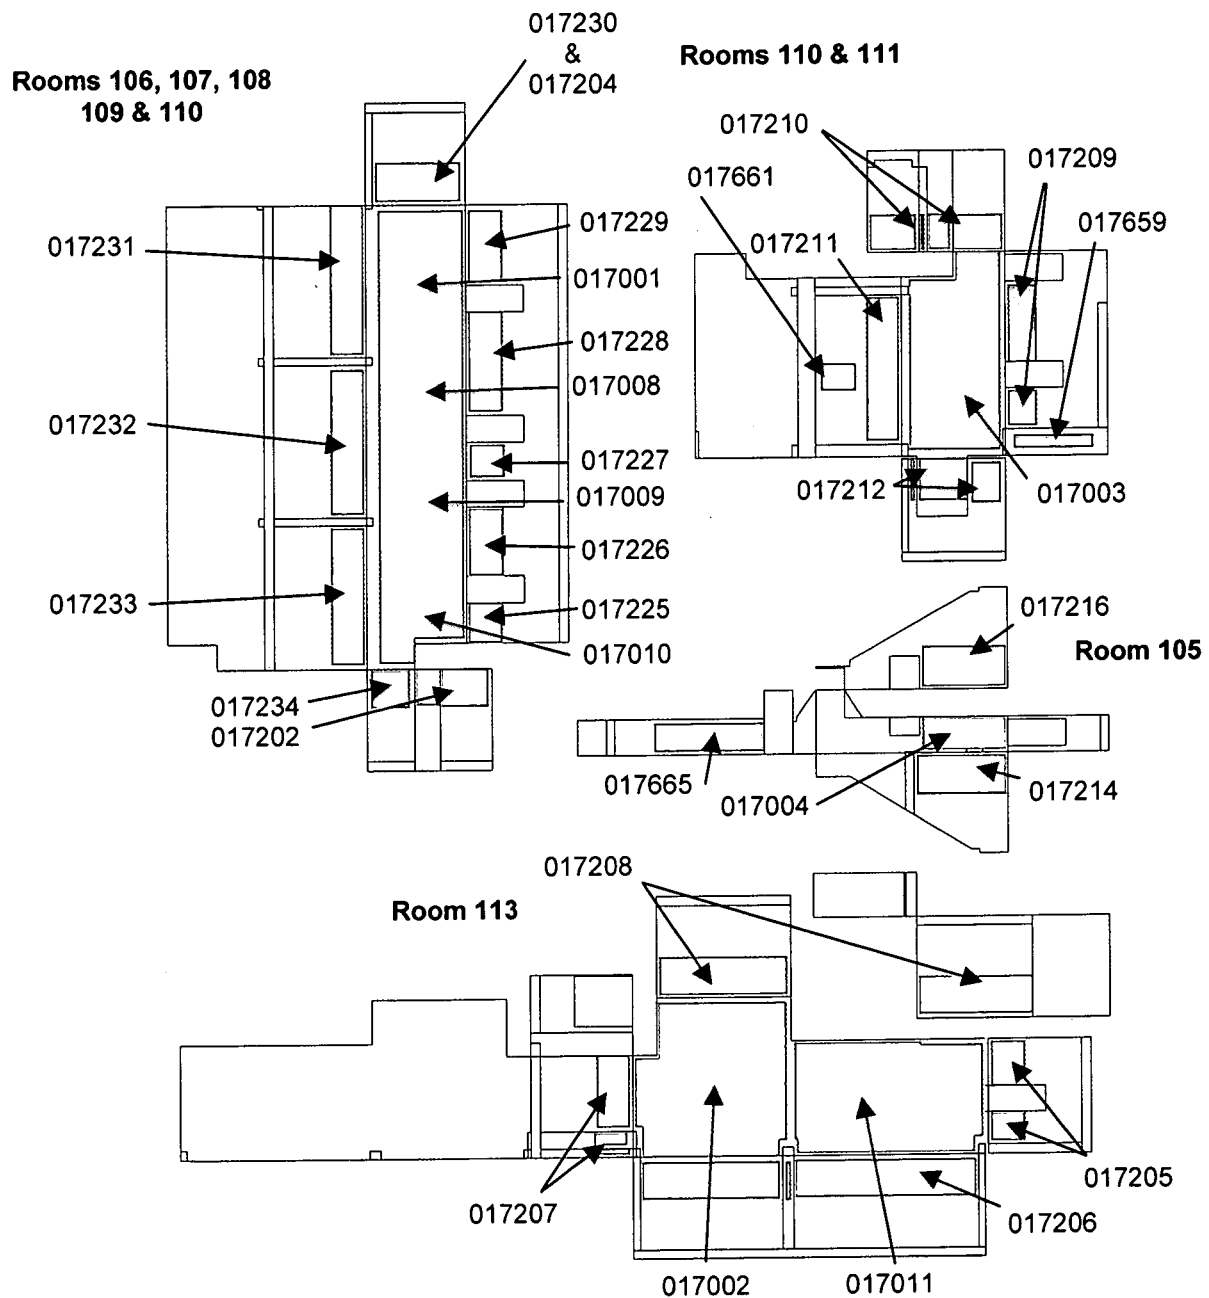

Survey Unit: 77917
B779 First Floor Office Areas (Rooms & Hallway)
Map 2 of 2

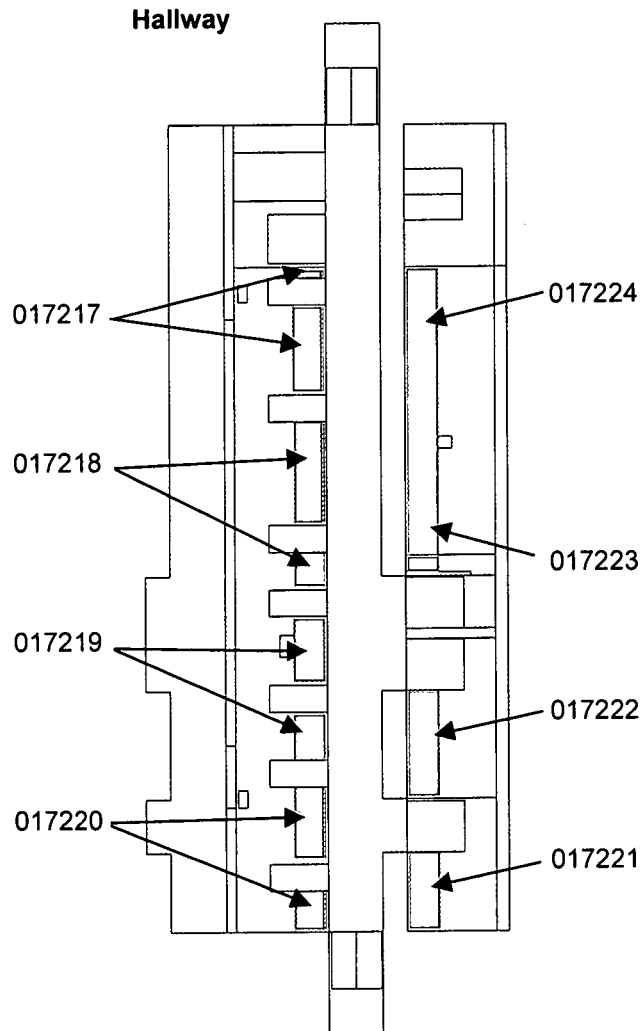


**Survey Unit 77918
B779 First Floor Admin Areas
Map 1 of 2**

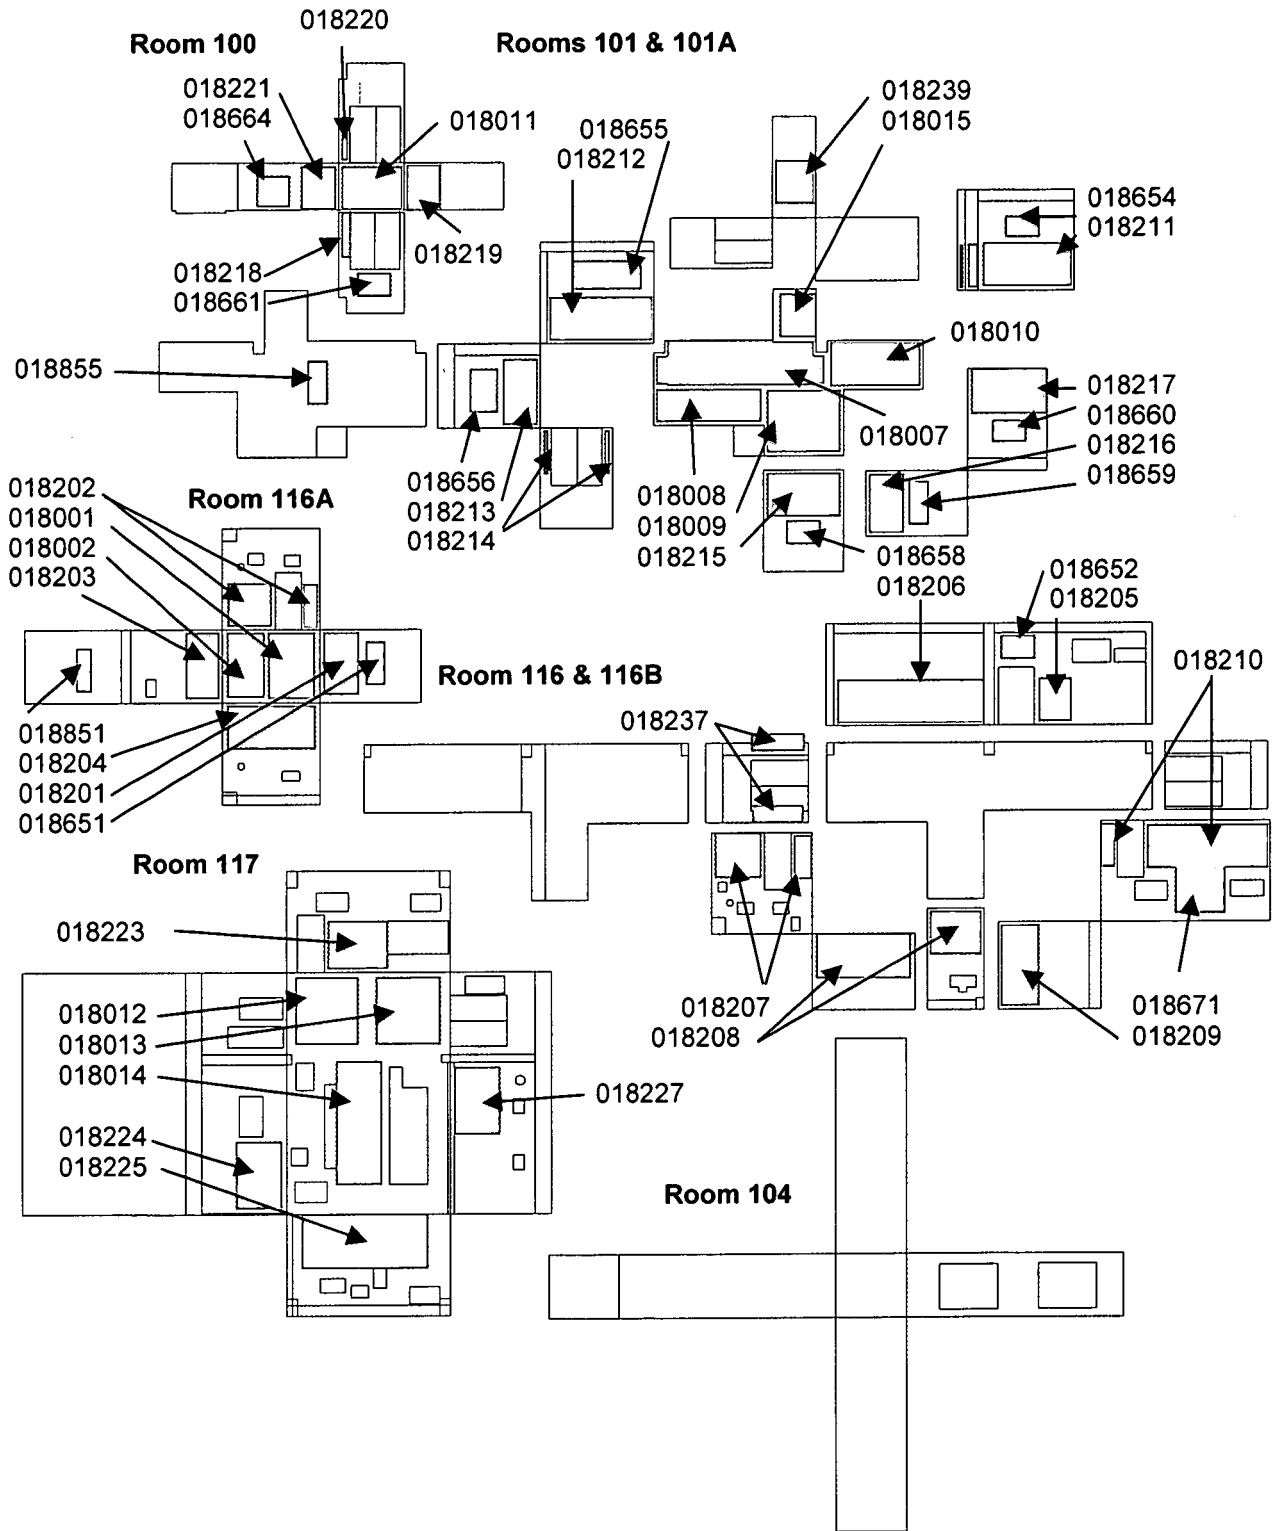


Survey Unit 77918
B779 First Floor Admin Bldg Hallways
Map 2 of 2

1st Floor Hallway

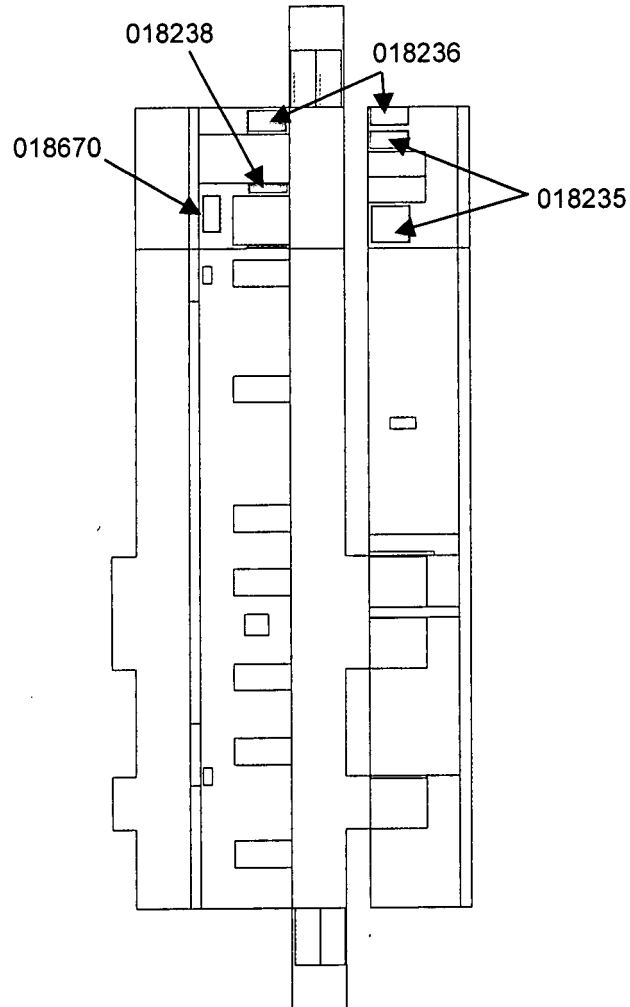

**Survey Unit 77920
B779 Rooms 114, 115, 115A & Exhaust
Duct Tower (Interior)
Map 1 of 1**

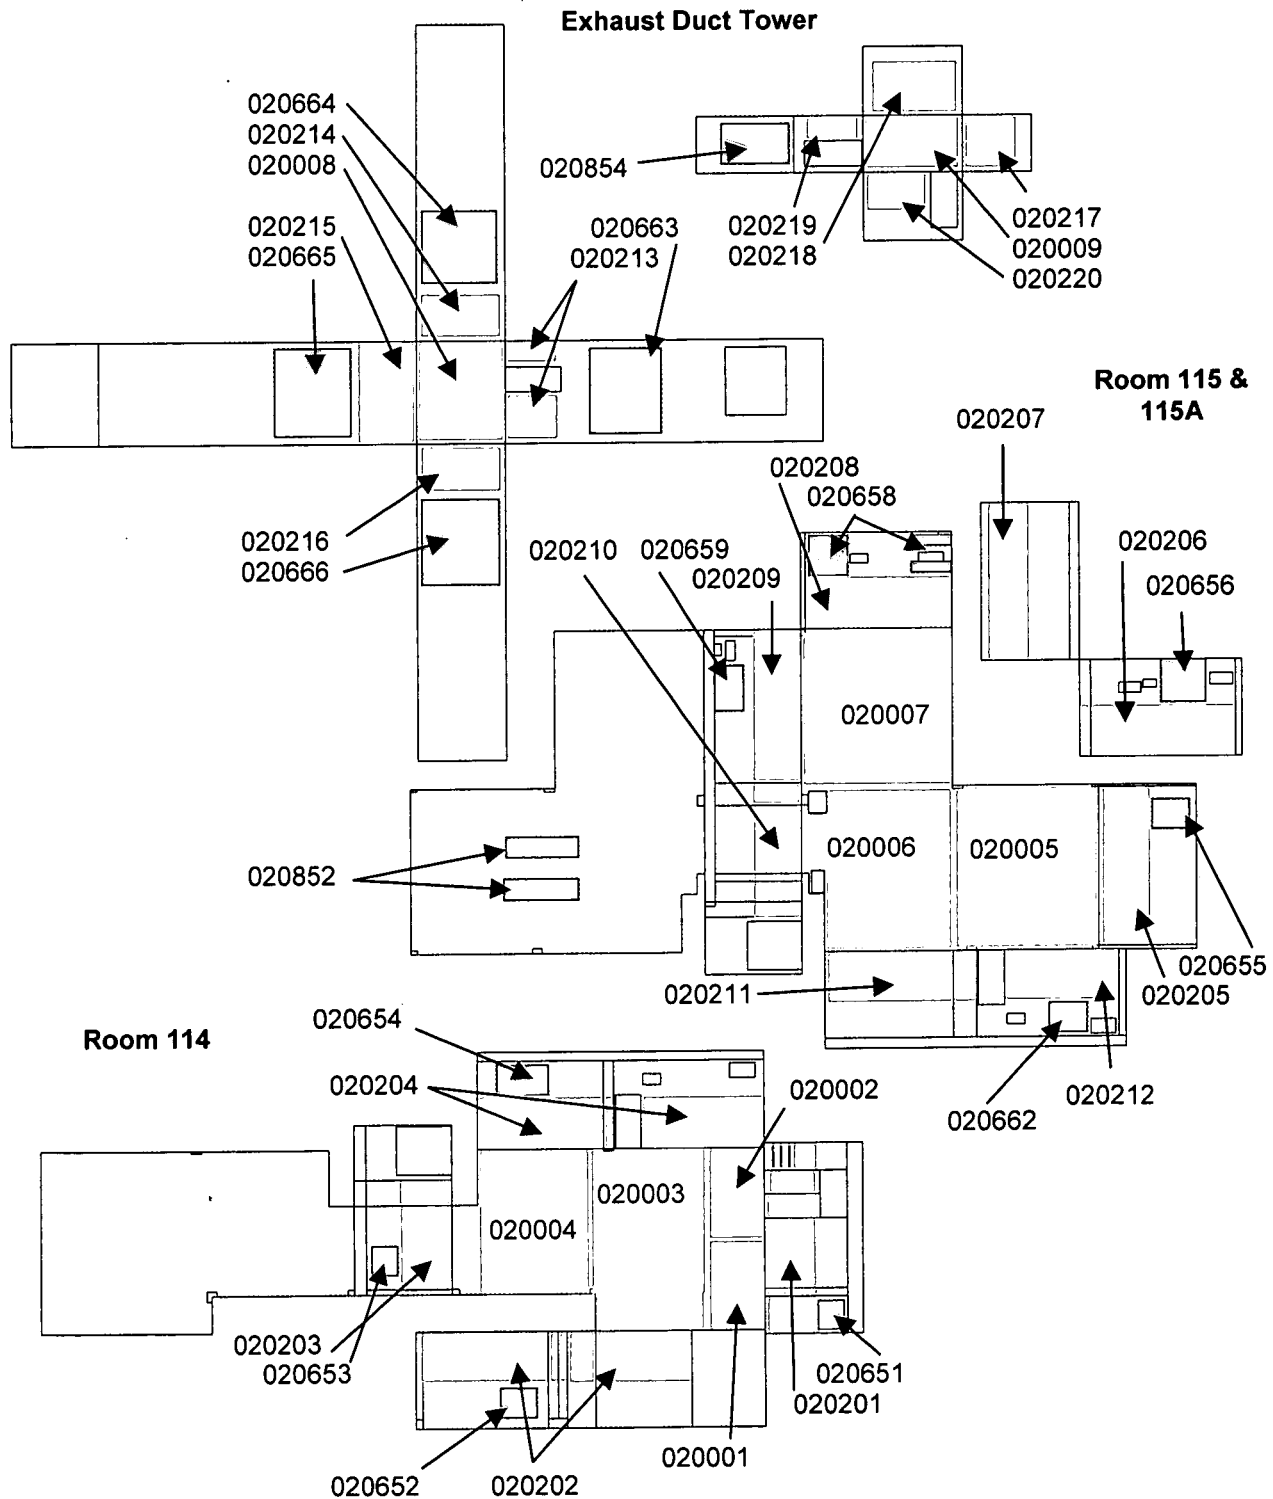

ATTACHMENT B
Survey Unit 77909 Data Summary

SURVEY UNIT 77909 DATA

COLOR CODES:

Less Than or Equal to 75% of $DCGL_W$ =



>75% and <100% of $DCGL_W$ =



Greater Than or Equal to $DCGL_W$ =



Survey Unit 77909 Data Summary

Total Surface Activity Measurements

	15	26
	Number Required	Number Obtained
MIN	-0.9	dpm/100 cm ²
MAX	56.6	dpm/100 cm ²
MEAN	22.5	dpm/100 cm ²
STD DEV	15.5	dpm/100 cm ²
TRANSURANIC DCGL _w	100	dpm/100 cm ²

Removable Activity Measurements

	15	26
	Number Required	Number Obtained
MIN	-2	dpm/100 cm ²
MAX	10	dpm/100 cm ²
MEAN	2	dpm/100 cm ²
STD DEV	3	dpm/100 cm ²
TRANSURANIC DCGL _w	20	dpm/100 cm ²

Media Sample Activity

Media Samples	15	18
	Number Required	Number Obtained

Total Uranium Results

MIN	4.5	dpm/100 cm ²
MAX	192.0	dpm/100 cm ²
MEAN	50.1	dpm/100 cm ²
STD DEV	44.4	dpm/100 cm ²
DCGL _w	5000	dpm/100 cm ²

Total Transuranic Results ⁽¹⁾

MIN	5.5	dpm/100 cm ²
MAX	85.4	dpm/100 cm ²
MEAN	17.9	dpm/100 cm ²
STD DEV	20.6	dpm/100 cm ²
DCGL _w	100	dpm/100 cm ²

Survey Unit 77909 Building 779 Total Surface Contamination Results

Total Surface Activity Survey						Quality Control Survey				
Meter Model:	NE Electra w/ DP6 Probe			Local Area Bkgd (cpm)		NE Electra w/ DP6 Probe			Local Area Bkgd (cpm)	
Instrument #:	1375	2372	2358	2.9		1194	N/A	N/A	2.7	
Cal. Due Date:	12/8/99	1/19/00	1/19/00			10/27/99	N/A	N/A		
Efficiency (c/d):	0.219	0.203	0.203			0.221	N/A	N/A		
Sample Location Number	Total Surface Activity Measurements					Quality Control Measurements				
	Serial #	Date	(cpm)	MDA (dpm/100 cm ²)	(dpm/100 cm ²)	Serial #	Date	(cpm)	MDA (dpm/100 cm ²)	(dpm/100 cm ²)
1	1375	07/23/99	4.0	38	5.0					
2	2372	07/24/99	15.3	38	56.6					
3	1375	07/23/99	6.0	38	14.1					
4	1375	07/23/99	4.0	38	5.0					
5	2358	07/26/99	5.3	38	10.9					
6	1375	07/23/99	10.0	38	32.4					
7	2358	07/26/99	6.0	38	14.1					
8	2358	07/26/99	6.7	38	17.3	1194	07/27/99	9.3	36	29.8
9	2358	07/26/99	2.7	38	-0.9					
10	2372	07/24/99	8.0	38	23.3					
11	1375	07/23/99	6.0	38	14.1					
12	2372	07/24/99	13.3	38	47.4					
13	2358	07/26/99	8.0	38	23.3					
14	2372	07/24/99	13.3	38	47.4					
15	2358	07/26/99	4.0	38	5.0					
16	1375	07/23/99	6.0	38	14.1					
17	2372	07/24/99	7.3	38	20.1					
18	2358	07/26/99	9.3	38	29.2					
19	2358	07/26/99	7.3	38	20.1	1194	07/27/99	8.0	36	23.9
20	2358	07/26/99	15.3	38	56.6					
21	2358	07/26/99	5.3	38	10.9					
22	2358	07/26/99	10.7	38	35.6					
23	2358	07/26/99	6.7	38	17.3					
24	2358	07/26/99	7.3	38	20.1					
25	2358	07/26/99	6.7	38	17.3					
26	2358	07/26/99	9.3	38	29.2					
				MIN	-0.9					
				MAX	56.6					
				MEAN	22.5					
				SD	15.5					
				Transuranic DCGL _w	100					

Survey Unit 77909 Building 779 Smear Results

Smear Location Number	Smear Results				
	Serial Number	Date Counted	Gross (cpm)	(dpm/100 cm ²)	MDA
1	888	7/26/99	0	-2	10
2	1354	7/26/99	2	5	8
3	888	7/26/99	1	1	10
4	1354	7/26/99	0	-1	8
5	888	7/26/99	4	10	10
6	1354	7/26/99	1	2	8
7	888	7/26/99	0	-2	10
8	1354	7/26/99	1	2	8
9	888	7/26/99	2	4	10
10	1354	7/26/99	1	2	8
11	888	7/26/99	1	1	10
12	1354	7/26/99	0	-1	8
13	888	7/26/99	0	-2	10
14	1354	7/26/99	0	-1	8
15	888	7/26/99	2	4	10
16	1354	7/26/99	1	2	8
17	888	7/26/99	2	4	10
18	1354	7/26/99	0	-1	8
19	888	7/26/99	0	-2	10
20	1354	7/26/99	1	2	8
21	888	7/26/99	1	1	10
22	1354	7/26/99	2	5	8
23	888	7/26/99	1	1	10
24	1354	7/26/99	0	-1	8
25	888	7/26/99	2	4	10
26	1354	7/26/99	1	2	8
			MIN	-2	
			MAX	10	
			MEAN	2	
			SD	3	
			Transuranic DCGL _w	20	

Survey Unit 77909 Building 779 Paint/Solid Media Sample Results

LOCATION DESCRIPTION	SAMPLE LOCATION NUMBER	SITE SAMPLE ID	NUCLIDE	pCi/g	MDA (pCi/g)	WEIGHT (g)	SURFACE AREA (in ²)	INDIVIDUAL NUCLIDE (dpm/100cm ²)	ESTIMATED MDA (dpm/100cm ²)	URANIUM TOTAL (dpm/100cm ²) DCGL _w =5000	TRANSURANIC TOTAL (dpm/100cm ²) DCGL _w =100
Admin. Bldg. Roof	1	001.002	U-233/234	0.022	0.094	564.57	40	10.8	45.8		
			U-235	0.000	0.051			0.0	24.8		
			U-238	0.019	0.051			9.2	24.8	20.0	
			Pu-239/240	-0.006	0.013			-3.0	6.2		
			Am-241	0.182	0.062			88.4	30.0		85.4
Admin. Bldg. Roof	2	002.002	U-233/234	0.599	0.245	67.18	40	34.6	14.2		
			U-235	0.000	0.100			0.0	5.8		
			U-238	0.719	0.219			41.6	12.7	76.2	
			Pu-239/240	0.030	0.194			1.7	11.2		
			Am-241	0.072	0.098			4.2	5.7		5.9
Admin. Bldg. Roof	3	003.002	U-233/234	Represents the average of 9 samples (includes the original). Refer to pages 9 and 10 of this data summary.							
			U-235								
			U-238								
			Pu-239/240								
			Am-241								23.9
Admin. Bldg. Roof	4	004.002	U-233/234	0.228	0.250	245.62	40	48.2	52.8		
			U-235	0.016	0.179			3.3	37.8		
			U-238	0.174	0.150			36.8	31.7	88.3	
			Pu-239/240	0.026	0.170			5.5	35.9		
			Am-241	0.035	0.094			7.3	19.8		12.8
Admin. Bldg. Roof	5	005.002	U-233/234	0.060	0.260	32.36	40	1.7	7.2		
			U-235	-0.032	0.242			-0.9	6.7		
			U-238	0.133	0.090			3.7	2.5	4.5	
			Pu-239/240	0.182	0.239			5.1	6.7		
			Am-241	0.150	0.101			4.2	2.8		9.2
Admin. Bldg. Roof	6	006.002	U-233/234	0.147	0.177	299.88	40	37.9	45.7		
			U-235	0.013	0.145			3.3	37.4		
			U-238	0.159	0.145			41.0	37.4	82.2	
			Pu-239/240	0.021	0.141			5.5	36.4		
			Am-241	0.000	0.063			0.0	16.2		5.5
Admin. Bldg. Roof	7	007.002	U-233/234	0.176	0.177	324.41	40	49.1	49.4		
			U-235	-0.011	0.134			-3.0	37.4		
			U-238	0.097	0.151			27.0	42.1	73.1	
			Pu-239/240	0.139	0.075			38.8	21.0		
			Am-241	0.064	0.154			17.9	43.0		56.7

Survey Unit 77909 Building 779 Paint/Solid Media Sample Results

LOCATION DESCRIPTION	SAMPLE LOCATION NUMBER	SITE SAMPLE ID	NUCLIDE	pCi/g	MDA (pCi/g)	WEIGHT (g)	SURFACE AREA (in ²)	INDIVIDUAL NUCLIDE (dpm/100cm ²)	ESTIMATED MDA (dpm/100cm ²)	URANIUM TOTAL (dpm/100cm ²) DCGL _w =5000	TRANSURANIC TOTAL (dpm/100cm ²) DCGL _w =100
Admin. Bldg., East Wall	8	008.002	U-233/234	0.245	0.342	70.65	40	14.9	20.8		
			U-235	-0.026	0.239			-1.6	14.5		
			U-238	0.170	0.179			10.3	10.9	23.7	
			Pu-239/240	-0.010	0.207			-0.6	12.6		
			Am-241	0.109	0.183			6.6	11.1		6.0
Admin. Bldg., South Wall	9	009.002	U-233/234	0.293	0.173	49.55	40	12.5	7.4		
			U-235	0.000	0.071			0.0	3.0		
			U-238	0.566	0.130			24.1	5.5	36.6	
			Pu-239/240	0.224	0.101			9.5	4.3		
			Am-241	0.056	0.212			2.4	9.0		11.9
Exhaust Duct Tower Exterior	10	010.002	U-233/234	0.258	0.204	43.43	40	9.6	7.6		
			U-235	-0.008	0.171			-0.3	6.4		
			U-238	0.301	0.171			11.2	6.4	20.6	
			Pu-239/240	0.044	0.118			1.6	4.4		
			Am-241	0.453	0.153			16.9	5.7		18.6
Admin. Bldg., South Wall	11	011.002	U-233/234	0.429	0.263	52.89	40	19.5	12.0		
			U-235	-0.015	0.188			-0.7	8.6		
			U-238	0.436	0.158			19.8	7.2	38.7	
			Pu-239/240	0.176	0.119			8.0	5.4		
			Am-241	0.086	0.155			3.9	7.1		11.9
Exhaust Duct Tower Exterior	12	012.002	U-233/234	0.488	0.257	80.11	40	33.6	17.7		
			U-235	-0.032	0.240			-2.2	16.5		
			U-238	0.296	0.089			20.4	6.2	51.8	
			Pu-239/240	0.076	0.216			5.2	14.9		
			Am-241	0.123	0.208			8.5	14.3		13.7
Exhaust Duct Tower Exterior	13	013.002	U-233/234	0.314	0.190	66.06	40	17.8	10.8		
			U-235	0.014	0.155			0.8	8.8		
			U-238	0.457	0.155			26.0	8.8	44.6	
			Pu-239/240	0.111	0.188			6.3	10.7		
			Am-241	0.018	0.117			1.0	6.6		7.3
Exhaust Duct Tower Exterior	14	014.002	U-233/234	0.510	0.252	96.47	40	42.3	20.9		
			U-235	0.017	0.192			1.4	15.9		
			U-238	0.364	0.215			30.2	17.8	73.9	
			Pu-239/240	0.136	0.229			11.3	19.0		
			Am-241	0.024	0.159			2.0	13.2		13.3

Survey Unit 77909 Building 779 Paint/Solid Media Sample Results

LOCATION DESCRIPTION	SAMPLE LOCATION NUMBER	SITE SAMPLE ID	NUCLIDE	pCi/g	MDA (pCi/g)	WEIGHT (g)	SURFACE AREA (in ²)	INDIVIDUAL NUCLIDE (dpm/100cm ²)	ESTIMATED MDA (dpm/100cm ²)	URANIUM TOTAL (dpm/100cm ²) DCGL _w =5000	TRANSURANIC TOTAL (dpm/100cm ²) DCGL _w =100
Exhaust Duct Tower Exterior	15	015.002	U-233/234	0.162	0.320	43.99	40	6.1	12.1		
			U-235	0.043	0.223			1.6	8.4		
			U-238	0.260	0.167			9.8	6.3	17.6	
			Pu-239/240	0.020	0.227			0.8	8.6		
			Am-241	0.515	0.153			19.5	5.8		20.2
Admin. Bldg., South Wall	16	016.002	U-233/234	0.335	0.202	50.63	40	14.6	8.8		
			U-235	0.084	0.075			3.6	3.3		
			U-238	0.104	0.139			4.5	6.1	22.8	
			Pu-239/240	0.129	0.171			5.6	7.4		
			Am-241	0.064	0.087			2.8	3.8		8.4
Exhaust Duct Tower Exterior	17	017.002	U-233/234	0.288	0.163	74.27	40	18.4	10.4		
			U-235	0.076	0.137			4.8	8.8		
			U-238	0.103	0.137			6.6	8.8	29.9	
			Pu-239/240	0.008	0.200			0.5	12.8		
			Am-241	0.084	0.222			5.4	14.2		5.9
Exhaust Duct Tower Exterior	18	018.002	U-233/234	0.074	0.265	34.45	40	2.2	7.9		
			U-235	0.000	0.099			0.0	2.9		
			U-238	0.092	0.216			2.7	6.4	4.9	
			Pu-239/240	0.131	0.266			3.9	7.9		
			Am-241	0.069	0.245			2.0	7.3		5.9

MIN	4.5	5.5
MAX	192.0	85.4
MEAN	50.1	17.9
SD	44.4	20.6
DCGL _w =	5000	100

Survey Unit 77909 Building 779 Sample Weight Data Sheet

RIN NUMBER 99A9022			RIN NUMBER 99A9022			SUM (*)
Sample Location Number	Event	Rad Screening Weight, grams	Sample Location Number	Event	Isotopic Analysis Weight, grams	Total Weight, grams
1	001.001	1.0228	1	001.002	563.55	564.57
2	002.001	1.0300	2	002.002	66.15	67.18
3	003.001	1.1072	3	003.002	466.98	468.09
4	004.001	2.1107	4	004.002	243.51	245.62
5	005.001	1.5484	5	005.002	30.81	32.36
6	006.001	1.0644	6	006.002	298.82	299.88
7	007.001	2.0999	7	007.002	322.31	324.41
8	008.001	2.0681	8	008.002	68.58	70.65
9	009.001	1.0322	9	009.002	48.52	49.55
10	010.001	2.0797	10	010.002	41.35	43.43
11	011.001	1.0234	11	011.002	51.87	52.89
12	012.001	2.0723	12	012.002	78.04	80.11
13	013.001	1.0247	13	013.002	65.04	66.06
14	014.001	1.0220	14	014.002	95.45	96.47
15	015.001	1.0495	15	015.002	42.94	43.99
16	016.001	1.0175	16	016.002	49.61	50.63
17	017.001	2.0229	17	017.002	72.25	74.27
18	018.001	1.0168	18	018.002	33.43	34.45

(*) The total weight of each sample used for the activity calculations is the sum of the weights of each aliquot removed for rad screens and the weights of each sample received for isotopic analysis.

Survey Unit 77909, Location #3 Investigation Paint/Solid Media Sample Results

LOCATION DESCRIPTION	SAMPLE LOCATION NUMBER	SITE SAMPLE ID	NUCLIDE	pc/g	MDA (pc/g)	WEIGHT (g)	SURFACE AREA (in ²)	INDIVIDUAL NUCLIDE (dpm/100cm ²)	ESTIMATED MDA (dpm/100cm ²)	URANIUM TOTAL (dpm/100cm ²)	TOTAL TRANSURANIC (dpm/100cm ²)
Admin. Bldg. Roof	3	003.002	U-233/234	0.059	0.092	468.09	40	23.7	37.0		
			U-235	0.031	0.041			12.4	16.7		
			U-238	0.067	0.113			27.1	45.5	63.1	
			Pu-239/240	0.054	0.054			23.8	21.5		
		001.001	Am-241	0.194	0.120	29.07	4	78.1	48.3		101.9
			U-233/234	0.254	0.034			63.5	8.5		
			U-235	0.047	0.042			11.8	10.5		
			U-238	0.323	0.060			80.8	15.0	156.0	
		002.001	Am-241	0.018	0.048	43.00	4	8.0	10.8		22.0
			U-233/234	0.455	0.036			168.3	13.3		
			U-235	0.050	0.045			18.5	16.6		
			U-238	0.570	0.084			210.8	31.1	397.6	
		003.001	Am-241	0.078	0.042	23.80	4	8.1	24.0		
			U-233/234	0.345	0.081			28.9	15.5		37.0
			U-235	0.000	0.048			0.0	9.8		
			U-238	0.238	0.068			48.7	13.9	119.4	
	C	004.001	Pu-239/240	0.000	0.039	29.65	4	0.0	8.0		
			Am-241	0.016	0.044			3.3	9.0		3.3
			U-233/234	0.350	0.038			89.3	1.0		
			U-235	0.052	0.047			13.3	1.2		
E	D	004.001	U-238	0.329	0.067	29.65	4	83.9	1.7	186.5	
			Pu-239/240	0.014	0.038			3.6	1.0		
			Am-241	0.000	0.041			0.0	1.0		
			U-233/234	0.223	0.036			30.2	4.9		
	E	005.001	U-235	0.049	0.044	15.74	4	6.6	6.0		
			U-238	0.152	0.063			20.6	8.5	57.4	
			Pu-239/240	0.056	0.038			7.6	5.1		
			Am-241	0.032	0.043			4.3	5.8		11.9
	F	006.001	U-233/234	0.381	0.034	28.86	4	94.6	8.4		
			U-235	0.031	0.042			7.7	10.4		
			U-238	0.425	0.061			105.5	15.1	207.8	
			Pu-239/240	-0.006	0.068			-1.5	16.9		
			Am-241	0.067	0.046			16.6	11.4		15.1

Survey Unit 77909, Location #3 Investigation Paint/Solid Media Sample Results

	G	007.001	U-233/234	0.388	0.038	44.78	4	149.5	14.6						
			U-235	0.000	0.046			0.0	17.7						
			U-238	0.444	0.078			171.0	30.0						
			Pu-239/240	-0.007	0.085			-2.7	32.7						
			Am-241	0.057	0.038			22.0	14.6				19.3		
			U-233/234	0.426	0.073			116.7	20.0						
			U-235	0.063	0.043			17.3	11.8						
			U-238	0.314	0.061			86.0	16.7						
	H		Pu-239/240	-0.017	0.089	31.84	4	-4.7	24.4						
			Am-241	0.020	0.094			5.5	25.7				0.8		

MIN	57.4	DCGL ^w =
MAX	397.6	
MEAN	192.0	
SD	112.5	
	31.4	
	100	

Sign Test on 77909 Media Sample Data

Null Hypothesis:

H_0 : The median concentration of residual radioactivity in the survey unit is greater than the $DCGL_W$.

Alternate Hypothesis:

H_a : The median concentration of residual radioactivity in the survey unit is less than the $DCGL_W$.

$DCGL_W =$ 100 dpm/100 cm^2

$\alpha =$ 0.05

(1) (2)

X_i	D_i
Survey Results (dpm/100 cm^2)	$(DCGL_W - X_i)$
85.4	14.6
5.9	94.1
101.9	-1.9
12.8	87.2
9.2	90.8
5.5	94.5
56.7	43.3
6.0	94.0
11.9	88.1
18.6	81.4
11.9	88.1
13.7	86.3
7.3	92.7
13.3	86.7
20.2	79.8
8.4	91.6
5.9	94.1
5.9	94.1

(3) No value equals zero. Therefore, $n = 18$.

(4) Number of positive differences = $17 = S+$

(5) Compare $S+$ to the critical value, k (from Table I.3 in MARSSIM)

$k = 12$

$S+ > k$

Conclusion: Reject the null hypothesis. Accept the alternate hypothesis that the median concentration of residual radioactivity in the survey unit is less than the $DCGL_W$.

Note that the assumption is that the survey unit measurements are independent random samples from a symmetric distribution. If the distribution of measurements is symmetric, the median and the mean are the same. The distribution was proven to be symmetric per section 8.2.2 of MARSSIM (difference between the median and the mean is a small fraction of the sample standard deviation).

ATTACHMENT C
Survey Unit 77915 Data Summary

SURVEY UNIT 77915 DATA

COLOR CODES:

Less Than or Equal to 75% of $DCGL_W$ =



>75% and <100% of $DCGL_W$ =



Greater Than or Equal to $DCGL_W$ =



Survey Unit 77915 Data Summary

Total Surface Activity Measurements

	15	17
	Number Required	Number Obtained
MIN	-6.3	dpm/100 cm ²
MAX	60.2	dpm/100 cm ²
MEAN	19.0	dpm/100 cm ²
STD DEV	17.6	dpm/100 cm ²
TRANSURANIC DCGL _w	100	dpm/100 cm ²

Removable Activity Measurements

	15	17
	Number Required	Number Obtained
MIN	-0.6	dpm/100 cm ²
MAX	2.4	dpm/100 cm ²
MEAN	0.7	dpm/100 cm ²
STD DEV	1.0	dpm/100 cm ²
TRANSURANIC DCGL _w	20	dpm/100 cm ²

Media Sample Activity

Media Samples	N/A	N/A
	Number Required	Number Obtained

Total Uranium Results

MIN	N/A	dpm/100 cm ²
MAX	N/A	dpm/100 cm ²
MEAN	N/A	dpm/100 cm ²
STD DEV	N/A	dpm/100 cm ²
DCGL _w	N/A	dpm/100 cm ²

Total Transuranic Results

MIN	N/A	dpm/100 cm ²
MAX	N/A	dpm/100 cm ²
MEAN	N/A	dpm/100 cm ²
STD DEV	N/A	dpm/100 cm ²
DCGL _w	N/A	dpm/100 cm ²

69

Attachment C
Page 3 of 4

Survey Unit 77915 Building 779 Smear Results

[illegible]

ATTACHMENT D
Survey Unit 77916 Data Summary


SURVEY UNIT 77916 DATA

COLOR CODES:

Less Than or Equal to 75% of $DCGL_W$ =



>75% and <100% of $DCGL_W$ =



Greater Than or Equal to $DCGL_W$ =



Survey Unit 77916 Data Summary

Total Surface Activity Measurements

	15	17
	Number Required	Number Obtained
MIN	0.0	dpm/100 cm ²
MAX	45.6	dpm/100 cm ²
MEAN	15.2	dpm/100 cm ²
STD DEV	11.3	dpm/100 cm ²
TRANSURANIC DCGL _w	100	dpm/100 cm ²

Removable Activity Measurements

	15	17
	Number Required	Number Obtained
MIN	-0.6	dpm/100 cm ²
MAX	3.9	dpm/100 cm ²
MEAN	0.6	dpm/100 cm ²
STD DEV	1.5	dpm/100 cm ²
TRANSURANIC DCGL _w	20	dpm/100 cm ²

Media Sample Activity

Media Samples	N/A	N/A
	Number Required	Number Obtained

Total Uranium Results

MIN	N/A	dpm/100 cm ²
MAX	N/A	dpm/100 cm ²
MEAN	N/A	dpm/100 cm ²
STD DEV	N/A	dpm/100 cm ²
DCGL _w	N/A	dpm/100 cm ²

Total Transuranic Results

MIN	N/A	dpm/100 cm ²
MAX	N/A	dpm/100 cm ²
MEAN	N/A	dpm/100 cm ²
STD DEV	N/A	dpm/100 cm ²
DCGL _w	N/A	dpm/100 cm ²

Survey Unit 77916 Building 779 Total Surface Contamination Results

[illegible]

75

Attachment D
Page 4 of 4

ATTACHMENT E
Survey Unit 77917 Data Summary

SURVEY UNIT 77917 DATA

COLOR CODES:

Less Than or Equal to 75% of $DCGL_{W=}$



>75% and <100% of $DCGL_{W=}$



Greater Than or Equal to $DCGL_{W=}$



Survey Unit 77917 Data Summary

Total Surface Activity Measurements

	15	17
	Number Required	Number Obtained
MIN	-7.7	dpm/100 cm ²
MAX	43.7	dpm/100 cm ²
MEAN	9.8	dpm/100 cm ²
STD DEV	13.6	dpm/100 cm ²
TRANSURANIC DCGL _w	100	dpm/100 cm ²

Removable Activity Measurements

	15	17
	Number Required	Number Obtained
MIN	-0.3	dpm/100 cm ²
MAX	2.7	dpm/100 cm ²
MEAN	0.9	dpm/100 cm ²
STD DEV	1.1	dpm/100 cm ²
TRANSURANIC DCGL _w	20	dpm/100 cm ²

Media Sample Activity

Media Samples

N/A	N/A
Number Required	Number Obtained

Total Uranium Results

MIN	N/A	dpm/100 cm ²
MAX	N/A	dpm/100 cm ²
MEAN	N/A	dpm/100 cm ²
STD DEV	N/A	dpm/100 cm ²
DCGL _w	N/A	dpm/100 cm ²

Total Transuranic Results

MIN	N/A	dpm/100 cm ²
MAX	N/A	dpm/100 cm ²
MEAN	N/A	dpm/100 cm ²
STD DEV	N/A	dpm/100 cm ²
DCGL _w	N/A	dpm/100 cm ²

79

Attachment E
Page 3 of 4

80

Attachment E
Page 4 of 4

ATTACHMENT F
Survey Unit 77918 Data Summary


SURVEY UNIT 77918 DATA

COLOR CODES:

Less Than or Equal to 75% of $DCGL_W =$



>75% and <100% of $DCGL_W =$



Greater Than or Equal to $DCGL_W =$



Survey Unit 77918 Data Summary

Total Surface Activity Measurements

	15	15
	Number Required	Number Obtained
MIN	-4.5	dpm/100 cm ²
MAX	29.1	dpm/100 cm ²
MEAN	8.5	dpm/100 cm ²
STD DEV	8.8	dpm/100 cm ²
TRANSURANIC DCGL _w	100	dpm/100 cm ²

Removable Activity Measurements

	15	15
	Number Required	Number Obtained
MIN	-0.9	dpm/100 cm ²
MAX	3.6	dpm/100 cm ²
MEAN	0.5	dpm/100 cm ²
STD DEV	1.5	dpm/100 cm ²
TRANSURANIC DCGL _w	20	dpm/100 cm ²

Media Sample Activity

Media Samples

N/A	N/A
Number Required	Number Obtained

Total Uranium Results

MIN	N/A	dpm/100 cm ²
MAX	N/A	dpm/100 cm ²
MEAN	N/A	dpm/100 cm ²
STD DEV	N/A	dpm/100 cm ²
DCGL _w	N/A	dpm/100 cm ²

Total Transuranic Results

MIN	N/A	dpm/100 cm ²
MAX	N/A	dpm/100 cm ²
MEAN	N/A	dpm/100 cm ²
STD DEV	N/A	dpm/100 cm ²
DCGL _w	N/A	dpm/100 cm ²

Survey Unit 77918 Building 779 Total Surface Contamination Results

Total Surface Activity Survey						Quality Control Survey				
Meter Model:	NE Electra w/ DP6 Probe			Local Area Bkgd (cpm)		NE Electra w/ DP6 Probe			Local Area Bkgd (cpm)	
Instrument #:	2378	N/A	N/A	2.3		1370	1194	N/A	1.4	
Cal. Due Date:	2/26/00	N/A	N/A			10/8/99	10/22/99	N/A		
Efficiency (c/d):	0.220	N/A	N/A			0.222	0.221	N/A		
Sample Location Number	Total Surface Activity Measurements					Quality Control Measurements				
	Serial #	Date	(cpm)	MDA (dpm/100 cm ²)	(dpm/100 cm ²)	Serial #	Date	(cpm)	MDA (dpm/100 cm ²)	(dpm/100 cm ²)
1	2378	09/13/99	4.7	34	10.9	1370	09/13/99	2.7	28	5.9
2	2378	09/13/99	3.3	34	4.5					
3	2378	09/13/99	4.0	34	7.7					
4	2378	09/13/99	4.7	34	10.9					
5	2378	09/13/99	4.0	34	7.7					
6	2378	09/13/99	2.7	34	1.8					
7	2378	09/13/99	5.3	34	13.6	1194	09/13/99	2.7	28	5.9
8	2378	09/13/99	7.3	34	22.7					
9	2378	09/13/99	2.7	34	1.8					
10	2378	09/13/99	1.3	34	-4.5	1370	09/13/99	2.0	28	2.7
11	2378	09/13/99	2.7	34	1.8					
12	2378	09/13/99	3.3	34	4.5	1194	09/13/99	4.0	28	11.7
13	2378	09/13/99	2.7	34	1.8					
14	2378	09/13/99	8.7	34	29.1					
15	2378	09/13/99	5.3	34	13.6					
16	N/A	N/A	N/A	N/A	N/A					
17	N/A	N/A	N/A	N/A	N/A					
18	N/A	N/A	N/A	N/A	N/A					
19	N/A	N/A	N/A	N/A	N/A					
20	N/A	N/A	N/A	N/A	N/A					
21	N/A	N/A	N/A	N/A	N/A					
22	N/A	N/A	N/A	N/A	N/A					
23	N/A	N/A	N/A	N/A	N/A					
24	N/A	N/A	N/A	N/A	N/A					
25	N/A	N/A	N/A	N/A	N/A					
				MIN	-5					
				MAX	29					
				MEAN	9					
				SD	9					
				Transuranic DCGL _w	100					

85

Attachment F
Page 4 of 4

ATTACHMENT G
Survey Unit 77920 Data Summary

SURVEY UNIT 77920 DATA

COLOR CODES:

Less Than or Equal to 75% of $DCGL_W$ =



>75% and <100% of $DCGL_W$ =



Greater Than or Equal to $DCGL_W$ =



Survey Unit 77920 Data Summary

Total Surface Activity Measurements

	15	18
	Number Required	Number Obtained
MIN	-6.2	dpm/100 cm ²
MAX	30.5	dpm/100 cm ²
MEAN	10.1	dpm/100 cm ²
STD DEV	9.8	dpm/100 cm ²
TRANSURANIC DCGL _w	100	dpm/100 cm ²

Removable Activity Measurements

	15	18
	Number Required	Number Obtained
MIN	-0.6	dpm/100 cm ²
MAX	3.9	dpm/100 cm ²
MEAN	1.3	dpm/100 cm ²
STD DEV	1.3	dpm/100 cm ²
TRANSURANIC DCGL _w	20	dpm/100 cm ²

Media Sample Activity

Media Samples

15	18
Number Required	Number Obtained

Total Uranium Results

MIN	21.3	dpm/100 cm ²
MAX	169.0	dpm/100 cm ²
MEAN	69.8	dpm/100 cm ²
STD DEV	37.7	dpm/100 cm ²
DCGL _w	5000	dpm/100 cm ²

Total Transuranic Results

MIN	0.0	dpm/100 cm ²
MAX	5.7	dpm/100 cm ²
MEAN	1.9	dpm/100 cm ²
STD DEV	1.7	dpm/100 cm ²
DCGL _w	100	dpm/100 cm ²

89

Attachment G
Page 3 of 8

Survey Unit 77920 Building 779 Smear Results

[illegible]

Survey Unit 77920 Building 779 Paint/Solid Media Sample Results

LOCATION DESCRIPTION	SAMPLE LOCATION NUMBER	SITE SAMPLE ID	NUCLIDE	pCi/g	MDA (pCi/g)	WEIGHT (g)	SURFACE AREA (in ²)	INDIVIDUAL NUCLIDE (dpm/100cm ²)	ESTIMATED MDA (dpm/100cm ²)	URANIUM TOTAL (dpm/100cm ²) DCGL _w =5000	TRANSURANIC TOTAL (dpm/100cm ²) DCGL _w =100
Room 114, Wall 7/Wall 8 Beam	1	001.002	U-233/234	0.583	0.067	30.95	40	15.5	1.8		
			U-235	0.121	0.047			3.2	1.3		
			U-238	0.608	0.067			16.2	1.8	34.9	
			Pu-239/240	0.051	0.046			1.4	1.2		
			Am-241	0.020	0.055			0.5	1.5		1.9
Room 114, Ceiling	2	002.002	U-233/234	0.558	0.071	17.23	40	8.3	1.1		
			U-235	0.128	0.050			1.9	0.7		
			U-238	0.748	0.071			11.1	1.1	21.3	
			Pu-239/240	0.017	0.047			0.3	0.7		
			Am-241	0.000	0.047			0.0	0.7		0.3
Room 114, Wall 1	3	003.002	U-233/234	1.180	0.072	60.93	40	61.8	3.8		
			U-235	0.068	0.050			3.6	2.6		
			U-238	1.060	0.041			55.6	2.1	121.0	
			Pu-239/240	0.017	0.047			0.9	2.5		
			Am-241	0.016	0.044			0.8	2.3		1.7
Room 114, Floor	4	004.002	U-233/234	0.725	0.038	41.20	40	25.7	1.3		
			U-235	0.140	0.048			5.0	1.7		
			U-238	0.744	0.068			26.4	2.4	57.0	
			Pu-239/240	0.000	0.046			0.0	1.6		
			Am-241	0.015	0.039			0.5	1.4		0.5
Room 114, Floor	5	005.002	U-233/234	0.846	0.041	28.60	40	20.8	1.0		
			U-235	0.056	0.050			1.4	1.2		
			U-238	0.872	0.041			21.5	1.0	43.6	
			Pu-239/240	0.070	0.047			1.7	1.2		
			Am-241	0.061	0.041			1.5	1.0		3.2
Room 114, Wall 4	6	006.002	U-233/234	1.010	0.041	56.55	40	49.1	2.0		
			U-235	0.149	0.051			7.2	2.5		
			U-238	0.793	0.072			38.6	3.5	95.0	
			Pu-239/240	0.000	0.043			0.0	2.1		
			Am-241	0.035	0.047			1.7	2.3		1.7
Room 115/115A, Ceiling	7	007.002	U-233/234	0.768	0.046	34.84	40	23.0	1.4		
			U-235	0.168	0.057			5.0	1.7		
			U-238	0.724	0.081			21.7	2.4	49.8	
			Pu-239/240	0.110	0.043			3.3	1.3		
			Am-241	0.079	0.076			2.4	2.3		5.7

Survey Unit 77920 Building 779 Paint/Solid Media Sample Results

LOCATION DESCRIPTION	SAMPLE LOCATION NUMBER	SITE SAMPLE ID	NUCLIDE	pCi/g	MDA (pCi/g)	WEIGHT (g)	SURFACE AREA (in ²)	INDIVIDUAL NUCLIDE (dpm/100cm ²)	ESTIMATED MDA (dpm/100cm ²)	URANIUM TOTAL (dpm/100cm ²) DCGL _w =5000	TRANSURANIC TOTAL (dpm/100cm ²) DCGL _w =100
Room 115/115A, Wall 5	8	008.002	U-233/234	0.901	0.068	66.90	40	51.9	3.9		
			U-235	0.157	0.047			9.0	2.7		
			U-238	1.020	0.068			58.7	3.9	119.6	
			Pu-239/240	0.016	0.042			0.9	2.4		
			Am-241	-0.007	0.079			-0.4	4.5		0.5
Room 115/115A, Floor	9	009.002	U-233/234	0.628	0.039	29.42	40	15.9	1.0		
			U-235	0.088	0.046			2.2	1.2		
			U-238	1.000	0.068			25.3	1.7	43.4	
			Pu-239/240	0.095	0.037			2.4	0.9		
			Am-241	0.126	0.146			3.2	3.7		5.6
Room 115/115A, Floor	10	010.002	U-233/234	0.891	0.087	23.22	40	17.8	1.7		
			U-235	0.208	0.051			4.2	1.0		
			U-238	0.960	0.041			19.2	0.8	41.1	
			Pu-239/240	0.074	0.081			1.5	1.6		
			Am-241	0.059	0.040			1.2	0.8		2.7
Room 115/115A, Wall 5	11	011.002	U-233/234	1.220	0.081	82.29	40	86.4	5.7		
			U-235	0.270	0.056			19.1	4.0		
			U-238	0.898	0.080			63.6	5.7	169.0	
			Pu-239/240	0.000	0.061			0.0	4.3		
			Am-241	0.035	0.048			2.5	3.4		2.5
Room 115/115A, Floor	12	012.002	U-233/234	0.732	0.068	21.52	40	13.6	1.3		
			U-235	0.105	0.047			1.9	0.9		
			U-238	0.804	0.038			14.9	0.7	30.4	
			Pu-239/240	0.064	0.043			1.2	0.8		
			Am-241	0.035	0.048			0.6	0.9		1.8
Room 115/115A, Wall 8	13	013.002	U-233/234	0.589	0.041	45.54	40	23.1	1.6		
			U-235	0.242	0.051			9.5	2.0		
			U-238	0.686	0.072			26.9	2.8	59.4	
			Pu-239/240	0.054	0.049			2.1	1.9		
			Am-241	0.034	0.047			1.3	1.8		3.4
Room 115/115A, Wall 6	14	014.002	U-233/234	0.714	0.039	48.23	40	29.6	1.6		
			U-235	0.141	0.048			5.9	2.0		
			U-238	0.697	0.039			28.9	1.6	64.4	
			Pu-239/240	-0.007	0.084			-0.3	3.5		
			Am-241	0.016	0.045			0.7	1.9		0.4

93

[illegible]

MIN	21.3	0.0
MAX	169.0	5.7
MEAN	69.8	1.9
SD	37.7	1.7
DCGL _w =	5000	100

94

(*) The total weight of each sample used for the activity calculations is the sum of the weights of each aliquot removed for rad screens and the weights of each sample received for isotopic analysis.

ATTACHMENT H
Survey Unit 77914 Data Summary


SURVEY UNIT 77914 DATA

COLOR CODES:

Less Than or Equal to 75% of $DCGL_W$ =



>75% and <100% of $DCGL_W$ =



Greater Than or Equal to $DCGL_W$ =



Survey Unit 77914 Data Summary

Total Surface Activity Measurements

26	40
Number Required	Number Obtained

MIN	-14.4	dpm/100 cm ²
MAX	35.3	dpm/100 cm ²
MEAN	9.4	dpm/100 cm ²
STD DEV	10.9	dpm/100 cm ²

TRANSURANIC DCGL _w	100	dpm/100 cm ²
-------------------------------	-----	-------------------------

Removable Activity Measurements

26	40
Number Required	Number Obtained

MIN	-0.6	dpm/100 cm ²
MAX	4.5	dpm/100 cm ²
MEAN	0.2	dpm/100 cm ²
STD DEV	1.0	dpm/100 cm ²

TRANSURANIC DCGL _w	20	dpm/100 cm ²
-------------------------------	----	-------------------------

Media Sample Activity

Media Samples	N/A	N/A
	Number Required	Number Obtained

Total Uranium Results

MIN	N/A	dpm/100 cm ²
MAX	N/A	dpm/100 cm ²
MEAN	N/A	dpm/100 cm ²
STD DEV	N/A	dpm/100 cm ²

DCGL _w	N/A	dpm/100 cm ²
-------------------	-----	-------------------------

Total Transuranic Results

MIN	N/A	dpm/100 cm ²
MAX	N/A	dpm/100 cm ²
MEAN	N/A	dpm/100 cm ²
STD DEV	N/A	dpm/100 cm ²

DCGL _w	N/A	dpm/100 cm ²
-------------------	-----	-------------------------

Survey Unit 77914 Building 779 Total Surface Contamination Results

Total Surface Activity Survey						Quality Control Survey				
Meter Model:	NE Electra w/ DP6 Probe			Local Area Bkgd (cpm)		NE Electra w/ DP6 Probe			Local Area Bkgd (cpm)	
Instrument #:	1262	N/A	N/A	3.1		1834	N/A	N/A	5.0	
Cal. Due Date:	12/9/99	N/A	N/A			2/4/00	N/A	N/A		
Efficiency (c/d):	0.215	N/A	N/A			0.211	N/A	N/A		
Sample Location Number	Total Surface Activity Measurements					Quality Control Measurements				
	Serial #	Date	(cpm)	MDA (dpm/100 cm²)	(dpm/100 cm²)	Serial #	Date	(cpm)	MDA (dpm/100 cm²)	(dpm/100 cm²)
1	1262	10/08/99	3.3	39	0.9					
2	1262	10/08/99	7.3	39	19.5					
3	1262	10/08/99	5.3	39	10.2					
4	1262	10/08/99	10.7	39	35.3	1834	10/08/99	7.3	49	11
5	1262	10/08/99	6.7	39	16.7					
6	1262	10/08/99	10.7	39	35.3	1834	10/08/99	9.3	49	20
7	1262	10/08/99	7.3	39	19.5					
8	1262	10/08/99	4.7	39	7.4					
9	1262	10/08/99	6.7	39	16.7					
10	1262	10/08/99	6.0	39	13.5					
11	1262	10/08/99	3.3	39	0.9					
12	1262	10/08/99	6.7	39	16.7					
13	1262	10/08/99	7.3	39	19.5					
14	1262	10/08/99	4.0	39	4.2					
15	1262	10/08/99	0.7	39	-11.1					
16	1262	10/08/99	7.3	39	19.5					
17	1262	10/08/99	0.0	39	-14.4					
18	1262	10/08/99	2.0	39	-5.1					
19	1262	10/08/99	2.7	39	-1.9					
20	1262	10/08/99	2.7	39	-1.9					
21	1262	10/08/99	2.7	39	-1.9					
22	1262	10/08/99	4.0	39	4.2					
23	1262	10/08/99	4.7	39	7.4					
24	1262	10/08/99	3.3	39	0.9					
25	1262	10/08/99	3.3	39	0.9					
26	1262	10/08/99	3.3	39	0.9					
27	1262	10/08/99	5.3	39	10.2					
28	1262	10/08/99	7.3	39	19.5					
29	1262	10/08/99	6.0	39	13.5					
30	1262	10/08/99	7.3	39	19.5					
31	1262	10/08/99	4.7	39	7.4					
32	1262	10/08/99	7.3	39	19.5					
33	1262	10/08/99	4.0	39	4.2					
34	1262	10/08/99	6.0	39	13.5					
35	1262	10/08/99	7.3	39	19.5					
36	1262	10/08/99	6.0	39	13.5					
37	1262	10/08/99	2.7	39	-1.9					
38	1262	10/08/99	3.3	39	0.9					
39	1262	10/08/99	5.3	39	10.2					
40	1262	10/08/99	6.0	39	13.5					
				MIN	-14.4					
				MAX	35.3					
				MEAN	9.4					
				SD	10.9					
				Transuranic DCGL _w	100					

Survey Unit 77914 Building 779 Smear Results

Smear Results					
Smear Location Number	Serial Number	Date Counted	Gross (cpm)	(dpm/100 cm ²)	MDA
	1	814	10/8/99	0.0	-0.6
	2	1407	10/8/99	0.0	0.0
	3	814	10/8/99	0.0	-0.6
	4	1407	10/8/99	0.0	0.0
	5	814	10/8/99	0.0	-0.6
	6	1407	10/8/99	0.0	0.0
	7	814	10/8/99	0.5	0.9
	8	1407	10/8/99	0.0	0.0
	9	814	10/8/99	0.5	0.9
	10	1407	10/8/99	0.0	0.0
	11	814	10/8/99	0.0	-0.6
	12	1407	10/8/99	0.5	1.5
	13	814	10/8/99	0.0	-0.6
	14	1407	10/8/99	0.5	1.5
	15	814	10/8/99	0.5	0.9
	16	1407	10/8/99	0.5	1.5
	17	814	10/8/99	0.0	-0.6
	18	1407	10/8/99	0.0	0.0
	19	814	10/8/99	0.0	-0.6
	20	1407	10/8/99	0.0	0.0
	21	814	10/8/99	0.0	-0.6
	22	1407	10/8/99	0.5	1.5
	23	814	10/8/99	0.5	0.9
	24	1407	10/8/99	0.0	0.0
	25	814	10/8/99	0.0	-0.6
	26	1407	10/8/99	0.0	0.0
	27	814	10/8/99	0.0	-0.6
	28	1407	10/8/99	0.0	0.0
	29	814	10/8/99	0.0	-0.6
	30	1407	10/8/99	0.0	0.0
	31	814	10/8/99	0.0	-0.6
	32	1407	10/8/99	0.0	0.0
	33	814	10/8/99	0.0	-0.6
	34	1407	10/8/99	0.0	0.0
	35	814	10/8/99	0.0	-0.6
	36	1407	10/8/99	0.0	0.0
	37	814	10/8/99	0.0	-0.6
	38	1407	10/8/99	1.5	4.5
	39	814	10/8/99	0.0	-0.6
	40	1407	10/8/99	0.5	1.5
				Transuranic DCG _W	20
					SD
					MEAN
					MAX
					MIN
					-0.6
					4.5
					0.2
					1.0

ATTACHMENT I
SCM/SIMS Quality Control Charts

QC Control Charts

The QC control charts follow. The QC survey is to be distinguished from the daily source check. The daily source check allows the survey technician to determine that the instrument is responding within acceptable values for total background subtracted counts using a radioactive source. The QC survey is used to continuously update the control charts. The control charts are used to determine the efficiency of each detector assembly, verify adequate system performance, and to observe trends that may indicate monitoring system problems.

The control chart plots a mean of the Pu-238 source measurements (source strength = 194,400 dpm). It also shows the range of plus and minus 20% from the mean value. A typical QC survey contains at least six measurements (or twelve, if a recount assembly is used), which consist of at least three before and three after the radiological survey. Additionally, every three hours, three (or six) more measurements are obtained during the survey.


In a few cases, values have fallen outside of 20% from the mean. Singular events outside the range are not considered failures in the measurement process provided that the other values are within the acceptable range. Single events outside the range are treated as normal statistical occurrences.

The thirteen QC surveys that failed resulted in the rejection of 79 of the 547 surveys that were performed in the Admin Building. The rejected QC data is not reported on these charts.


The control chart for SCM2 in 180 recount mode exhibits a run below the mean line and a subsequent run above the mean line. However, the QC measurements of interest are within tolerance for the specific date and survey unit, and are therefore usable. The performance of this unique combination of SCM2 in the 180 recount mode has since been improved based on an upgrade of the assembly unit housing the detectors.

In conclusion, the following charts show no trends that would require re-survey of the Admin Building final surveys.

B779 Admin Bldg. Alpha Final Status Survey Quality Control Chart
SCM1 180corner mode, 7.26.99 - 9.10.99
Survey Units 77909, 77914, 77915, 77916, 77917, 77918, 77920

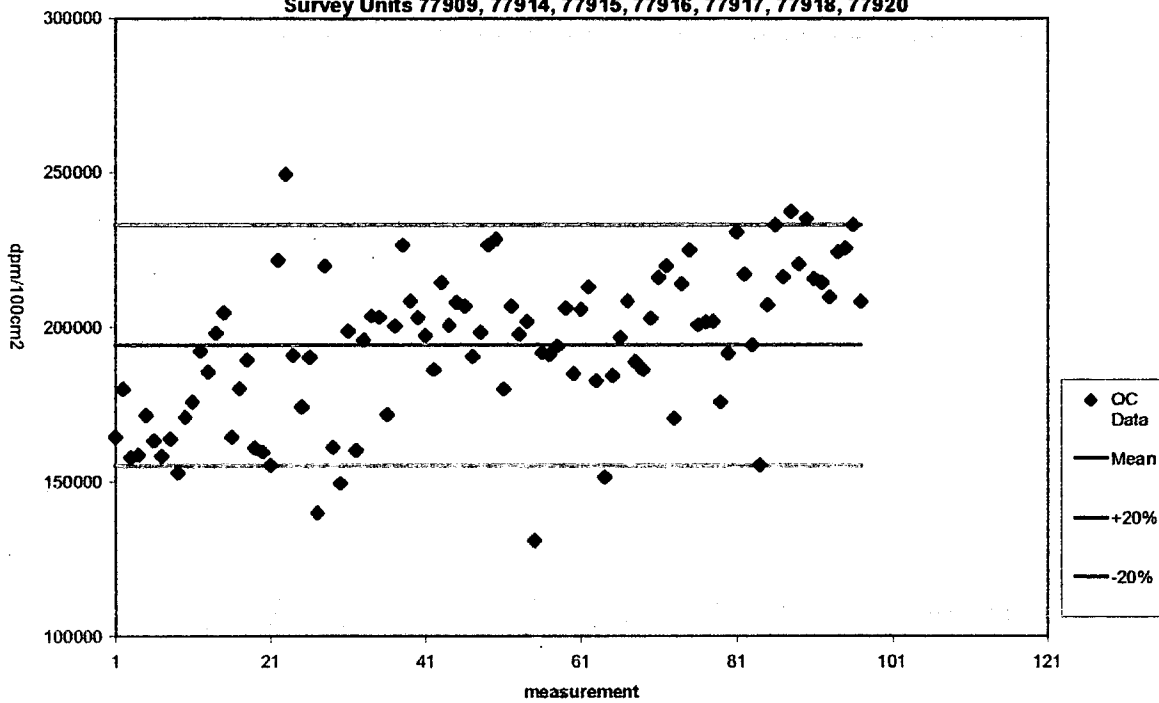

B779 Admin Bldg. Alpha Final Status Survey Quality Control Chart
SCM2 180corner mode, 7.12.99 - 7.27.99
Survey Units 77909, 77914, 77915, 77916, 77917, 77918, 77920

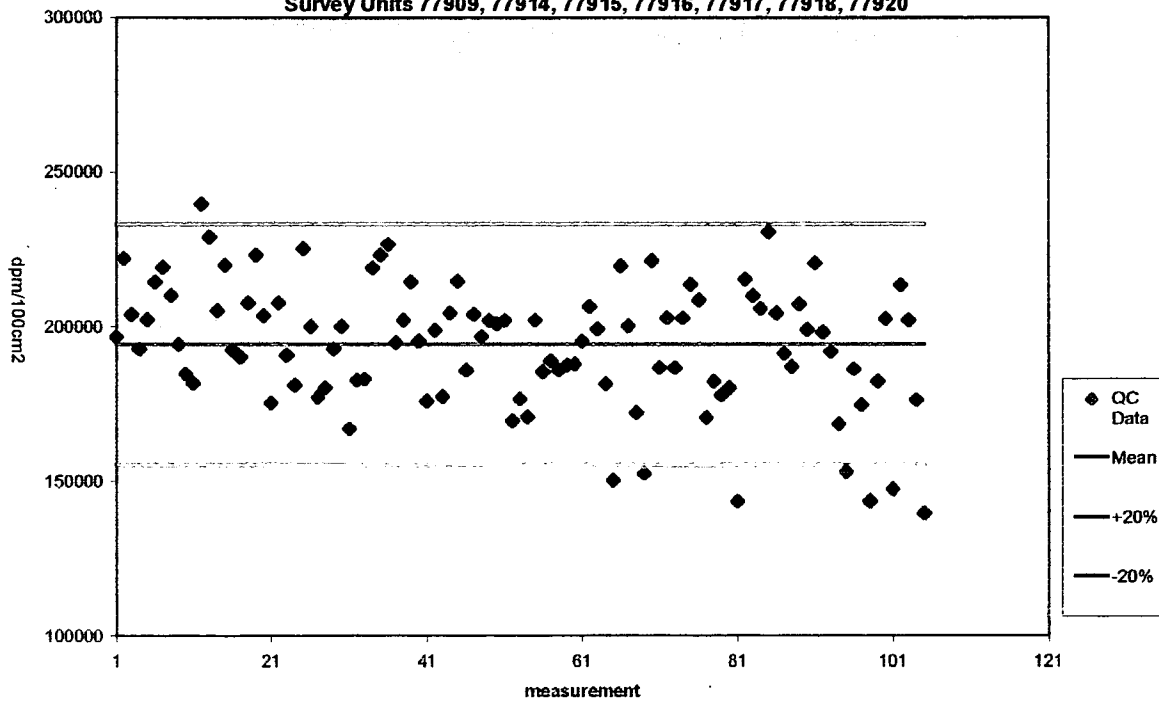


102

B779 Admin Bldg. Alpha Final Status Survey Quality Control Chart

SCM3 180corner mode, 8.2.99 - 10.8.99


Survey Units 77909, 77914, 77915, 77916, 77917, 77918, 77920

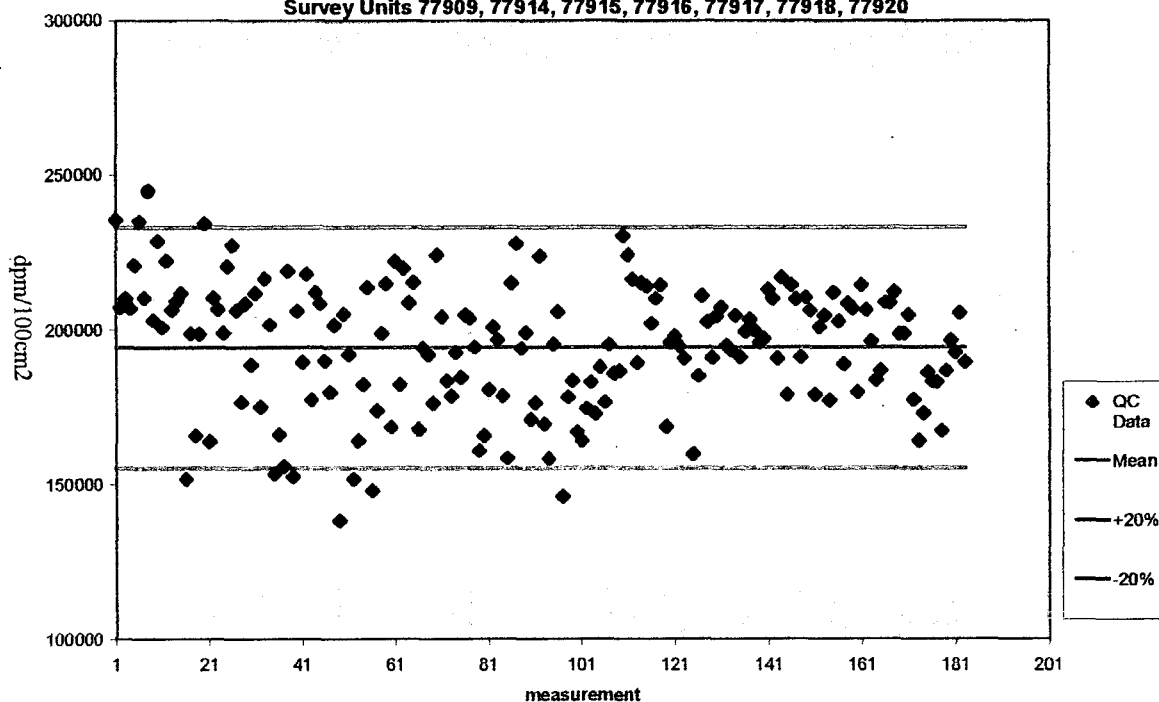

B779 Admin Bldg. Alpha Final Status Survey Quality Control Chart

SCM2 180recount mode, 7.15.99

Survey Units 77909, 77914, 77915, 77916, 77917, 77918, 77920

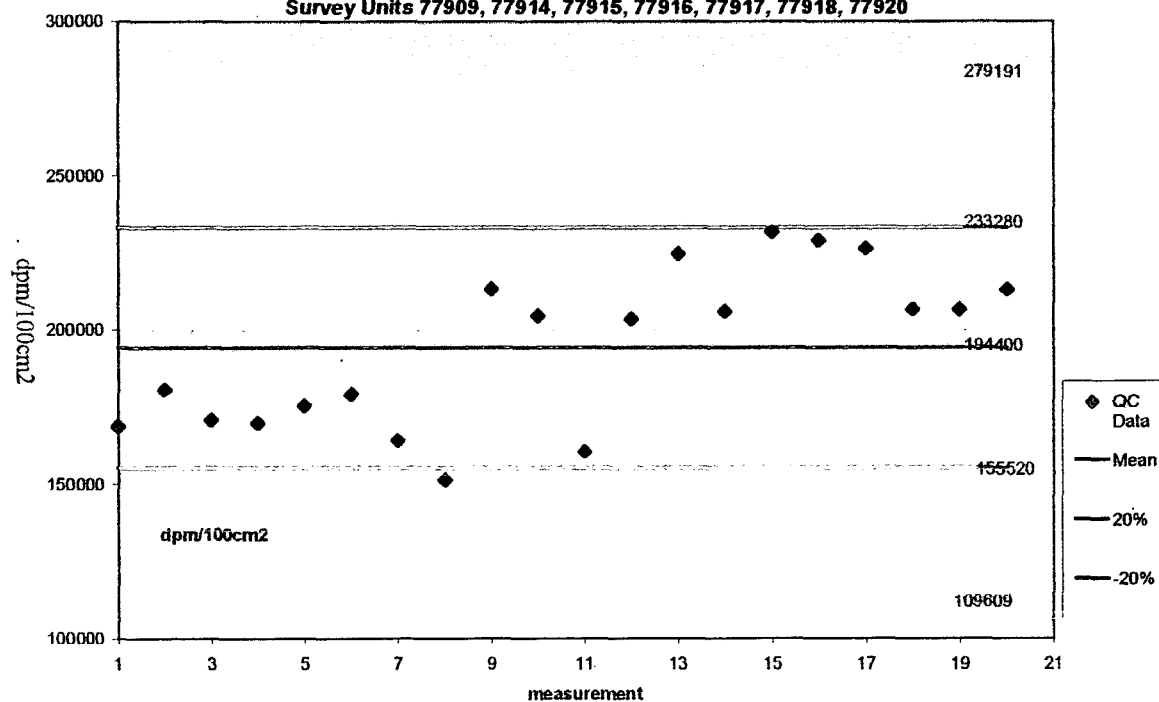


103

B779 Admin Bldg. Alpha Final Status Survey Quality Control Chart

SCM1 180recount mode, 7.23.99 - 8.12.99

Survey Units 77909, 77914, 77915, 77916, 77917, 77918, 77920

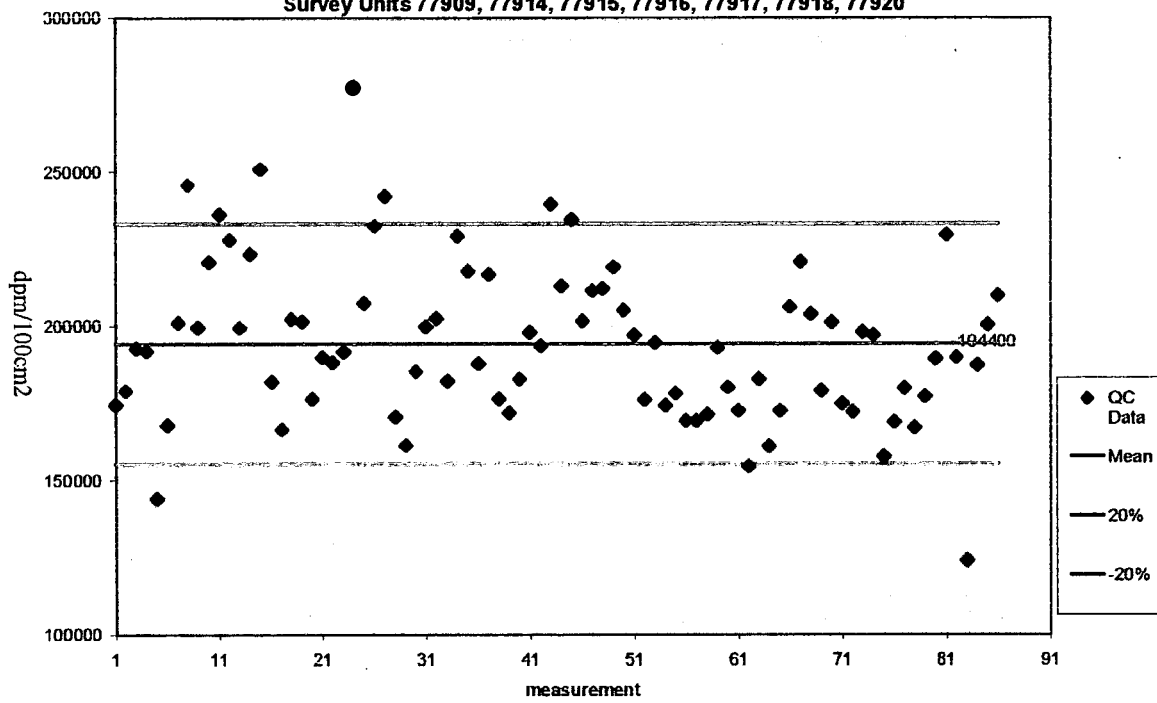

ATTACHMENT J
Data Quality Assessment

DATA QUALITY ASSESSMENT

1.0 INTRODUCTION

Data used in making management decisions for waste management remedial actions must be of adequate quality to support the decisions. Adequate data quality for decision-making is required by applicable RMRS and K-H corporate policies (RMRS, 1998, §6.4 and K-H, 1997, §7.1.4 and 7.2.2), as well as by the customer (DOE, RFFO; Order O 414.1, Quality Assurance, §4.b.(2)(b)). Regulators and the public also expect decisions and data that are technically and legally defensible. Verification and validation of the data ensure that data used in decisions resulting from the FSS are usable and defensible.

Verification and validation (V&V) of this Closeout Radiological Survey Report (CRSR) are the primary components of the DQA. The DQA presented in this Attachment supports conclusions in the report through implementation of the QA/QC guidelines taken from the following MARSSIM sections:

- §4.9, Quality Control
- §8.2, Data Quality Assessment
- §9.0, Quality Assurance & Quality Control
- Appendix E, Assessment Phase of the Data Life Cycle
- Appendix N, Data Validation using Data Descriptors

The MARSSIM-recommended criteria for V&V of final status survey data, listed above, are concisely summarized in Table J-1. The MARSSIM criteria are listed across the top of the table whereas the project's proof of implementation is listed along the left-hand side of the page. Note that 1 or more "checks" *per column* exhibit compliance with the MARSSIM criteria, which are listed per column.

Statistical evaluation of the data, through use of the Sign Test (included in Attachment B), was performed for Survey Unit 77909 to determine, with statistical confidence at the 95% level, that survey units in question were below DOE free-release limits. Measurement results from the remaining Survey Units were compared on a one-to-one basis with free-release criteria given in DOE Order 5400.5.

2.0 VERIFICATION OF RESULTS

Verification ensures that data produced and used by the project are documented and traceable per quality requirements. Verification consisted of reviewing the project's data relative to three subsets: 1) radiological scans with the SCM/SIMS, 2) static surveys for removable and total contamination, and 3) radiochemical data resulting from samples taken and subsequently analyzed via alpha spectrometry. Consistent with previous reports, verification will confirm that

- Chain-of-Custody was intact from initial sampling through transport and final analysis;
- preservation and hold-times were within tolerance
- format and content of the data are clearly presented relative to goals of the project, i.e., to determine, with at least 95% confidence, that the survey units of interest (Administrative Area) are adequate for radiological free release.

Verification of the Administrative Area FSS data will also address quality records representing implementation of the following quality controls:

- calibrations (radiochemistry & surveys), for accuracy
- laboratory control samples (LCS -- radiochemistry), for accuracy
- blanks (radiochemistry), for accuracy
- duplicate measurements (radiochemistry & surveys), for precision
- chemical yield (radiochemistry), for accuracy
- count times (radiochemistry & surveys), for sensitivity
- sample preparations (radiochemistry), for accuracy, representativeness

SCM data were systematically managed and verified as follows:

- A Survey Summary Sheet was generated for each survey unit, which lists all Final Survey subunits, including the associated investigation surveys.
- The Survey Summary Sheet was compared to the electronic (computer) directory structure, the Project File (handwritten survey data) and SIMS-generated survey data for a "3-way" verification.
- The Survey Summary Sheet, ordered by survey unit, is maintained at the front of the electronic database file structure as well as in the file cabinet.

Areas requiring 100% survey coverage were verified as follows:

- An overview map was developed for each survey unit.
- The overview map served as an index of the subunits, and defined the subunit boundaries.
- Every survey map used to document Electra as well as SCM scan surveys was reviewed against the overview map for coverage.
- Because every survey map was correlated to a survey form, and all survey forms were inventoried via the survey summary sheet, 100% coverage of every subunit was assured.

Areas requiring 10% to 50% survey coverage were verified as follows:

- The area covered by the survey was summed for each subunit.
- The subunit size was electronically calculated in Turbocad using scaled maps.
- The sum of all subunits in the survey unit was summed.
- The area surveyed was divided by the sum of the subunit size to determine the percent surveyed.

Upon completion of the data management activities listed above, an independent peer review was performed on each surveys package.

All relevant Quality records associated with the Administrative Area D&D final status survey decisions will be submitted to the RMRS Records Center for permanent storage within 30 days of the conclusion of the 779 project.

3.0 VALIDATION OF RESULTS

Validation consists of a technical review of all data that directly support the FSS decisions, so that any limitations of the data relative to project goals are delineated, and the associated data are qualified (caveated) accordingly. Data were validated relative to:

107

- 1) the DQOs of the project as defined in the CRSP for the 779 Cluster (i.e., did the final data achieve the initial DQOs of the project?), and
- 2) quality criteria discussed throughout various sections in the MARSSIM (sections noted previously).

MARSSIM criteria for the broad topic of "data quality assessment" used in final status surveys generally falls within the generic categories of quality assurance, quality control, data validation, and data assessment (including verification and validation). Table J-1 provides a "crosswalk" that lists the primary MARSSIM sections and generic data quality criteria (at top) and their corresponding implementation via the CRSP, CRSR, and project files.

All of the significant MARSSIM criteria listed in Table J-1 are summarily discussed within the "PARCC Parameters" section. PARCC parameters are congruent with "data descriptors" in the MARSSIM parlance and address characteristics of the data that must be defined for scientific integrity and defensibility. Recall that at least one "X" in each column of the table constitutes achievement of the MARSSIM quality objective (vs. one "X" in each row). The next section, which addresses the PARCC parameters -- Precision, Accuracy, Representativeness, Comparability, and Completeness, will also include discussion on bias and sensitivity, two more data descriptors emphasized in MARSSIM.

Validation of data to K-H contractual requirements (K-H Statements of Work is currently performed on a site-wide basis at ~25% frequency by the K-H Analytical Services Division. Satisfactory validation at this frequency indicates that subcontracted labs are operating competently relative to industry-wide standards, and more specifically, that sample custody and analytical procedures are implemented under defined quality controls on a sitewide programmatic basis. Sitewide data validation coupled with annual lab audits provides the inference that all analytical and radiochemical results not *specifically* validated, are represented by the percentage that is validated. Radiochemistry performed for this FSS were verified as meeting K-H contractual requirements -- Module RC01-B.3 for alpha spectrometry (4/24/98 and Module 9, 7/6/98).

PARCC PARAMETERS

PRECISION

Fundamental reproducibility of measurements, at levels near MDA and between different types/brands of instruments, are discussed at length in the "B779 Final Status Survey Meeting Resolution of CDPHE/EPA/IVC Comments, 6/30/99", which is included as Appendix 5 to the *Closeout Radiological Survey Report for Building 729*.

1) Radiological Surveys

Precision of the radiological instrumentation was satisfactory based on tolerance charting of daily source measurements for each individual sensor used on the project, which includes all measurement types (scans and static measures for total contamination, swipes for removable). Adequate precision was established through instrument performance within a $\pm 20\%$ range as defined by measurement results compared to a standard source value. Based on standard protocol (*Radiological Safety Practices*) any measurement exceeding the defined tolerance limits required corrective action (repair or replacement) prior to the instrument's use in final survey.

For the SCM, three (3) measurements were taken for each QC check "episode", i.e., before and after each set of measurements per work shift (Millennium QAP, 3/99). Of the 3 measurements, 2 measurements had to pass specifications. Performance checks performed on the SCM are shown in the respective control charts (Attachment I). Two measurements not within the $\pm 20\%$ tolerance envelope required corrective action prior to the instrument's use or re-use.

Duplicate total surface activity measurements were also periodically acquired ($\geq 5\%$ frequency of original final survey measurements) on the MARSSIM survey grids. All duplicate measurements were within tolerance based on the acceptance criterion that both results be below $DCGL_w$ (note that, even if populations were "significantly" different between real and duplicate results, if both duplicate and real population statistics are less than action levels, the difference between duplicate and real values is, ultimately, insignificant relative to free-release decisions).

2) Radiochemistry

Results from laboratory duplicates indicate adequate reproducibility based on duplicate results within statistical tolerance values ($>90\%$ confidence of equivalency between the original sample and the duplicate). Although blind duplicate samples were not acquired for determination of overall project precision, agreement between the multiple samples to within a range less than the $DCGL_w$ indicate that reproducibility is adequate for project decisions (i.e., relative to free-release of materials).

ACCURACY (and Bias)

1) Radiological Surveys

Accuracy of all radiological surveys is satisfactory based on implementation of protocols covering calibrations (at least annual) and periodic checks (at least daily). All instrumentation except the SCM/SIMS is controlled through (RFETS) site-specific procedures (e.g., RSPs), whereas the SCM/SIMS is controlled through the subcontractor's (Millennium Services Inc.) QAP and associated SOPs. Calibration and calibration check results were within the RFETS and industry-standard requirement of 20% of the applicable reference standard values. Full-scale, multi-point calibrations provided accuracies of $\pm 10\%$ prior to use of hand-held survey instruments in the project, consistent with guidelines put forth in ANSI-N323. All protocols that control instrumentation accuracy are included in the reference section, and may be referenced through the site document control system (site documents) or in the 779 Project File (Millennium QAP).

Key work-controlling procedures that contribute to accuracy (and representativeness) of the radiological surveys consist of the following:

- Kaiser-Hill, LLC., 1999. *Radiological Safety Practices*. RFETS, Golden, CO
- Millennium Services, Inc. 1999. *Quality Assurance Plan for Radiological Surveys at RFETS, 779 Cluster*.
- Ibid., 1999. SCM Procedure 008, *Conduct of Operations for Surveys using the SCM/SIMS*

- Ibid., 1999. SCM Procedure 005, *Requirements for the Completion of Surveys using the SCM*
- Ibid., 1999. SCM Procedure 006, *Performing a Position Calibration*
- Ibid., 1999. SCM Procedure 007, *Response Check of any Detector Configuration Installed on the SCM*
- Ibid. SCM Procedure 001, *Calibration and Field Confirmatory Tests of the Incremental Encoder included on the SCM*

Distance measurements recorded by the SCM/SIMS are within 3% of actual distances for mapping and location purposes, as documented in the "Incremental Encoder Calibration Verification Data Sheet."

Some bias may be indicated within control charts of the SCM (Attachment I), with runs of data below or above the reference standard value. However, given the overall low values of the data sets relative to the free-release criteria and the low probability of false negatives, the potential biases do not impact the ultimate project decisions of compliance with free-release criteria for the 7 survey units of interest for Administrative Area. Potential low biases in recount results – where recounts were performed with a hand-held instrument (Electra) following elevated counts (above action- or investigative-levels) by the SCM – have been concluded as insignificant, primarily based on the higher sensitivities of the hand-held instrumentation, where lower values would be expected if contamination was, in fact, absent. Comparability of these instruments, their results, and the role of measurement uncertainties in evaluating bias have been addressed in related documentation (Appendix 5 of the Building 729 Closeout Report).

2) Radiochemistry

Accuracies of radiochemical results were within tolerance and acceptable based on the associated results of LCS and calibrations at the lab. Preparation blanks also confirmed that no significant cross-contamination occurred in the analysis process. Uncertainties of the radiochemical results are quantified for each sample by 2-sigma (counting) error. Uncertainties associated with the alpha-spec analyses were within standard industry magnitudes and did not adversely impact project decisions.

REPRESENTATIVENESS

Samples and surveys are representative based on the following criteria:

- familiarity with facilities -- multiple walk-downs and collaborations by management and technical staff;
- implementation of industry-standard Chain-of-Custody protocols;
- compliance with sample preservation and hold times;
- documented and (site) approved methods:
 - radiochemistry - alpha spectrometry via K-H Module RC01-B.3 (4/24/98)
 - radiological surveys - K-H RSP 7.02
- compliance with the CRSP (RMRS, March 1999) -- reviewed & approved by technical and management consensus prior to implementation

110

COMPLETENESS

Data packages for all 7 Survey Units are complete with respect to Survey Package contents. The following table summarizes the minimum required number of samples or surveys and the actual quantity of samples or surveys.

611

Rad Measurement Type	Required # of Samples/ Surveys ⁽¹⁾	Actual # of Samples/ Surveys	Comments
Survey Unit 77914			
Shonka: SCM/SIMS (total)	100% areal coverage	100% areal coverage	DQO achieved
NE Electra (total) ²	40	40	DQO achieved
Eberline SAC-4 (removable) ²	40	40	DQO achieved
Radiochemical	NA	NA	NA
Survey Unit 77915			
Shonka: SCM/SIMS (total)	>10% areal coverage ³	>>10% areal coverage	DQO achieved
NE Electra (total) ²	13	17	DQO achieved
Eberline SAC-4 (removable) ²	13	17	DQO achieved
Radiochemical	NA	NA	NA
Survey Unit 77916			
Shonka: SCM/SIMS (total)	100% areal coverage	100% areal coverage	DQO achieved
NE Electra (total) ²	13	17	DQO achieved
Eberline SAC-4 (removable) ²	13	17	DQO achieved
Radiochemical	NA	NA	NA
Survey Unit 77917			
Shonka: SCM/SIMS (total)	>10% areal coverage ³	>>10% areal coverage ³	DQO achieved
NE Electra (total) ²	13	17	DQO achieved
Eberline SAC-4 (removable) ²	13	17	DQO achieved
Radiochemical	NA	NA	NA
Survey Unit 77918			
Shonka: SCM/SIMS (total)	>10% areal coverage ³	>>10% areal coverage ³	DQO achieved
NE Electra (total) ²	13	15	DQO achieved
Eberline SAC-4 (removable) ²	13	15	DQO achieved
Radiochemical	NA	NA	NA
Survey Unit 77920			
Shonka: SCM/SIMS (total)	>10% areal coverage ³	>>10% areal coverage ³	DQO achieved
NE Electra (total) ²	13	14	DQO achieved
Eberline SAC-4 (removable) ²	13	14	DQO achieved
Radiochemical	13	18	DQO achieved
Survey Unit 77909			
Shonka: SCM/SIMS (total)	>10% areal coverage ³	>>10% areal coverage ³	DQO achieved
NE Electra (total) ²	13	26	DQO achieved
Eberline SAC-4 (removable) ²	13	26	DQO achieved
Radiochemical	13	18	DQO achieved

(1) see "Summary Statistics Calculation Verification Worksheets." - refer to respective survey packages in 779 project files.

(2) also see data summaries for additional "Post-media" surveys, i.e., following paint scrapes

(3) MARSSIM guidelines are 10% to 100% for Class 2 interior units; Radiological Engineering professional judgement (stated in the CRSP) yielded ~100% coverage for floors and walls to 2m height; 10% of remaining room surface areas. Class 2 exterior survey units require minimum 50% lower walls, 10% upper walls/roof.

Consistent with EPA's G-4 DQO process, the sampling design was optimized through back-calculating actual measurement results (acquired during final status survey) and comparing model output with original estimates. Use of actual sample/survey (result) variances in MARSSIM's DQO model provided confirmation that an adequate number of samples/surveys had been acquired. Inputs required for decision-making, as stated in the original (planning) DQOs, were acquired, including coverage of originally-planned 3-dimensional boundaries of the structure. All radiological results are valid without qualification, and form data sets with adequate quantities and quality of data for free-release decisions on the seven survey units of interest.

COMPARABILITY

All results presented are comparable with radiological survey and radiochemistry data on a site- and DOE-complex wide basis. This comparability is based on:

- use of standardized engineering units in the reporting of measurement results
- consistent sensitivities of measurements at $\leq 50\%$ DCGL_W ($\leq 50\%$ DCGL_{EMC} for scans)
- use of site-approved procedures (RSPs)
- systematic quality controls
- thorough documentation of the planning, sampling/analysis process, and data reduction into formats designed for making decisions posed from the project's original data quality objectives.

SENSITIVITY

Adequate sensitivities, in units of dpm/100 cm², were attained for all surveys and radiochemical methods based on MDAs at approximately 50% of the transuranic DCGL_W (~50% DCGL_{EMC} for scans). The nominal MDAs for each survey and radiochemical method are summarized as follows:

- SCM/SIMS - scan surveys/total contamination: <160 dpm/100 cm²
- Surveys (Eberline SAC-4) - removable contamination: 10 dpm/100 cm²
- Surveys (NE Electra) - total contamination: 50 dpm/100 cm²
- Radiochemistry (alpha spec) - total contamination: <10 dpm/100 cm²

In summary, the data presented in this report have been verified and are qualified as valid and complete for comparison with free-release criteria (action levels) as stated in the original DQOs. All media sampled and surveyed, relative to both total and removable alpha activities, yielded results less than action levels for the associated contaminants of concern. Therefore, the Survey Units in question meet the free-release criteria with the confidences stated in this section and throughout the report.

4.0 QA ELEMENTS of DOE Order 414.1 and 10CFR830.120

Adequate implementation of the ten quality elements required by DOE Quality Assurance Order (414.1) was corroborated through the verification and validation process described above. The ten DOE quality elements, or criteria, are inherent within the MARSSIM guidance, as DOE was a co-authoring organization to the MARSSIM. Quality elements deserving emphasis include qualifications of project personnel and additional controls in the areas of engineering design and computer software.

All personnel performing quality-affecting activities within the FSS project were qualified to perform their specific tasks. Suitable **training and qualification** documentation for personnel performing the work, from the laborers to technical professionals to management, is documented in several ways. T&Q status for personnel is included in the *Building 779 Cluster Closure Project Health & Safety Plan* (Rev. 6, 18 August 1998) and personnel dossiers controlled by company-specific Human Resource departments.

Software quality control for the SCM/SIMS is chronologically documented and archived within the QA/QC folder (for Millennium Services) of the Project File. Software used to reduce data from radiochemical sampling and hand-held instrumentation was modified to record verifications and any alterations to calculations following V&V of the calculations. Details of the verification process were also improved through use of a checklist, which was completed for each Survey Unit Data Summary

[illegible]

ATTACHMENT K
Sample/Survey Measurement Location Maps

RADIOLOGICAL CLOSEOUT SURVEY FOR THE 779 CLUSTER

Survey Area: H

Survey Unit: 77909

Classification: 2

Building: 779




Survey Unit Description: B779 Exterior Walls, Roof & Exhaust Duct Tower (Admin Bldg & Exh. Duct Tower)

Total Floor Area: 662 sq. m

Total Area: 2004 sq. m

Grid Size: 11m x 11m

SURVEY UNIT 77909-MAP 1 OF 2

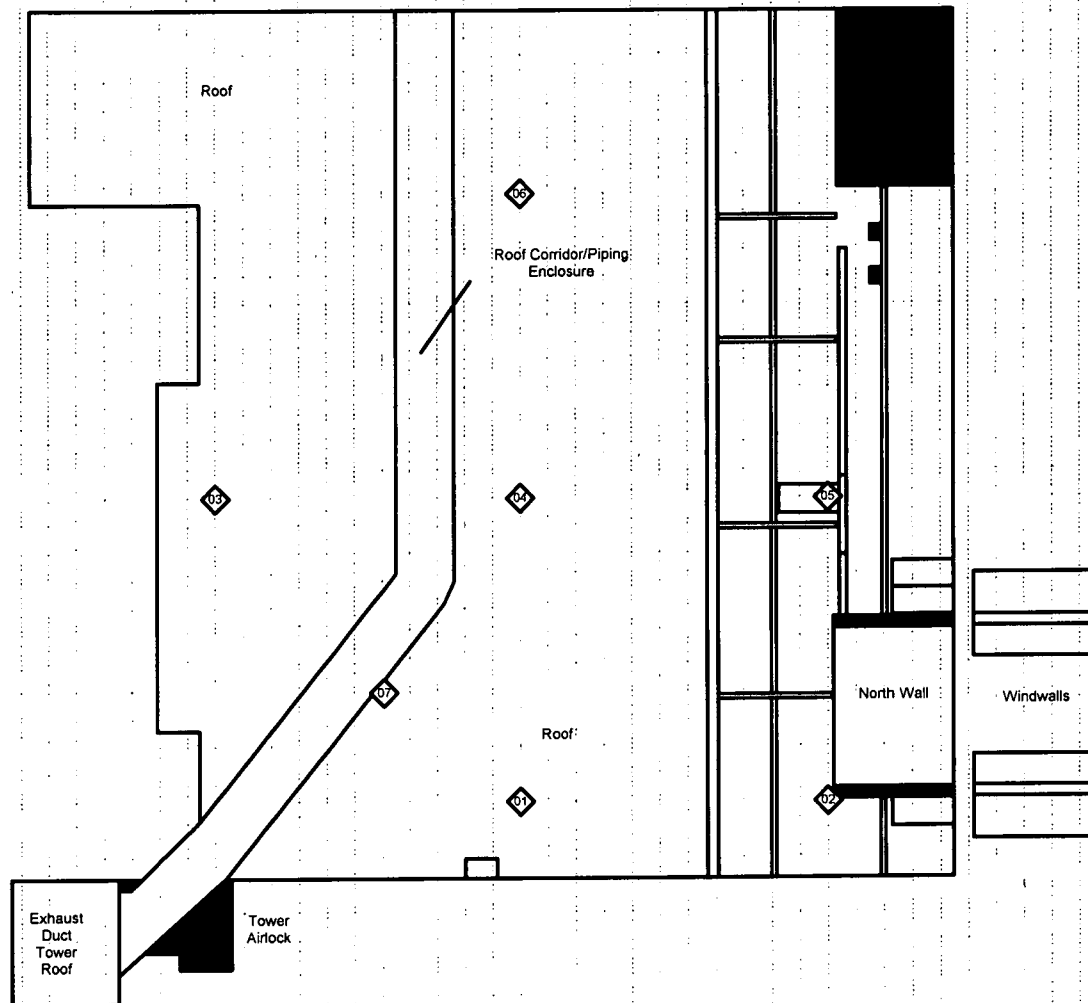

Attachment K


Page 1 of 13

117

RADIOLOGICAL CLOSEOUT SURVEY FOR THE 779 CLUSTER

Survey Area: H Survey Unit: 77909 Classification: 2
 Building: 779
 Survey Unit Description: B779 Exterior Walls, Roof & Exhaust Duct Tower (Admin Bldg & Exh. Duct Tower)
 Total Floor Area: 662 sq. m Total Area: 2004 sq. m Grid Size: 11m x 11m

SURVEY UNIT 77909-MAP 2 OF 2

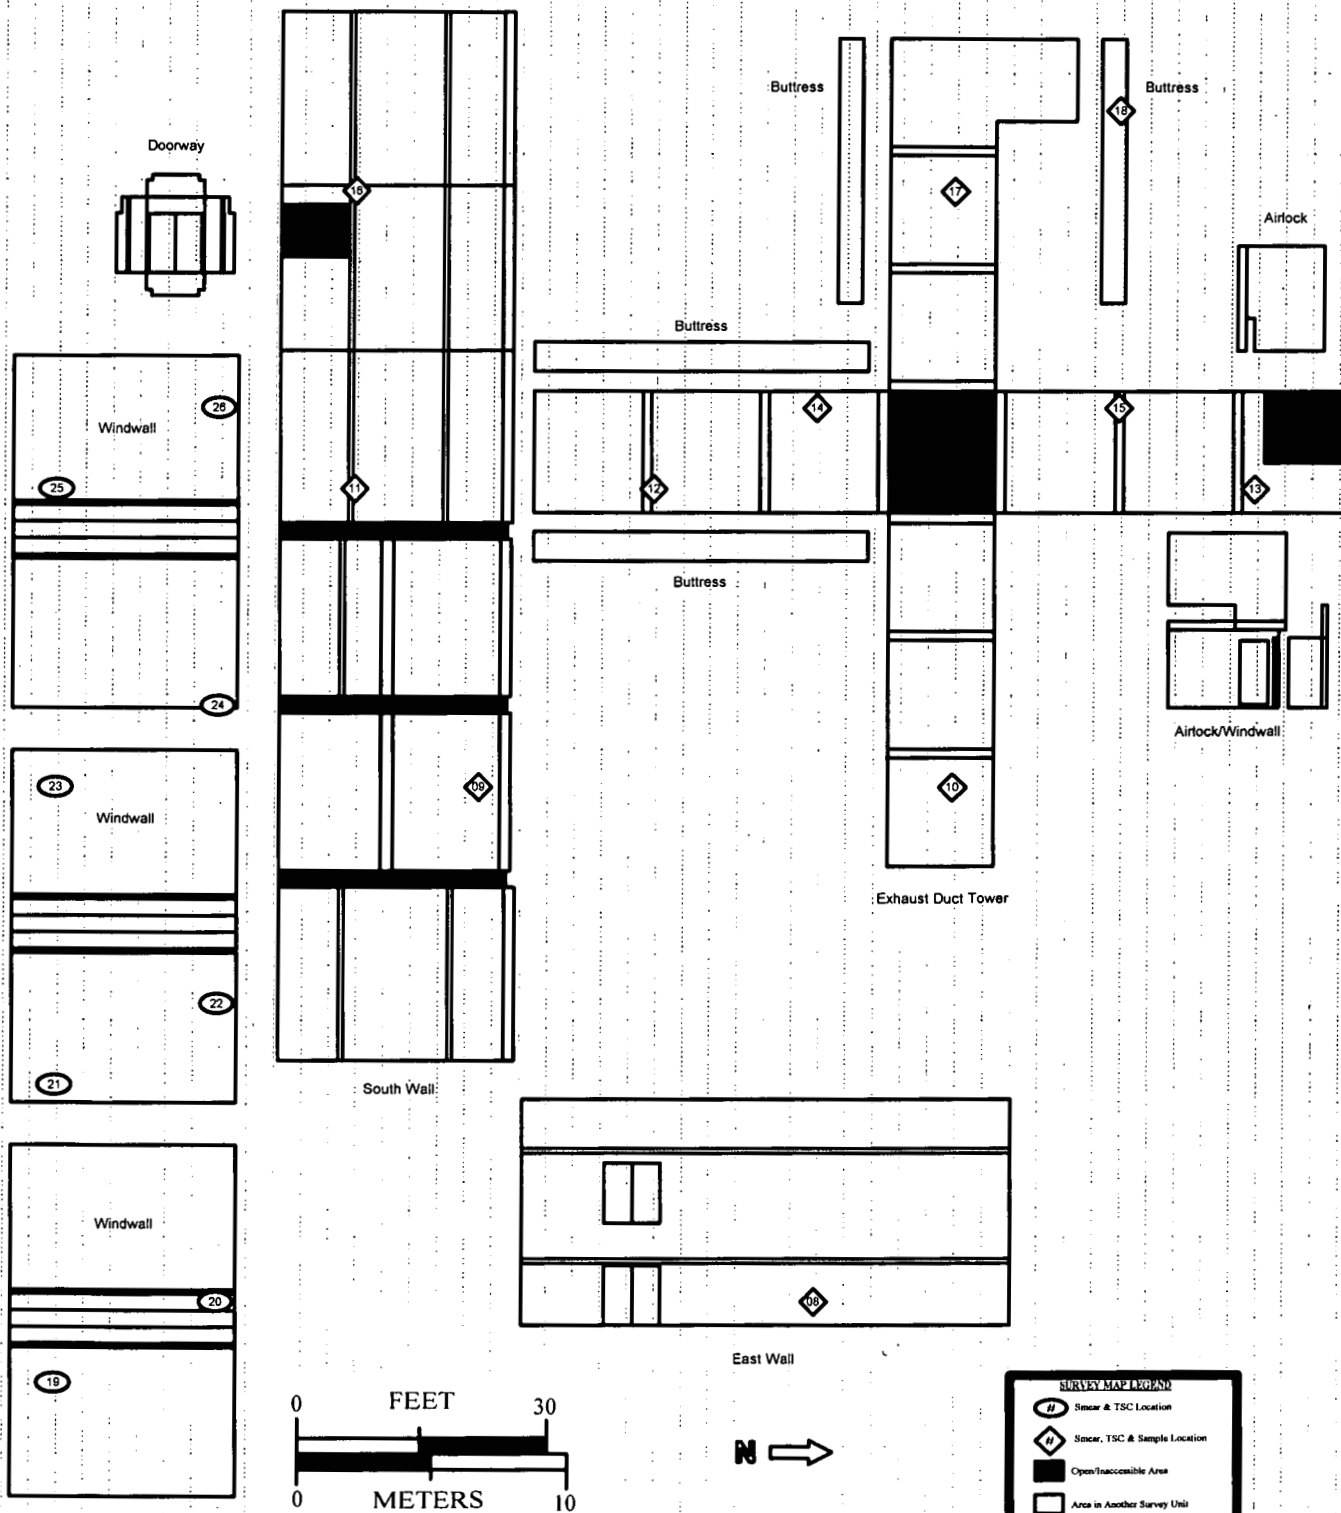




RADIOLOGICAL CLOSEOUT SURVEY FOR THE 779 CLUSTER

Survey Area: D Survey Unit: 77914 Classification: 1
Building: 779
Survey Unit Description: B779 Admin Area Hallway (1st and 2nd Floor)
Total Floor Area: 173 sq. m Grid Size: 2.0m x 2.0m

SURVEY UNIT 77914 - MAP 1 OF 1

1st Floor Hallway

Second Floor Hallway

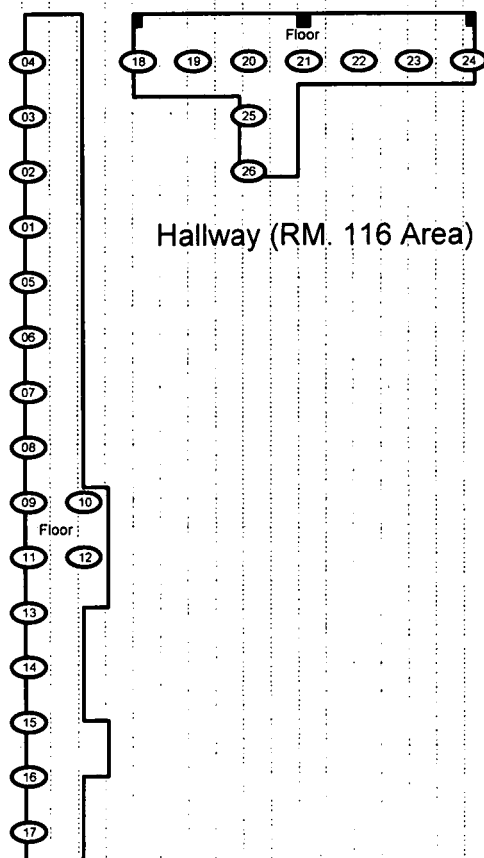

Attachment K


Page 3 of 13

RADIOLOGICAL CLOSEOUT SURVEY FOR THE 779 CLUSTER


Survey Area: C Survey Unit: 77915 Classification: 3
 Building: 779
 Survey Unit Description: B779 Second Floor Admin Area
 Total Area: 2834 sq. m

SURVEY UNIT 77915 - MAP 1 OF 4




Rooms 202, 202A,
 203, 204, 204A &
 204B

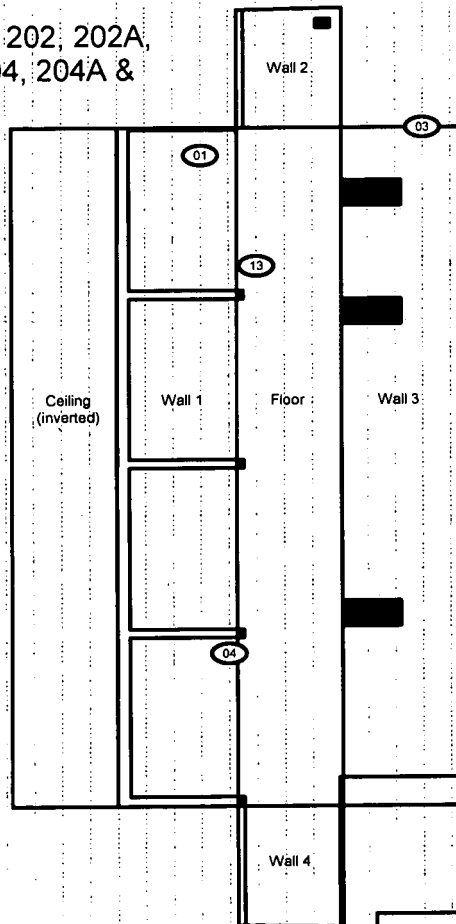

Hallway

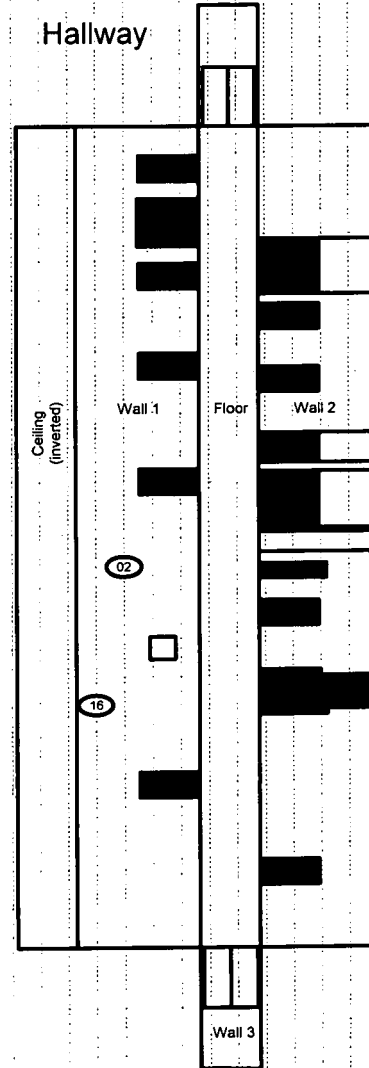




Stairwell to First Floor
 Room 101

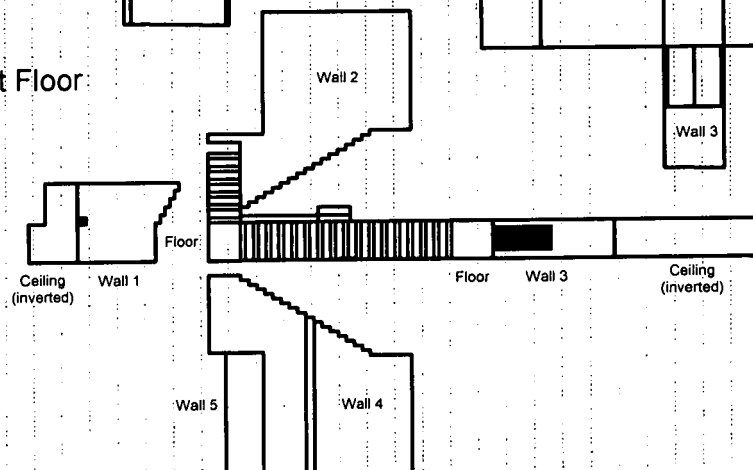

RADIOLOGICAL CLOSEOUT SURVEY FOR THE 779 CLUSTER

Survey Area: C Survey Unit: 77915 Classification: 3
 Building: 779
 Survey Unit Description: B779 Second Floor Admin Area
 Total Area: 2834 sq. m

SURVEY UNIT 77915 - MAP 2 OF 4

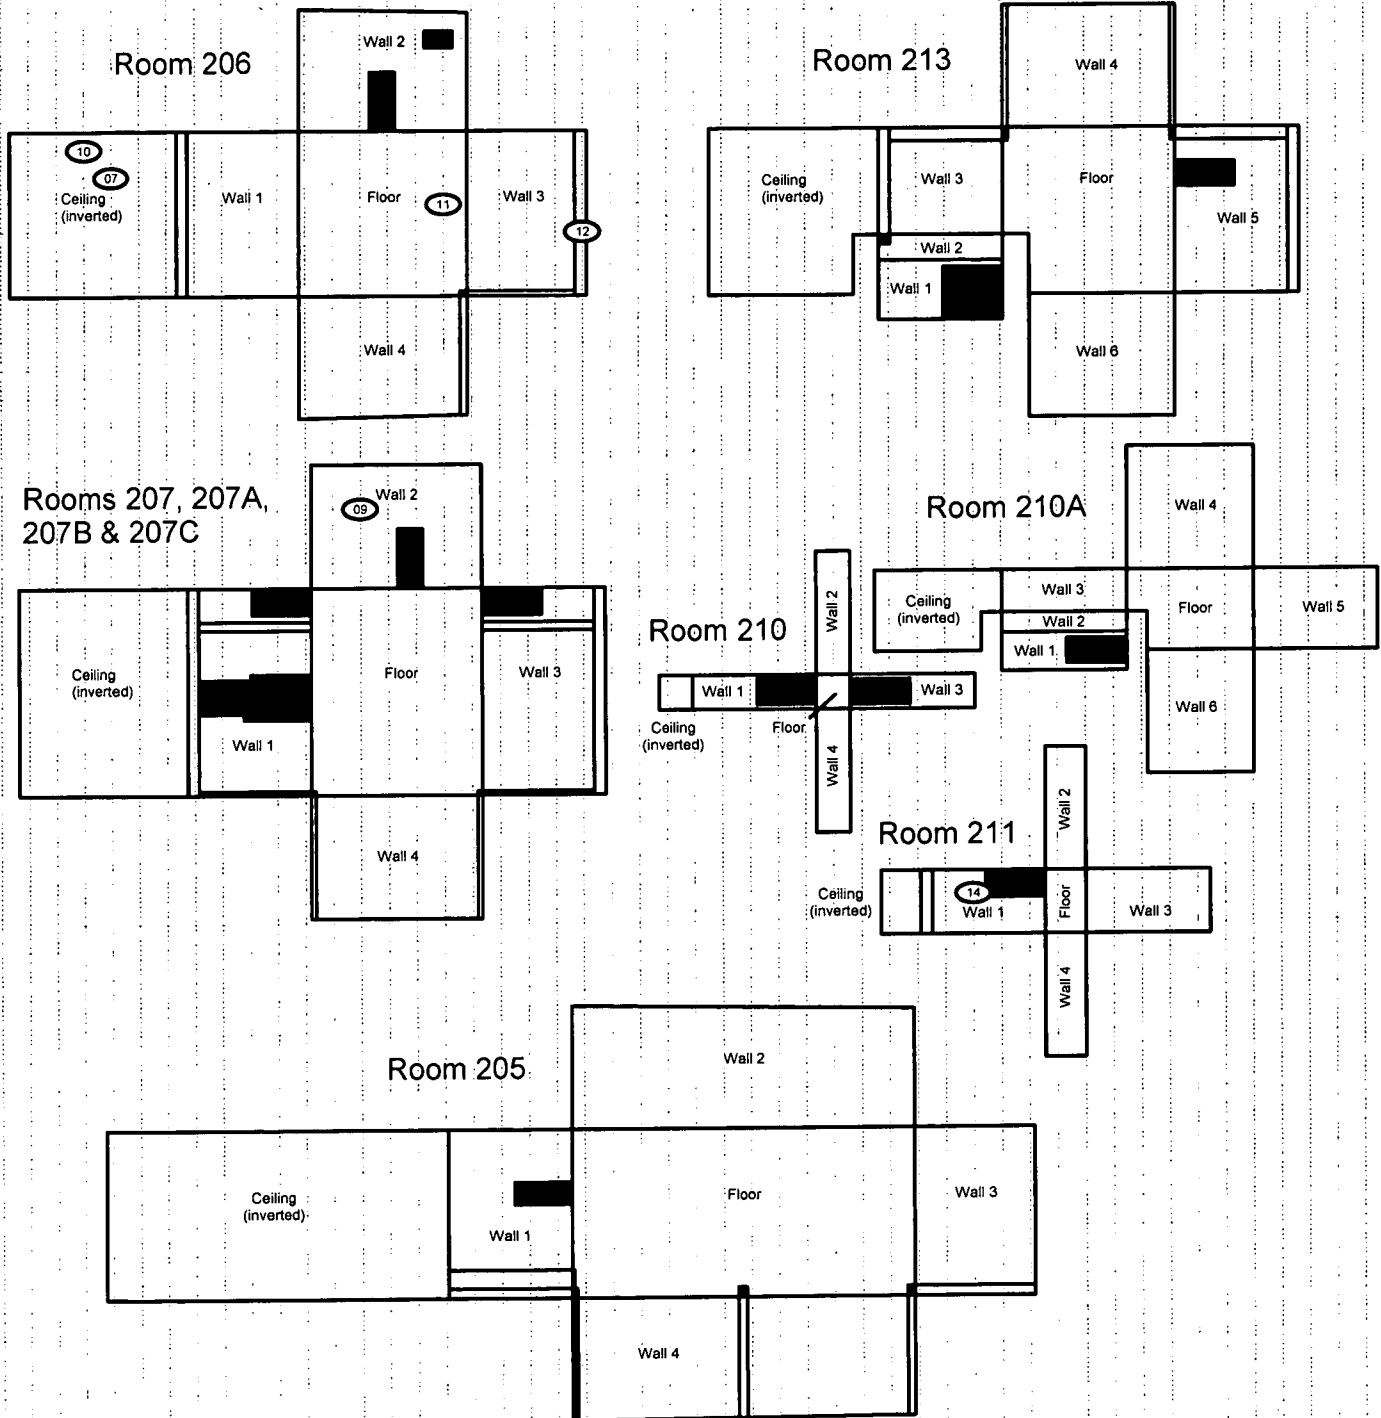


RADIOLOGICAL CLOSEOUT SURVEY FOR THE 779 CLUSTER


Survey Area: C Survey Unit: 77915 Classification: 3
 Building: 779
 Survey Unit Description: B779 Second Floor Admin Area
 Total Area: 2834 sq. m

SURVEY UNIT 77915 - MAP 3 OF 4


Room 212

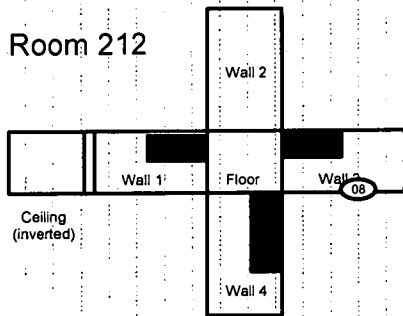


Room 212A

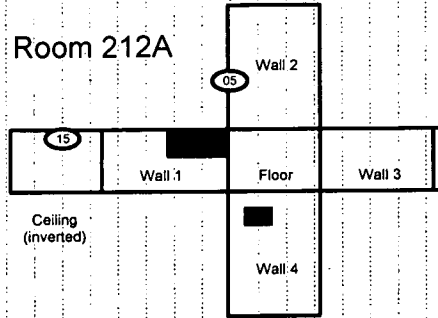


Room 208

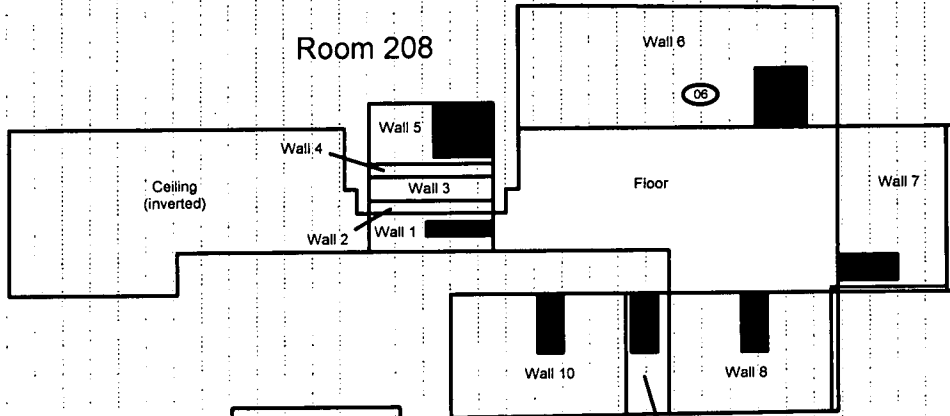




Room 209

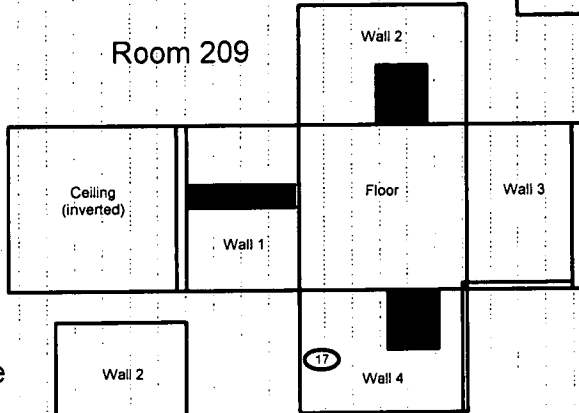

Room 209
Pipe Chase



Room 214

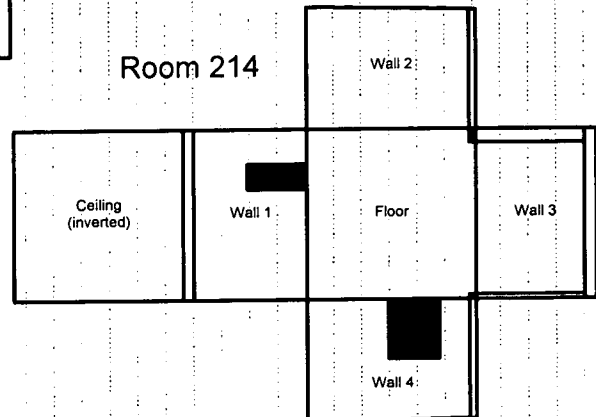

Attachment K

Page 6 of 13



122

RADIOLOGICAL CLOSEOUT SURVEY FOR THE 779 CLUSTER

Survey Area: C Survey Unit: 77915 Classification: 3
Building: 779
Survey Unit Description: B779 Second Floor Admin Area
Total Area: 2834 sq. m

SURVEY UNIT 77915 - MAP 4 OF 4

Rooms 201,
201A & 201B

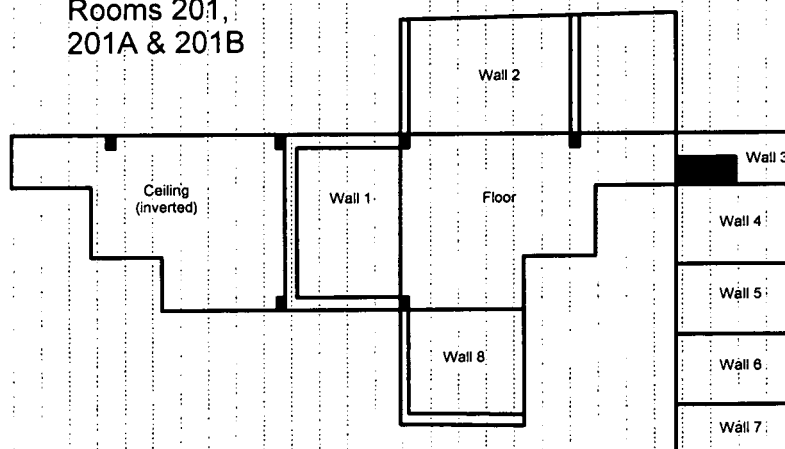




Attachment K

Page 7 of 13

RADIOLOGICAL CLOSEOUT SURVEY FOR THE 779 CLUSTER

Survey Area: C Survey Unit: 77916 Classification: 1
 Building: 779
 Survey Unit Description: B779 Second Floor Admin Area, Room 208 Floor
 Total Area: 61 sq. m Total Area: 61 sq. m Grid Size: 2 m x 2 m

SURVEY UNIT 77916 - MAP 1 OF 1

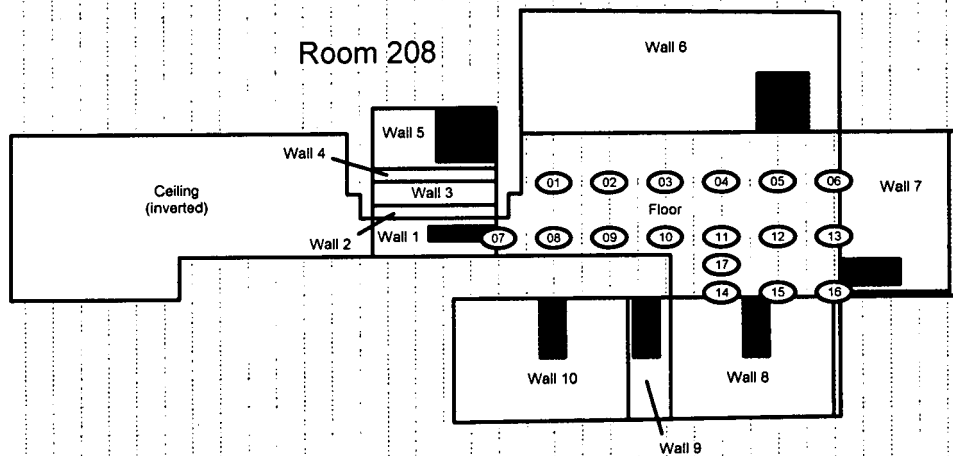

RADIOLOGICAL CLOSEOUT SURVEY FOR THE 779 CLUSTER

Survey Area: D

Survey Unit: 77917

Classification: 3


Building: 779

Survey Unit Description: B779 First Floor Office Areas (Rooms & Hallway)


Total Area: 1035 sq. m

SURVEY UNIT 77917 - MAP 1 OF 2


Rooms 106, 107, 108
109 & 110

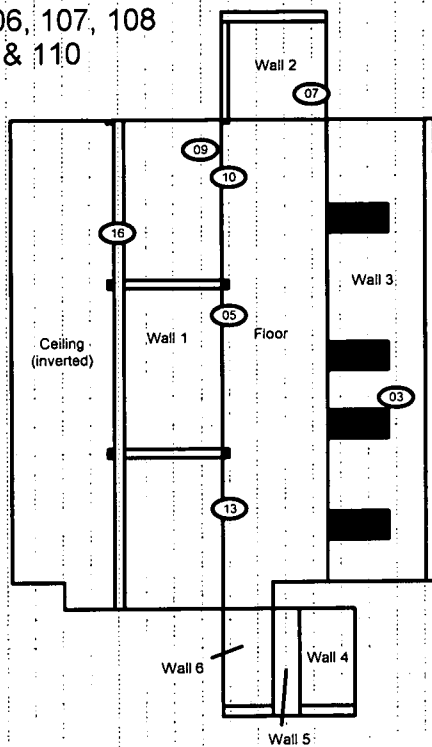




Rooms
110A & 111

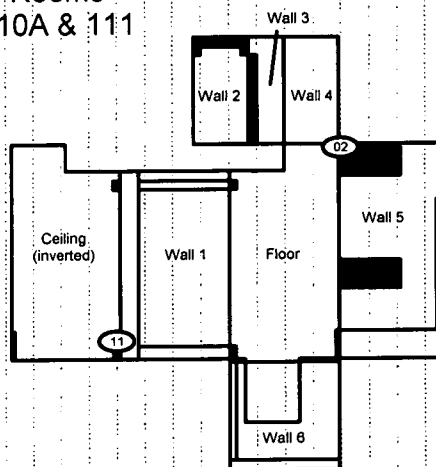

Room 105

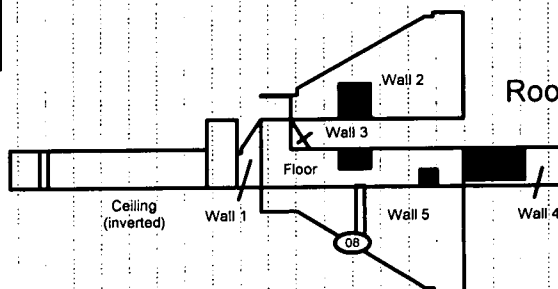

Room 113

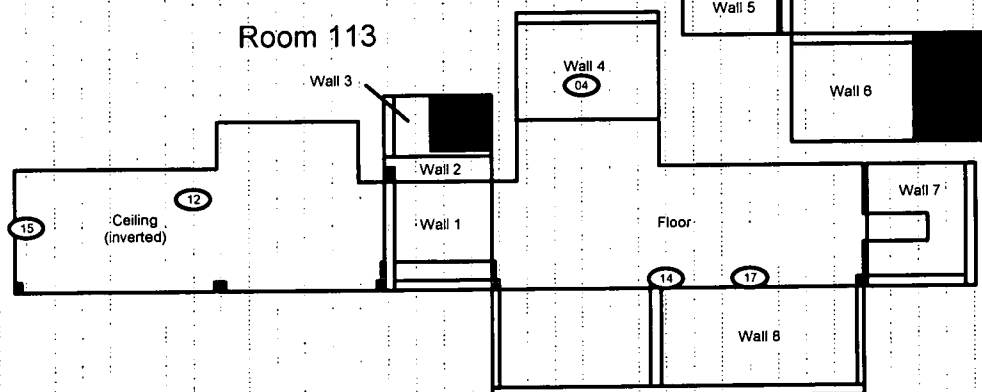

Attachment K

Page 9 of 13

RADIOLOGICAL CLOSEOUT SURVEY FOR THE 779 CLUSTER

Survey Area: D

Survey Unit: 77917




Classification: 3

Building: 779

Survey Unit Description: B779 First Floor Office Areas (Rooms & Hallway)

Total Area: 1035 sq. m

SURVEY UNIT 77917 - MAP 2 OF 2

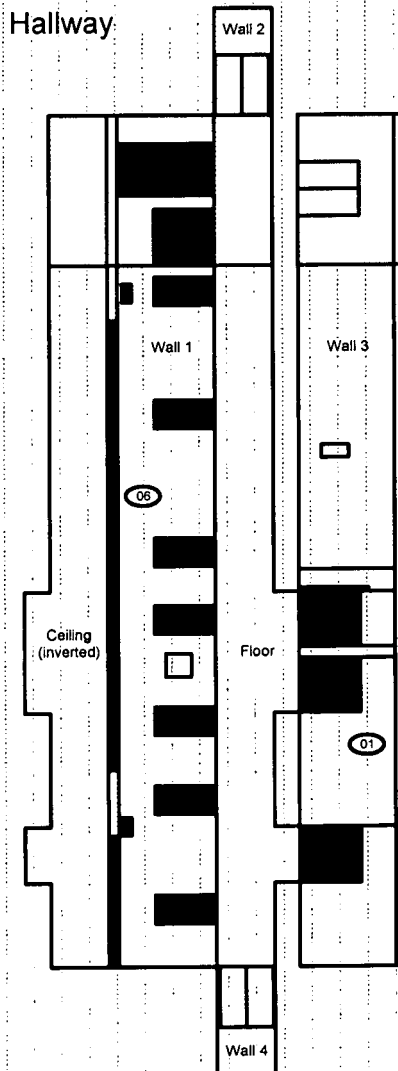

Attachment K

Page 10 of 13

RADIOLOGICAL CLOSEOUT SURVEY FOR THE 779 CLUSTER

Survey Area: D

Survey Unit: 77918


Classification: 3

Building: 779

Survey Unit Description: B779 First Floor Admin Areas (Rooms 100, 101, 101A, 104, 116, 116A, 116B & 117)

Total Area: 839 sq. m

SURVEY UNIT 77918 - MAP 1 OF 2

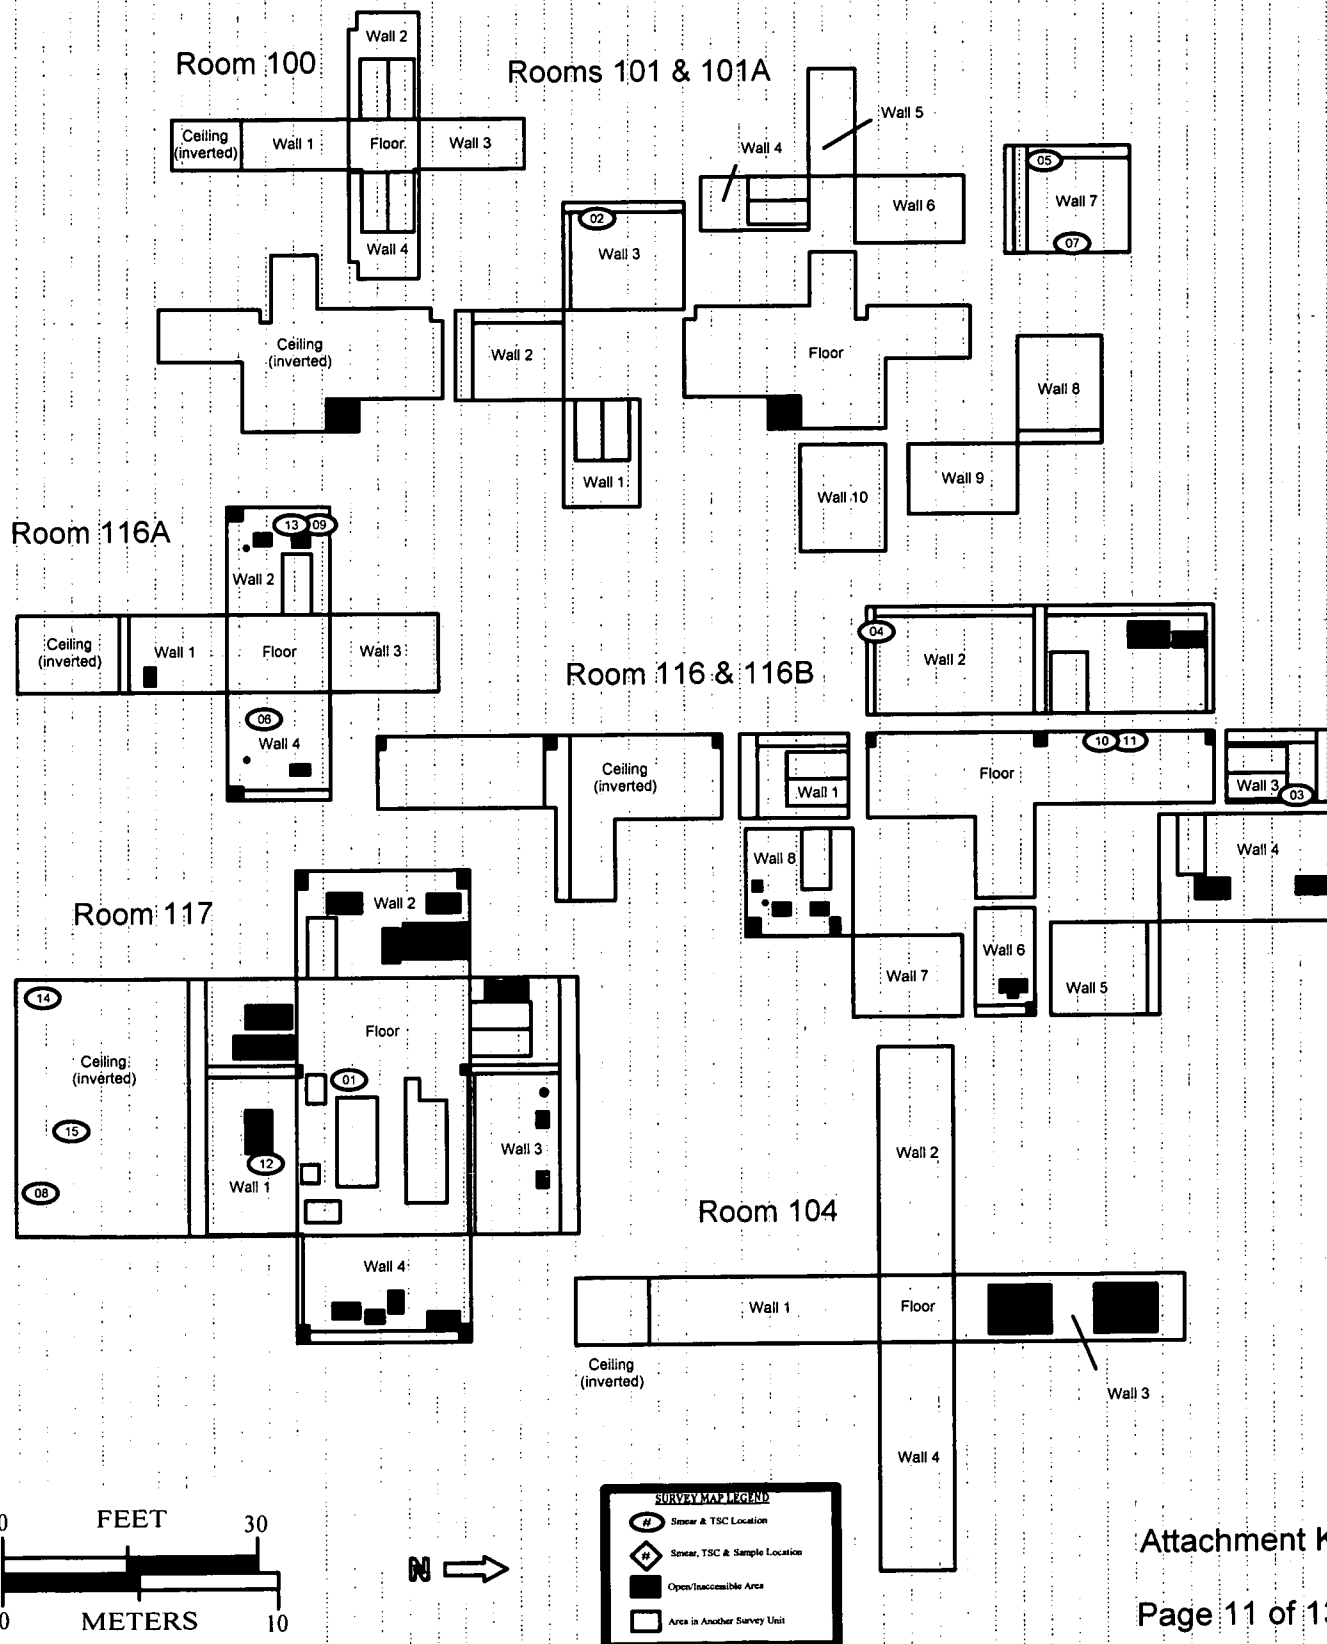

Attachment K

Page 11 of 13

RADIOLOGICAL CLOSEOUT SURVEY FOR THE 779 CLUSTER

Survey Area: D

Survey Unit: 77918




Classification: 3

Building: 779

Survey Unit Description: B779 First Floor Admin Areas (Rooms 100, 101, 101A, 104, 116, 116A, 116B & 117)

Total Area: 839 sq. m

SURVEY UNIT 77918 - MAP 2 OF 2

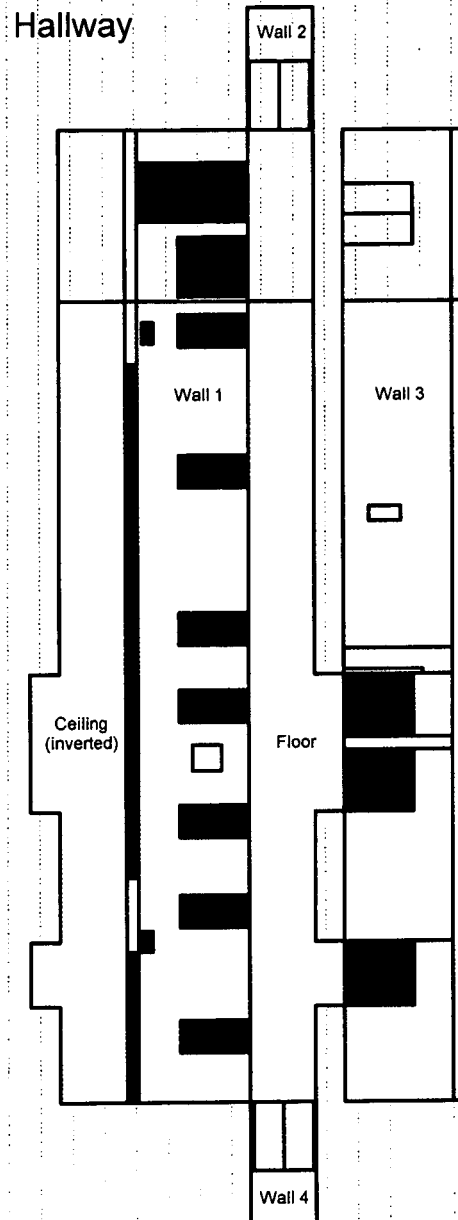


Attachment K

Page 12 of 13

RADIOLOGICAL CLOSEOUT SURVEY FOR THE 779 CLUSTER

Survey Area: D Survey Unit: 77920 Classification: 2
 Building: 779
 Survey Unit Description: B779 Rooms 114, 115, 115A & Exhaust Duct Tower (Interior)
 Total Floor Area: 214 sq. m Total Area: 963 sq. m Grid Size: 7m x 7m

SURVEY UNIT 77920-MAP 1 OF 1

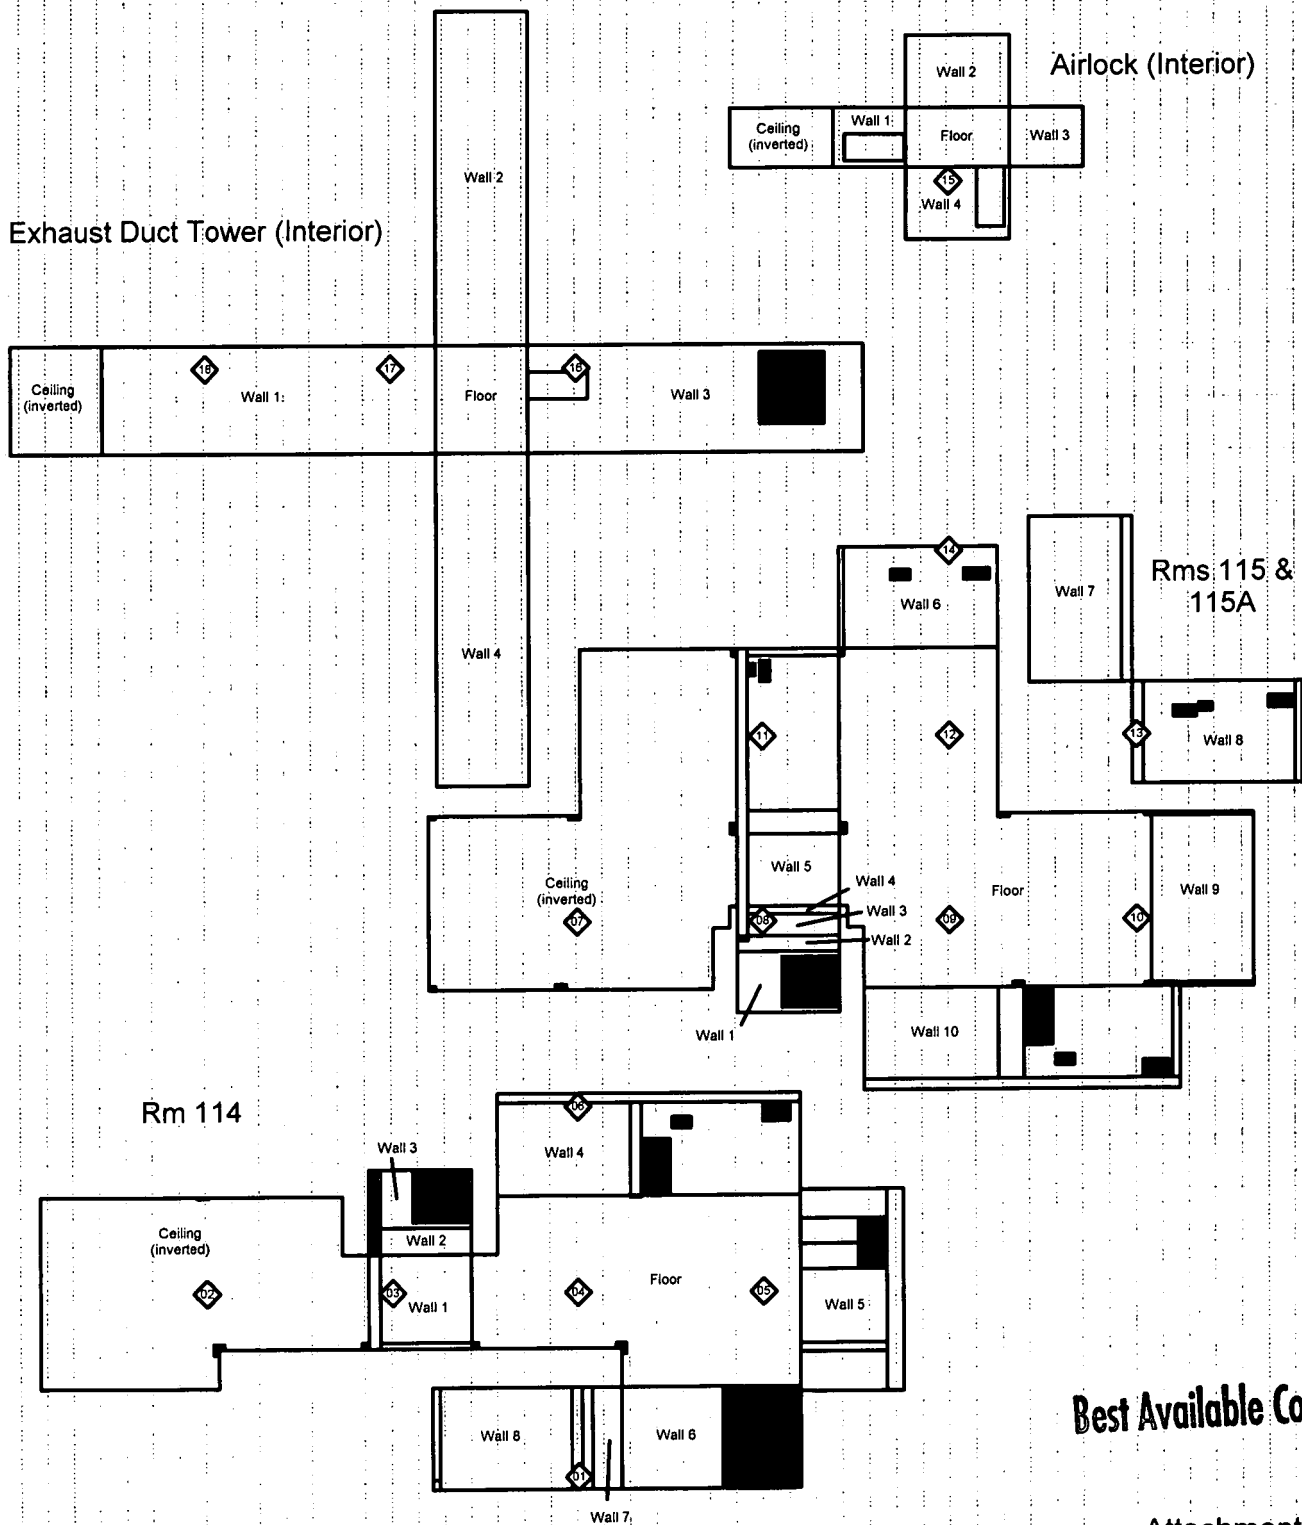

Best Available Copy

Attachment K

Page 13 of 13

0 FEET 30
 0 METERS 10

129 / 129
