



## Type I Facility Closeout Report

<b>Section A Facility Data</b>	
Facility No	Trailer T119B
Facility Descriptor	Office Trailer
Project	RISS
Date of Demolition	3/24/04
Additional Information	Attached
<i>(Must include information on environmental releases and conditions of site at turnover to Environmental Restoration)</i>	
<b>Section B Final Characterization Data</b>	
Reconnaissance Level Characterization Report <i>(concurrency received)</i>	RLCR for Trailer T119B - Concurrence Steven H Gundersen to Joseph A Legare dated July 18 2003
In-process Characterization	N/A
Pre-Demolition Survey Report <i>(approval received)</i>	RLC functioned as PDS
Post-Demolition Survey Report <i>(as necessary)</i>	N/A
<b>Section C Waste Data (complete categories as appropriate)</b>	
<u>Soil and Debris Disposal</u>	
Disposal Site	BFI Foothills Hwy 93 Landfill
Waste Volume (m <sup>3</sup> )	3120 m <sup>3</sup>
Waste Weight (tons)	2205 tons
Additional Information	Wastes included trailer structure, windbreakers, small shed, concrete anchors, concrete block, asphalt from driveways and parking areas (including the Helicopter Pad), concrete from sidewalks, bollards, posts, concrete from pads.
<u>TSCA Waste Disposal (other than ACM)</u>	
Disposal Site	BFI Foothills Hwy 93 Landfill
Waste Volume (m <sup>3</sup> )	< 1m <sup>3</sup>
Additional Information	PCB ballasts (< 9 lbs and not leaking) were sent to the landfill as PCB Bulk Product Waste co-mingled with building debris.
<u>Asbestos Waste Disposal</u>	
Disposal Site	N/A
Additional Information	No asbestos was generated.
<u>Low Level Waste Disposal</u>	
Disposal Site	N/A
Additional Information	No LLW was generated.
<u>Low Level Mixed Waste Disposal</u>	
Disposal Site	N/A
Additional Information	No LLMW was generated.
<u>Recycled Material</u>	
Waste Volume (lbs)	Freon R-12, R-22 and R134A 99 lbs
Additional Information	Freon transferred to PU&D for offsite resale/reuse.
<u>Property Disposition</u>	
Receiver Locations (major items only)	N/A
Additional Information	PU&D removed miscellaneous office furniture suitable for resale.


  
 Date: 5/3/04



ADMIN RECORD

IA-A-002146

1/5

### Historical Information

Trailer T119B was historically used as a general office trailer by Site security personnel. The trailer has no history of radiological or hazardous operations.

Dates and duration of specific activities are shown below:

CDPH/RRC concurrence January 10, 2003  
Demolition permit application to CDPHE/Asbestos Unit March 15, 2004  
CDPHL demolition approval notice March 25, 2004  
Demolition start date March 29, 2004  
Demolition completion date April 8, 2004

### Building Characterization

Reconnaissance Level Characterization (RLC) was performed to enable facility Typing (as per the DPP (10/8/98)) and compliant disposition and waste management of the Area 5, Group 3 (i.e., Buildings 119, T119B, 121, 122S, T124A, 127 and 128). Because T119B was anticipated Type 1 facility, the characterization was performed in accordance with the Pre-Demolition Survey Plan (MAN 127 PDSP) requirements. All facility surfaces were characterized and the data reported in the RLC report, including the interior and exterior surfaces (i.e., floor, walls, ceiling, and roof).

RLC encompassed both radiological and chemical characterization to enable compliant disposition and waste management pursuant to the D&D characterization protocol (MAN 77-DDCP). The characterization was built upon physical, chemical, and radiological hazards identified in the facility-specific Historical Site Assessment report.

Results indicate no radiological contamination exists in excess of the PDSP unrestricted release limits of DOE Order 5400.5. All beryllium sample results were less than  $0.1 \mu\text{g}/100\text{cm}^2$ . As part of the RLC, a visual and tactile survey of building materials suspected of containing asbestos was conducted in Trailer T119B. Building materials suspected of containing asbestos were not identified; therefore, no bulk sampling was performed in this facility as part of the RLC. All construction debris was free released and disposed of as sanitary waste.

### Physical Description

Trailer T119B was a 15,400 square-foot general office trailer and was acquired in 1991. This modular trailer was approximately 120-feet wide by 130 feet long. T119B had corrugated metal siding with corrugated metal skirting. The entrances have wooden stairs leading to a wooded enclosure.

The interior was primarily a cubical layout, but had several hard-walled offices, conference rooms, and restrooms. Interior walls were wallboard, the ceiling was a drop ceiling with acoustical tiles and recessed lights. The floor was primarily covered with carpet except in the restrooms and dock entranceways, which were covered with vinyl tile.

Building T119B had the following utilities: electric, plant water, plant sanitary, and fire protection (provided by an overhead sprinkler system) and wall-mounted fire extinguishers.

### Description of Site Condition at the End of Decommissioning

D&D of the trailer consisted of the demolition of the structure, HVAC system, electrical conduit, lighting, sprinkler system, and ductwork systems. RCRA components (i.e., fluorescent tubes, sodium vapor bulbs, incandescent bulbs, mercury switches, sealed lead acid batteries, Freon, electronic equipment, and circuit boards) were segregated from non-hazardous materials and removed prior to demolition.

Environmental media beneath and surrounding the facility was not within the scope of this Project and will be addressed at a future date under the scope of the LR RSOP, if required. However no remedial action is planned. The asphalt parking lots (including the Helicopter Pad) and driveways around the Trailer 119B were removed. The concrete pads at the entrances to the trailer and the trailer concrete tie-downs and crissons were removed. All trailer debris was removed.

The plant water lines for potable water and fire protection were gapped at the mains. The domestic and fire water lines under the trailer were ungapped at grade. The remaining water lines between the mains and the trailer were abandoned. Fire hydrant 1-19 was removed and abandoned to 4 feet below final grade. The sanitary sewer line was flushed and MH 21 was left open, however this manhole will be abandoned and plugged as part of the sanitary sewer system closure (B995). Electric service was provided through underground cables that were removed with the transformer and switchgear (west side of the building). Conduit for the telephone and local area network were stripped of wires and the conduit abandoned 3 feet below grade. The attached map shows the approximate utility disconnect locations. There are no UBC concerns, and no further work remains other than establishing the final grade. There are no UBC concerns and no further work remains other than backfilling, establishing the final grade and revegetation.

#### **Additional Information**


Listed below are the databases that provide the administrative controls for waste package and area information, chemical management, storage tank management, and RIIS environmental compliance tracking. Applicable databases were updated to reflect the status of the building at the time of demolition/removal.

- Waste and Environmental Management System (WEMS)
- Chemical Tracking System (CTS)
- Tank Management System and
- Environmental Compliance Action Tracking System (ECATS)

4

# T1198 & B119 Utility Disconnections

SANITARY SEWER TO BE PLUGGED AT MANHOLE (SCHEDULE TBD)

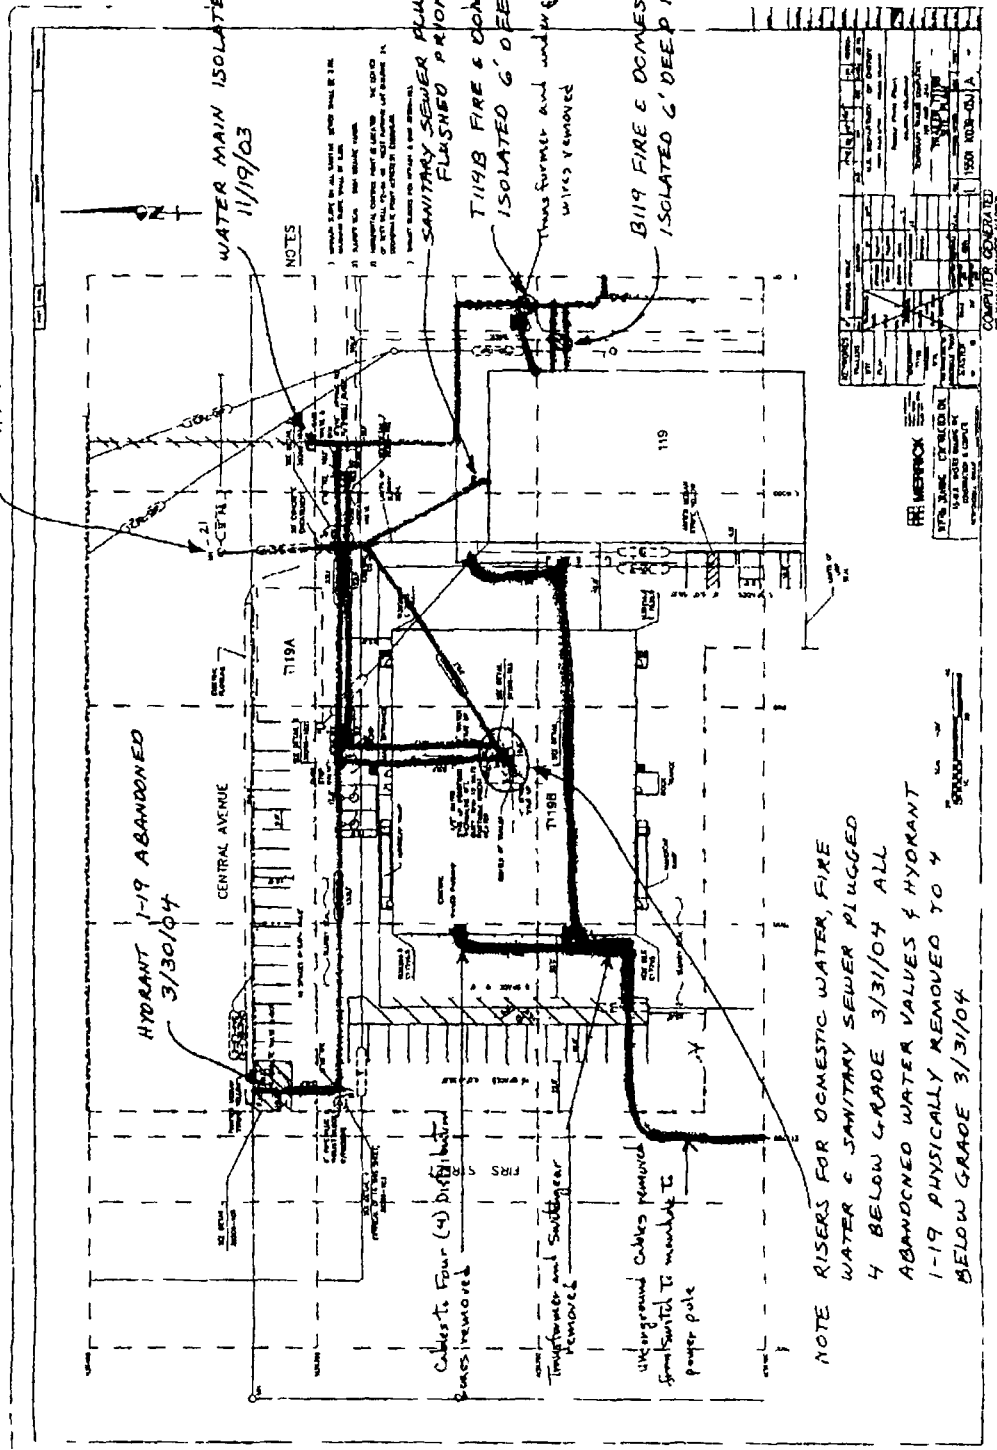

NOTE RISERS FOR DOMESTIC WATER, FIRE WATER & SANITARY SEWER PLUGGED 4' BELOW GRADE 3/31/04 ALL ABANDONED WATER VALVES & HYDRANT 1-19 PHYSICALLY REMOVED TO 4' BELOW GRADE 3/31/04

B119 Utility Disconnections

KEY

1 = POTABLE WATER  
2 = SANITARY SEWER  
3 = ELECTRICAL

Best Available Copy

**CTRL04-00508**

---

<b>Ticket Type</b> Incoming	<b>File Code</b> 5400	<b>Status</b> N/A
<b>Task</b> FYI	<b>Due Date.</b>	<b>Priority</b> Normal
<b>Task Desc</b>		
<b>Congressional</b> No	<b>UCNI.</b> No	

---

<b>Addressee:</b> Gary Morgan	<b>Doc Date</b> 5/6/2004	
<b>From</b> Frank E Gibbs	<b>Rec Date</b> 5/13/2004	<b>Ref No</b> 04-RF-00516
<b>Title:</b> Deputy Project Manager, Remediation, Industrial D&D, and Site Services		
<b>CC.</b> Joseph Legare		
<b>Subject.</b> TRANSMITTAL OF CLOSE-OUT REPORT FOR B119 WSLLC FITNESS CENTER AND T119B OFFICE TRAILER - FEG-015-04		
<b>Agency</b> Kaiser-Hill Company, LLC		

---

<b>Responsible:</b> Morgan, Gary	<b>Direct Report:</b> Morgan, GaryDR	<b>Signed By.</b>
<b>Org</b> CADRE	<b>Div</b> CADRE	
<b>Comments.</b>		
<b>Additional Notifications</b> Legare, Joe		
<b>Response Readers</b>		

---

5/5
