

Revised 12/04

CORRES. CONTROL  
INCOMING LTR NO.

00011 RFQS

DUE DATE

ACTION



RECEIVED

2005 JAN 12 P 3:53

Department of Energy

CORRESPONDENCE

ROCKY FLATS PROJECT OFFICE

10808 HIGHWAY 93, UNIT A

GOLDEN, COLORADO 80403-8200

JAN 03 2005

04-DOE-00987

DIST.	LTR	ENC
BERARDINI, J.H.	X	X
BOGNAR, E.S.	X	X
BROOKS, L.	X	X
CARPENTER, M.	X	X
CIUCCI, J.A.		
CROCKETT, G.A.		
DECK, C.A.	X	X
DEGENHART, K.R.	X	X
DEL VECCHIO, D.		
DIETER, T.J.		
FERRERA, D.W.	X	X
GIACOMINI, J.J.		
LINDSAY, D.C.		
LONG, J.W.		
LYLE, J.L.		
MARTINEZ, L.A.	X	X
NAGEL, R.E.	X	X
NESTA, S.	X	X
NORTH, K.	X	X
SHELTON, D.C.	X	X
SPEARS, M.S.	X	X
TUOR, N.R.	X	X
WIEMELT, K.	X	X
WILLIAMS, J.L.		
ZAHM, C.	X	X

Freiboth, C. X X

Mr. Steven H. Gunderson

Rocky Flats Cleanup Agreement Project Coordinator

Colorado Department of Public Health and Environment

4300 Cherry Creek Drive South

Denver, Colorado 80246-1530

Dear Mr. Gunderson:

Please find enclosed a completed Rocky Flats Cleanup Agreement Type 1 Building Disposition Closeout Report provided for your information for Building 564 - Office Building.

Questions may be directed to Gary Morgan, Rocky Flats Project Office, at (303) 966-6003.

Sincerely,

Joseph A. Legare, Director  
RFPO Project Management

Enclosure

cc w/o Encl.:

S. Nesta, K-H RISS Env

C. Freiboth, K-H RISS D&D

K. Wiemelt, K-H RISS D&D

M. Aguilar, USEPA

D. Abelson, RFCLOG

cc w/ Encl:

G. Morgan, RFPM, RFPO

D. McCranie, HQCPM, RFPO

Administrative Record

COR. CONTROL	X	X
ADMIN. RECORD	X	X
PATS/130		

Reviewed for Addressee  
Corres. Control RFP

1-12-05  
Date


By

Ref. Ltr. #

042F01297

DOE ORDER #

5400.1



ADMIN RECORD

B559-A-000034



December 22, 2004

04-RF-01297

Gary Morgan, Functional Lead  
Cadre Project Management Division  
DOE, RFPO

TRANSMITTAL OF CLOSE OUT REPORT FOR B564 OFFICE BUILDING-- FEG-048-04

Attached is the Closeout Report for the Type 1 facility Building 564 Office Building. Please note that a copy of the report has been submitted to the CERCLA AR by the Kaiser-Hill RISS project.

Please contact Steve Nesta x6386 with questions or concerns.

Frank E. Gibbs  
Deputy Project Manager  
Remediation, Industrial D&D, and Site Services

Attachment:  
As Stated

SMN:pvt


Orig. and 1 cc – Gary Morgan

cc:  
Joseph Legare

<b>Section A. Facility Data</b>	
Facility No.	564
Facility Descriptor:	Office Building
Project:	RISS 559 Project
Date of Demolition:	11-16-04
Additional Information:	This was a type 1 single story, 3000 sq. ft. steel office building on slab. Building was located south of building 561.
<i>(Must include information on environmental releases and conditions of site at turnover to Environmental Restoration)</i>	

<b>Section B. Final Characterization Data</b>	
Reconnaissance Level Characterization Report	1-9-02
<i>(concurrence received)</i>	
In-process Characterization	
Pre-Demolition Survey Report <i>(approval received)</i>	Type 1
Post-Demolition Survey Report <i>(as necessary)</i>	

<b>Section C. Waste Data <i>(complete categories as appropriate)</i></b>	
<u>Sanitary Disposal</u>	
Disposal Site:	Demo debris (concrete and metal) BFI Foothills Highway 93
Waste Volume:	820 cubic yards
Waste Weight (tons):	285.72 tons
Additional Information:	Dates shipped 11/16/04 and 11/17/04
<u>Hazardous Disposal</u>	
Disposal Site:	
Waste Volume (m <sup>3</sup> ):	
Additional Information:	
<u>TSCA Waste Disposal</u>	
Disposal Site:	
Waste Volume (m <sup>3</sup> ):	
Additional Information:	
<u>Asbestos Waste Disposal</u>	
Disposal Site:	
Waste Volume (m <sup>3</sup> ):	
Additional Information:	
<u>Low-Level Waste Disposal</u>	
Disposal Site:	
Waste Volume (m <sup>3</sup> ):	
Additional Information:	
<u>Low-Level Mixed Waste Disposal</u>	
Disposal Site:	
Waste Volume (m <sup>3</sup> ):	
Additional Information:	
<u>Recycled Material</u>	
Recycle Facility:	
Waste Volume (m <sup>3</sup> ):	
Additional Information:	
<u>Property Disposition</u>	
Receiver Locations <i>(major items only)</i> :	
Volume (m <sup>3</sup> ):	
Weight (tons):	
Additional Information:	

<b>Section D. Approvals</b>	
Kaiser-Hill Project Manager	
Name/Signature	Date 12.21.04


**Utility isolation for Building 564:**

**Natural Gas:** 1-Inch natural gas line isolated above ground and purged 8/17/03. Line was air gapped 9/28/04 approximately 10 feet east of 564 slab.

**Domestic Water:** The 4-inch domestic water isolated 5.5 feet deep 9/8/04 near center of 8<sup>th</sup> Street east of 564.

**Sewer:** The 4 inch PVC sewer line flushed, cut, and grouted 6 feet deep 9-7-04 outside of 564 south east corner.

**Electrical:** The electrical line was supplying heat was isolated at the pole east of 564 on the east side of 8th Street. The main power for the building was isolated at the transformer on a pole east side 564 east of 8<sup>th</sup> Street.

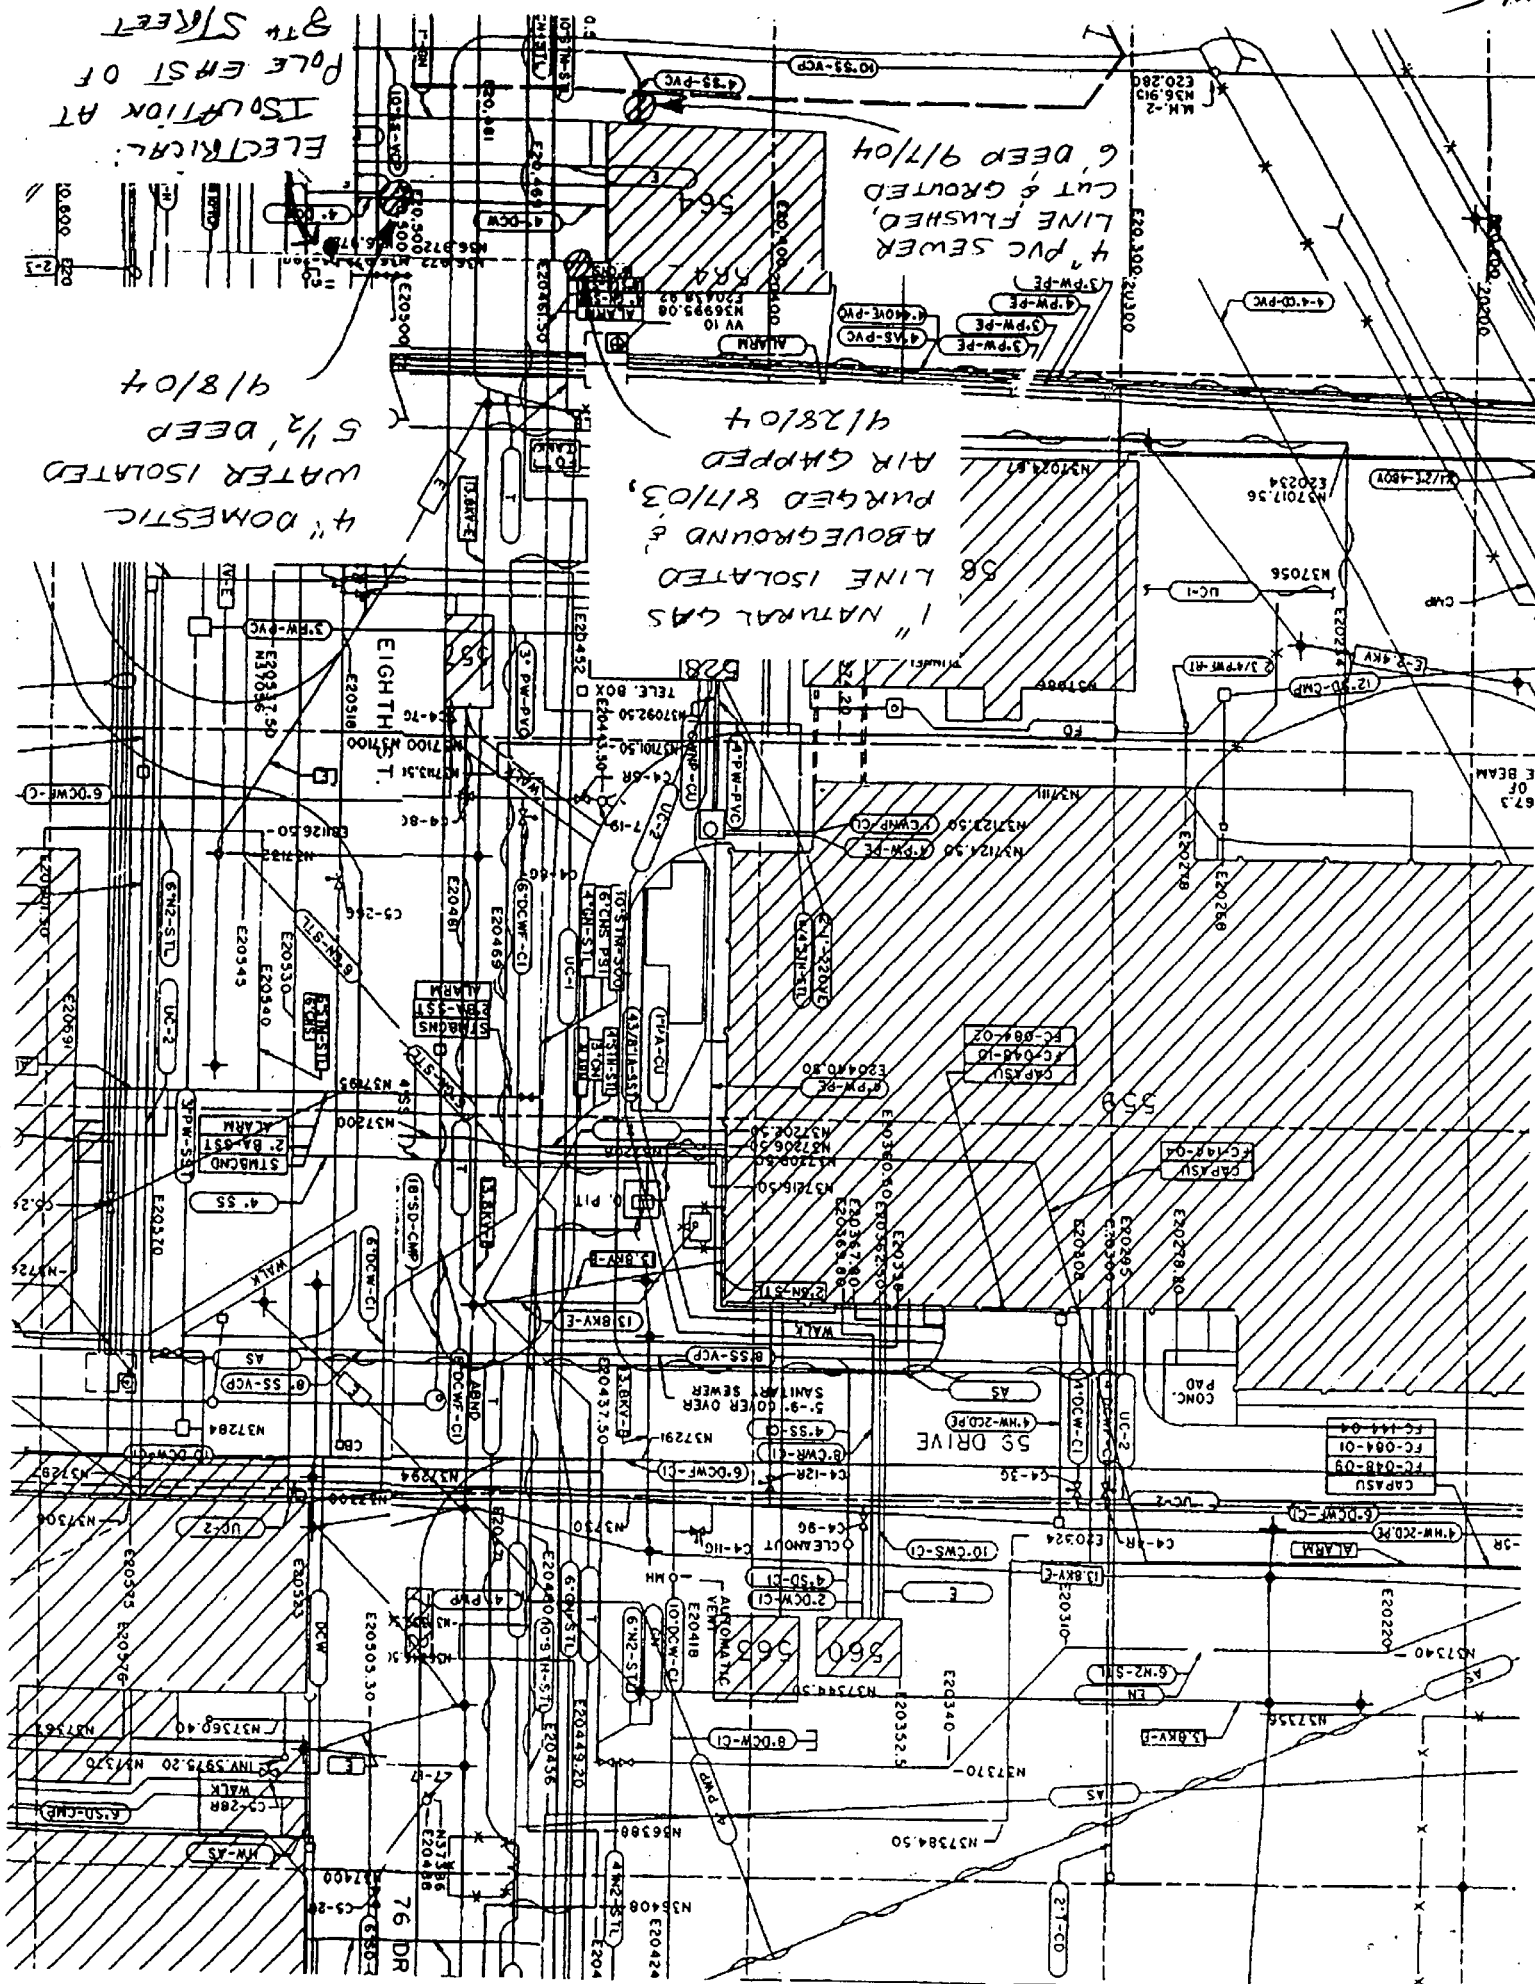

ELECTRICAL:  
ISOLATION AT  
POLE EAST OF  
8TH STREET

4\"/>

1\"/>

4\"/>

55 DRIVE

76 DR
