

CORRES. CONTROL
INCOMING LTR NO.

00171 RF05

DUE DATE

ACTION

RECEIVED

2005 APR -4 A 8:23

Department of Energy

CORRESPONDENCE
CONTROL

**ROCKY FLATS PROJECT OFFICE
10808 HIGHWAY 93, UNIT A
GOLDEN, COLORADO 80403-8200**

MAR 29 2005

05-DOE-00159

[illegible]

Mr. Steven H. Gunderson

Rocky Flats Cleanup Agreement Project Coordinator

Colorado Department of Public Health and Environment

4300 Cherry Creek Drive South

• Denver, Colorado 80246-1530

Dear Mr. Gunderson:

Please find enclosed a completed Rocky Flats Cleanup Agreement Type 1 Building

Disposition Closeout Report provided for your information for T130E, FEG-007-05 and

T130G, FEG-006-05. Questions may be directed to Gary Morgan, RFFO RFPM, at

-(303) 966-6003.

Sincerely,

Joseph A. Legare, Director
RFPO Project management

Enclosure

COR. CONTROL	X	X
ADMIN. RECORD	X	X
PATS		

cc w/o Encl.:

F. Lockhart, OOM, RFPO

D. McCranie, HOCPM, RFPO

G. Morgan, RFPM, RFPO

S. Nesta, K-H RISS Env

C. Freiboth, K-H RISS D&D

K. Wiemelt, K-H RISS D&D

M. Aguilar, USEPA

D. Abelson, RFCLOG

Reviewed for Addressee
Corres. Control RFP

Date 4/4/05 By 21

Ref. Ltr. #

OS RFO0271


052F00270

cc w/Encl.:

Administrative Record

DOE ORDER #

5400.1



ADMIN RECORD

RECEIVED

MAR 15 P 2:02

KAISER HILL
COMPANY



March 14, 2005

05-RF-00271

Gary Morgan, Functional Lead
Cadre Project Management Division
DOE, RFPO

TRANSMITTAL OF CLOSE OUT REPORT FOR BUILDING T130E - FEG-007-05

Attached is the Closeout Report for the Type 1 facility Building T130E - Office Trailer. Please note that a copy of the report has been submitted to the CERCLA AR by the Kaiser-Hill RISS project.

Please contact Steve Nesta x6386 with questions or concerns.

Frank E. Gibbs
Deputy Project Manager
Remediation, Industrial D&D, and Site Services

Attachment:
As Stated

SMN:pvt

Orig. and 1 cc - Gary Morgan

cc:
Joseph Legare
Deanna McCranie

Type 1 Facility Closeout Report

Section A. Facility Data	
Facility No.	T130E
Facility Descriptor:	Office Trailer, 15,400 square feet
Project:	RISS - Area 5 D&D
Date of Demolition:	February 17, 2005
Additional Information:	Modular corrugated metal office trailer demolished and disposed of as sanitary waste. (Must include information on environmental releases and conditions of site at turnover to Environmental Restoration)
Section B. Final Characterization Data	
Reconnaissance Level Characterization Report (concurrency received)	Reconnaissance Level Characterization Report - Concurrency, Steven H. Gunderson to Joseph A. Legare, dated April 22, 2003.
In-process Characterization	N/A
Pre-Demolition Survey Report (approval received)	N/A
Post-Demolition Survey Report (as necessary)	N/A
Section C. Waste Data (complete categories as appropriate)	
Sanitary Disposal	
Disposal Site:	BFI Foothills Landfill, Golden, Colorado
Waste Volume (m ³):	2760 Cubic yards
Waste Weight (tons):	634.09 tons
Additional Information:	Above grade building debris
Hazardous Disposal	
Disposal Site:	Kettleman Hills Facility, Kettleman City, CA or Bethlehem Apparatus Co, Hellertown, PA
Waste Volume (m ³):	Minor amounts
Additional Information:	Electronic circuit boards, thermostats, exit signs, batteries, fluorescent light bulbs and any other RCRA hazardous components were removed and taken to the RFCA temporary unit for combination with like waste streams for disposal.
TSCA Waste Disposal	
Disposal Site:	
Waste Volume (m ³):	N/A
Additional Information:	
Asbestos Waste Disposal	
Disposal Site:	
Waste Volume (m ³):	N/A
Additional Information:	
Low-Level Waste Disposal	
Disposal Site:	
Waste Volume (m ³):	N/A
Additional Information:	
Low-Level Mixed Waste Disposal	
Disposal Site:	
Waste Volume (m ³):	N/A
Additional Information:	
Recycled Material	
Recycle Facility:	
Waste Volume (m ³):	
Additional Information:	

Type 1 Facility Closeout Report

Property Disposition

Receiver Locations (major items only): N/A

Volume (m³):

Weight (tons):

Additional Information:

Section D. Approvals

Kaiser-Hill Project Manager

CJ FREEMAN
Name/Signature

03/11/05

Date


Additional Facility Information


Building T130E was an approximately 15,400 square foot modular trailer acquired in 1991. The structure was corrugated metal siding with corrugated metal skirting. The entrances had wooden stairs leading to a wooden enclosure.

Building T130E had the following utilities: electrical, plant water, plant sanitary and fire protection provided by an overhead sprinkler system and wall mounted fire extinguishers.

The entire T130E structure was removed during D&D activities, and sent offsite for disposal. The utilities were disconnected and removed to at least three feet below final grade as indicated on the attached map. There are no remaining structural components, utility lines, or parts of the foundation. The buildings are not in an IHSS or PAC therefore no soil sampling is required.

5

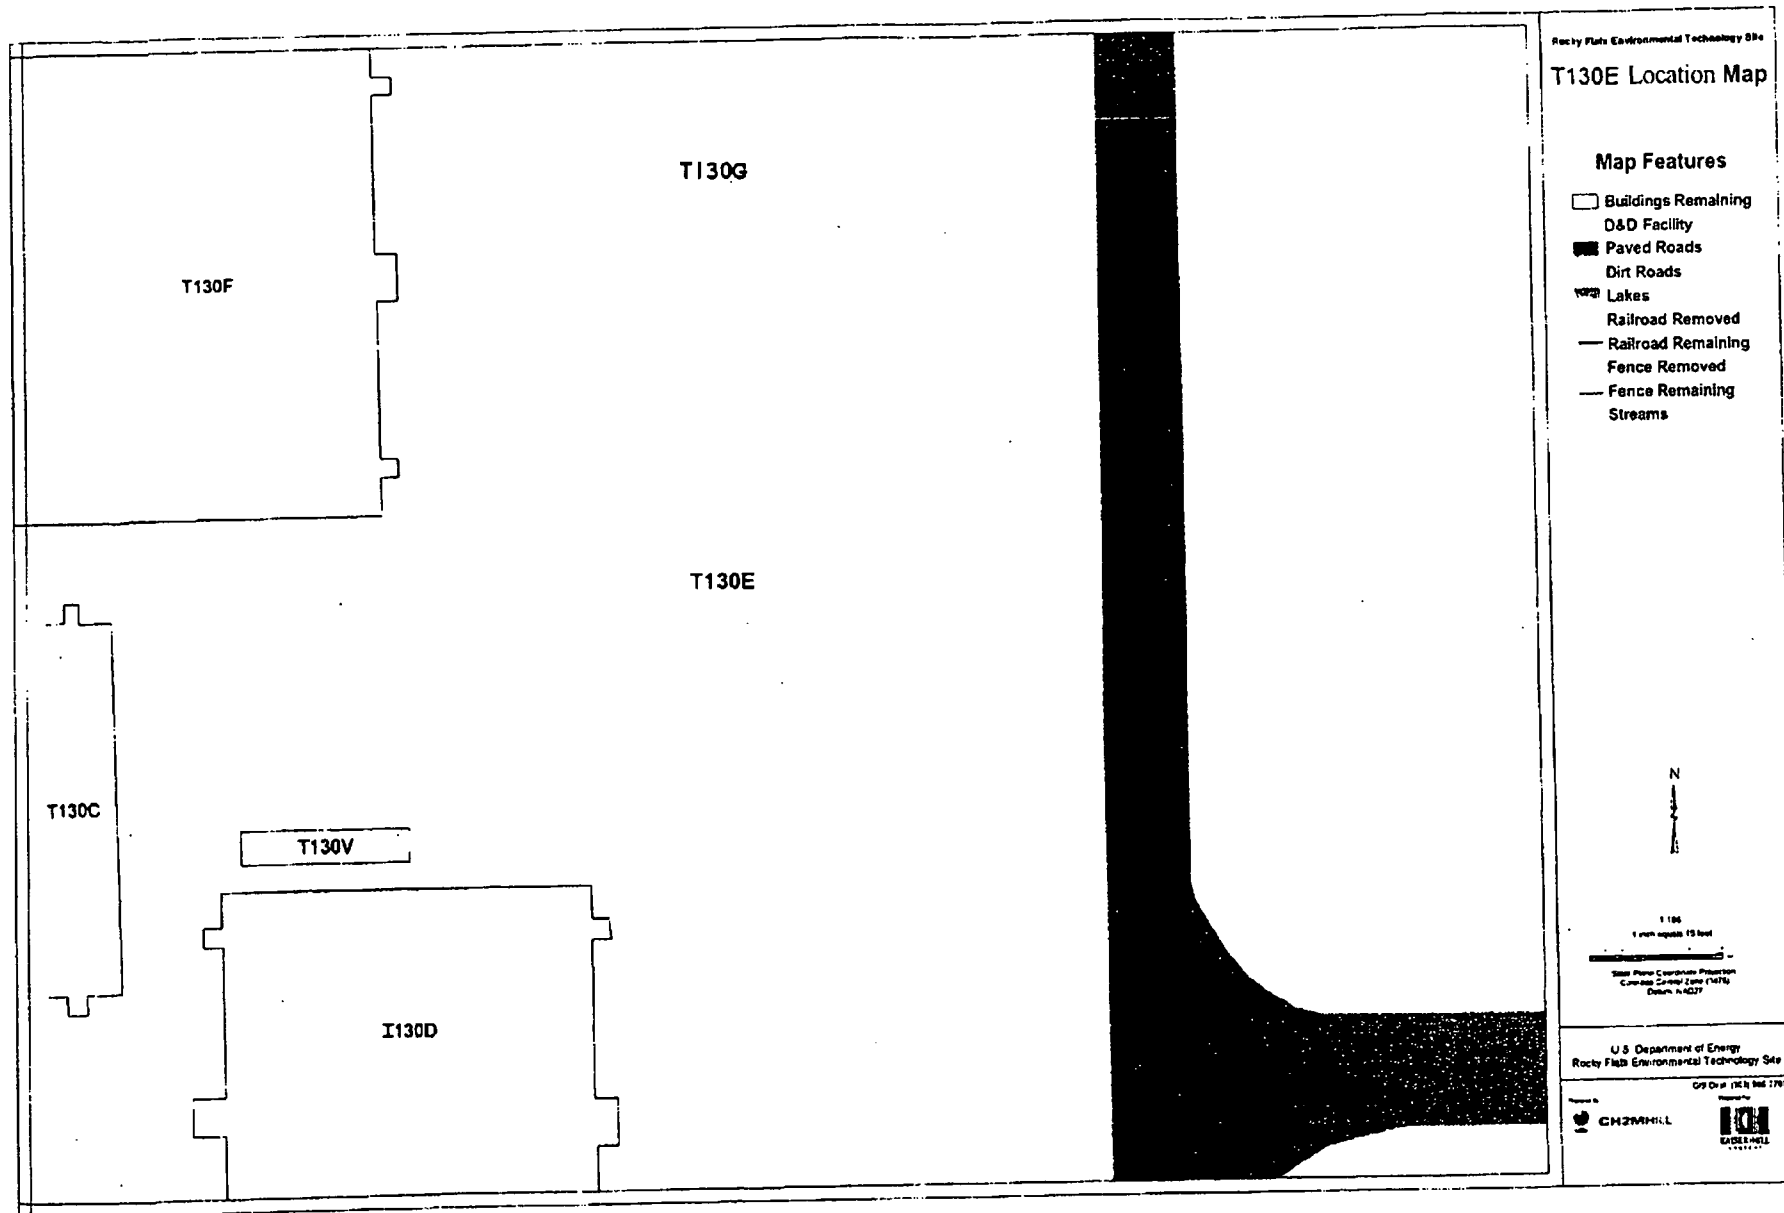

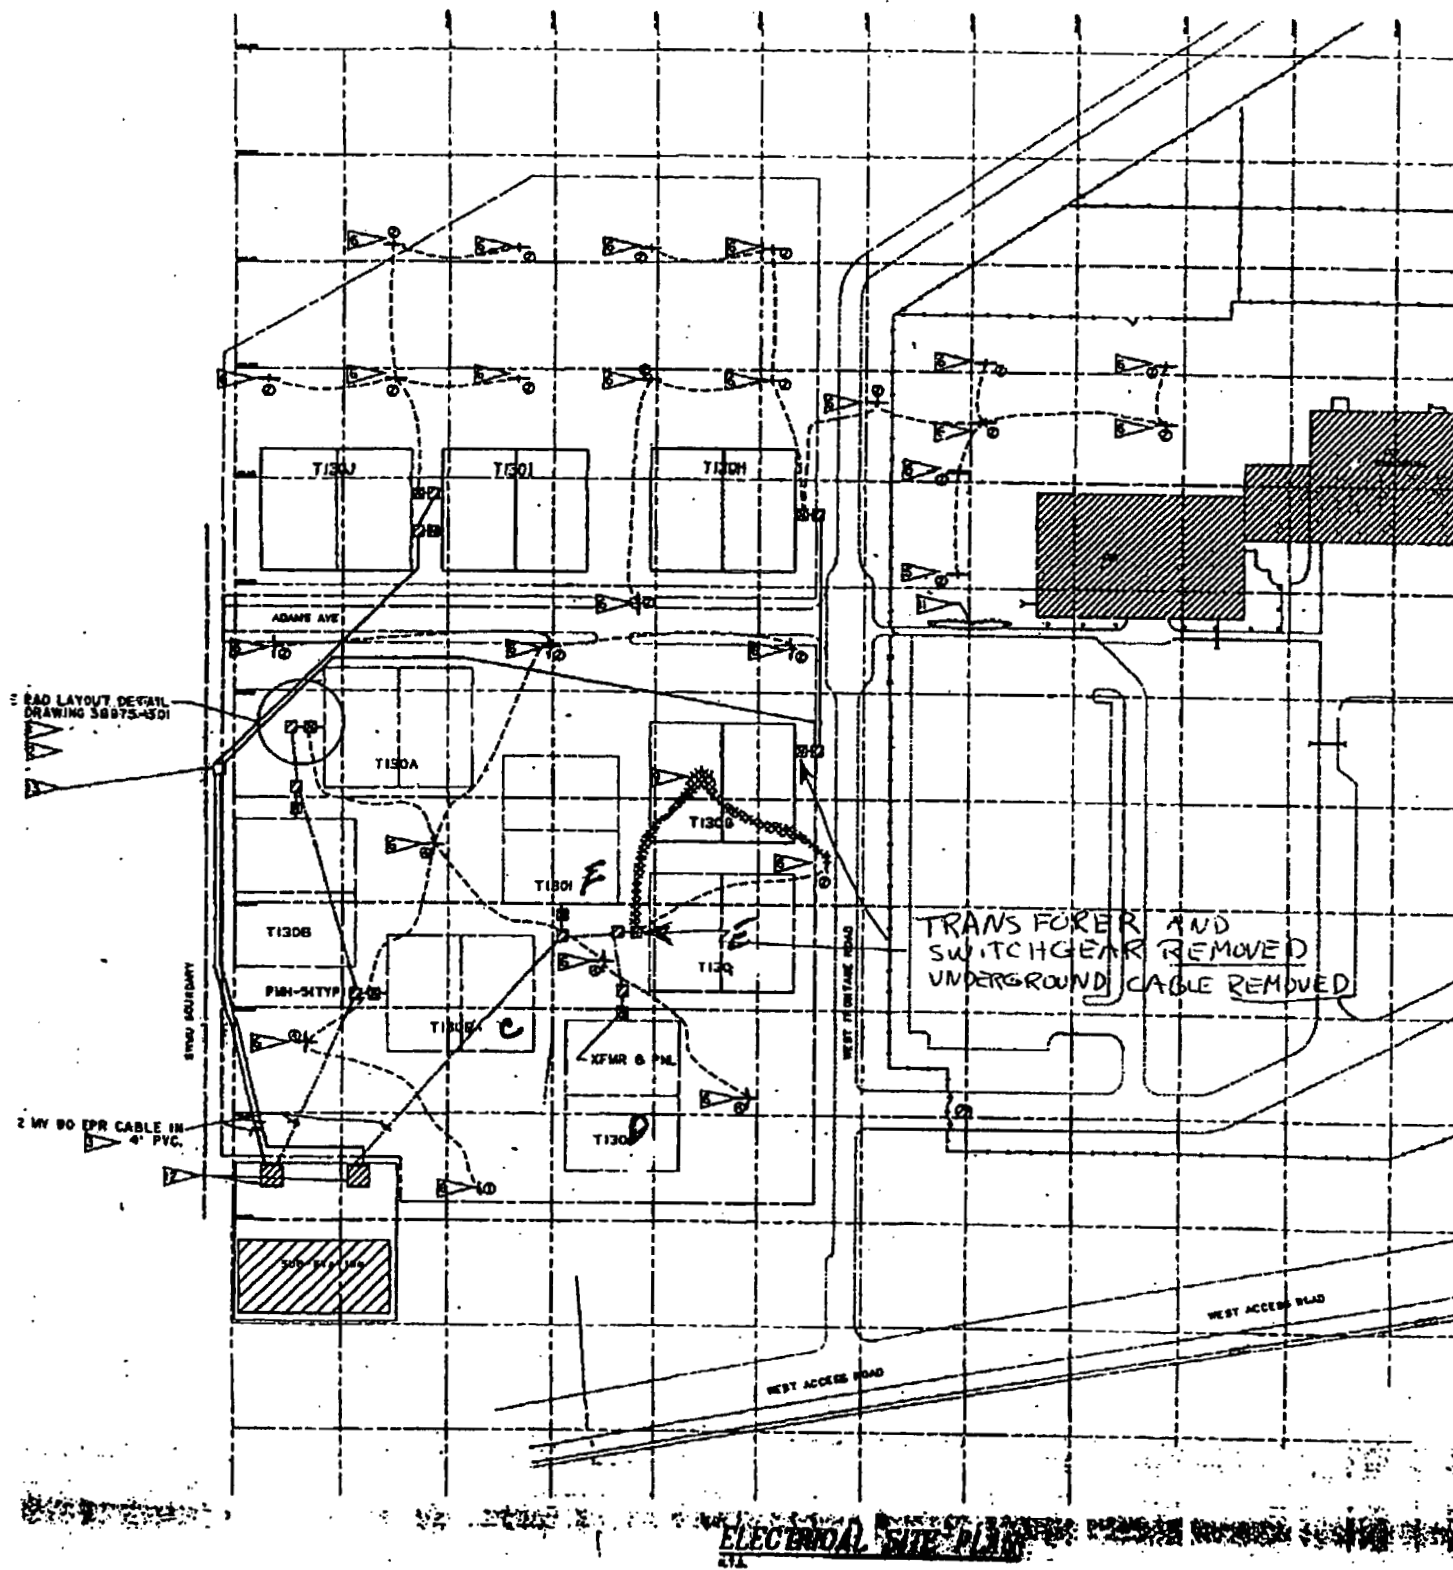

RECEIVED

MAR 15 P 2 21

RECEIVED
DOE



March 14, 2005

05-RF-00270

Gary Morgan, Functional Lead
Cadre Project Management Division
DOE, RFPO

TRANSMITTAL OF CLOSE OUT REPORT FOR BUILDING -- T130G -- FEG-006-05

Attached is the Closeout Report for the Type 1 facility Building T130G -- Office Trailer. Please note that a copy of the report has been submitted to the CERCLA AR by the Kaiser-Hill RISS project.

Please contact Steve Nestax6386 with questions or concerns.

Frank E. Gibbs
Frank E. Gibbs
Deputy Project Manager
Remediation, Industrial D&D, and Site Services

Attachment:
As Stated

SMN:pvt

Orig. and 1 cc -- Gary Morgan

cc:
Joseph Legare
Deanna McCranie

Kaiser-Hill Company, L.L.C. *5400*
Rocky Flats Environmental Technology Site, 10808 Highway 93, Unit B, T130F, Golden, CO 80403-8200 • (303) 966-6386

Type 1 Facility Closeout Report

Section A. Facility Data	
Facility No.	T130G
Facility Descriptor:	Office Trailer, 15,400 square feet
Project:	RISS - Area 5 D&D
Date of Demolition:	February 24, 2005
Additional Information:	Modular corrugated metal office trailer demolished and disposed of as sanitary waste. (Must include information on environmental releases and conditions of site at turnover to Environmental Restoration)
Section B. Final Characterization Data	
Reconnaissance Level Characterization Report (concurrency received)	Reconnaissance Level Characterization Report - Concurrence, Steven H. Gunderson to Joseph A. Legare, dated April 22, 2003.
In-process Characterization	N/A
Pre-Demolition Survey Report (approval received)	N/A
Post-Demolition Survey Report (as necessary)	N/A
Section C. Waste Data (complete categories as appropriate)	
Sanitary Disposal	
I Sit	BFI Foothills Landfill, Golden, Colorado
Waste Volume (m ³):	2660 Cubic yards
Waste Weight (tons):	602.94 tons
Additional Information:	Above grade building debris
Hazardous Disposal	
Disposal Site:	Kettleman Hills Facility, Kettleman City, CA or Bethlehem Apparatus Co, Hellertown, PA
Waste Volume (m ³):	Minor amounts
Additional Information:	Electronic circuit boards, thermostats, exit signs, batteries, fluorescent light bulbs and any other RCRA hazardous components were removed and taken to the RFCA temporary unit for combination with like waste streams for disposal.
TSCA Waste Disposal	
Disposal Site:	
Waste Volume (m ³):	N/A
Additional Information:	
Asbestos Waste Disposal	
Disposal Site:	
Waste Volume (m ³):	N/A
Additional Information:	
Low-Level Waste Disposal	
Disposal Site:	
Waste Volume (m ³):	N/A
Additional Information:	
Low-Level Mixed Waste Disposal	
Disposal Site:	
Waste Volume (m ³):	N/A
Additional Information:	
Recycled Material	
Recycle Facility:	
Waste Volume (m ³):	
Additional Information:	

Type 1 Facility Closeout Report

Property Disposition

Receiver Locations (*major items only*): N/A

Volume (m³):

Weight (tons):

Additional Information:

Section D. Approvals

Kaiser-Hill Project Manager

CJ Freeman

Name/Signature

05/14/05


Date

Additional Facility Information

Building T130G was an approximately 15,400 square foot modular trailer acquired in 1991. The structure was corrugated metal siding with corrugated metal skirting. The entrances had wooden stairs leading to a wooden enclosure.

Building T130G had the following utilities: electrical, plant water, plant sanitary and fire protection provided by an overhead sprinkler system and wall mounted fire extinguishers.

The entire T130G structure was removed during D&D activities, and sent offsite for disposal. The utilities were disconnected and removed to at least three feet below final grade as indicated on the attached map. There are no remaining structural components, utility lines, or parts of the foundation. The buildings are not in an IHSS or PAC therefore no soil sampling is required.

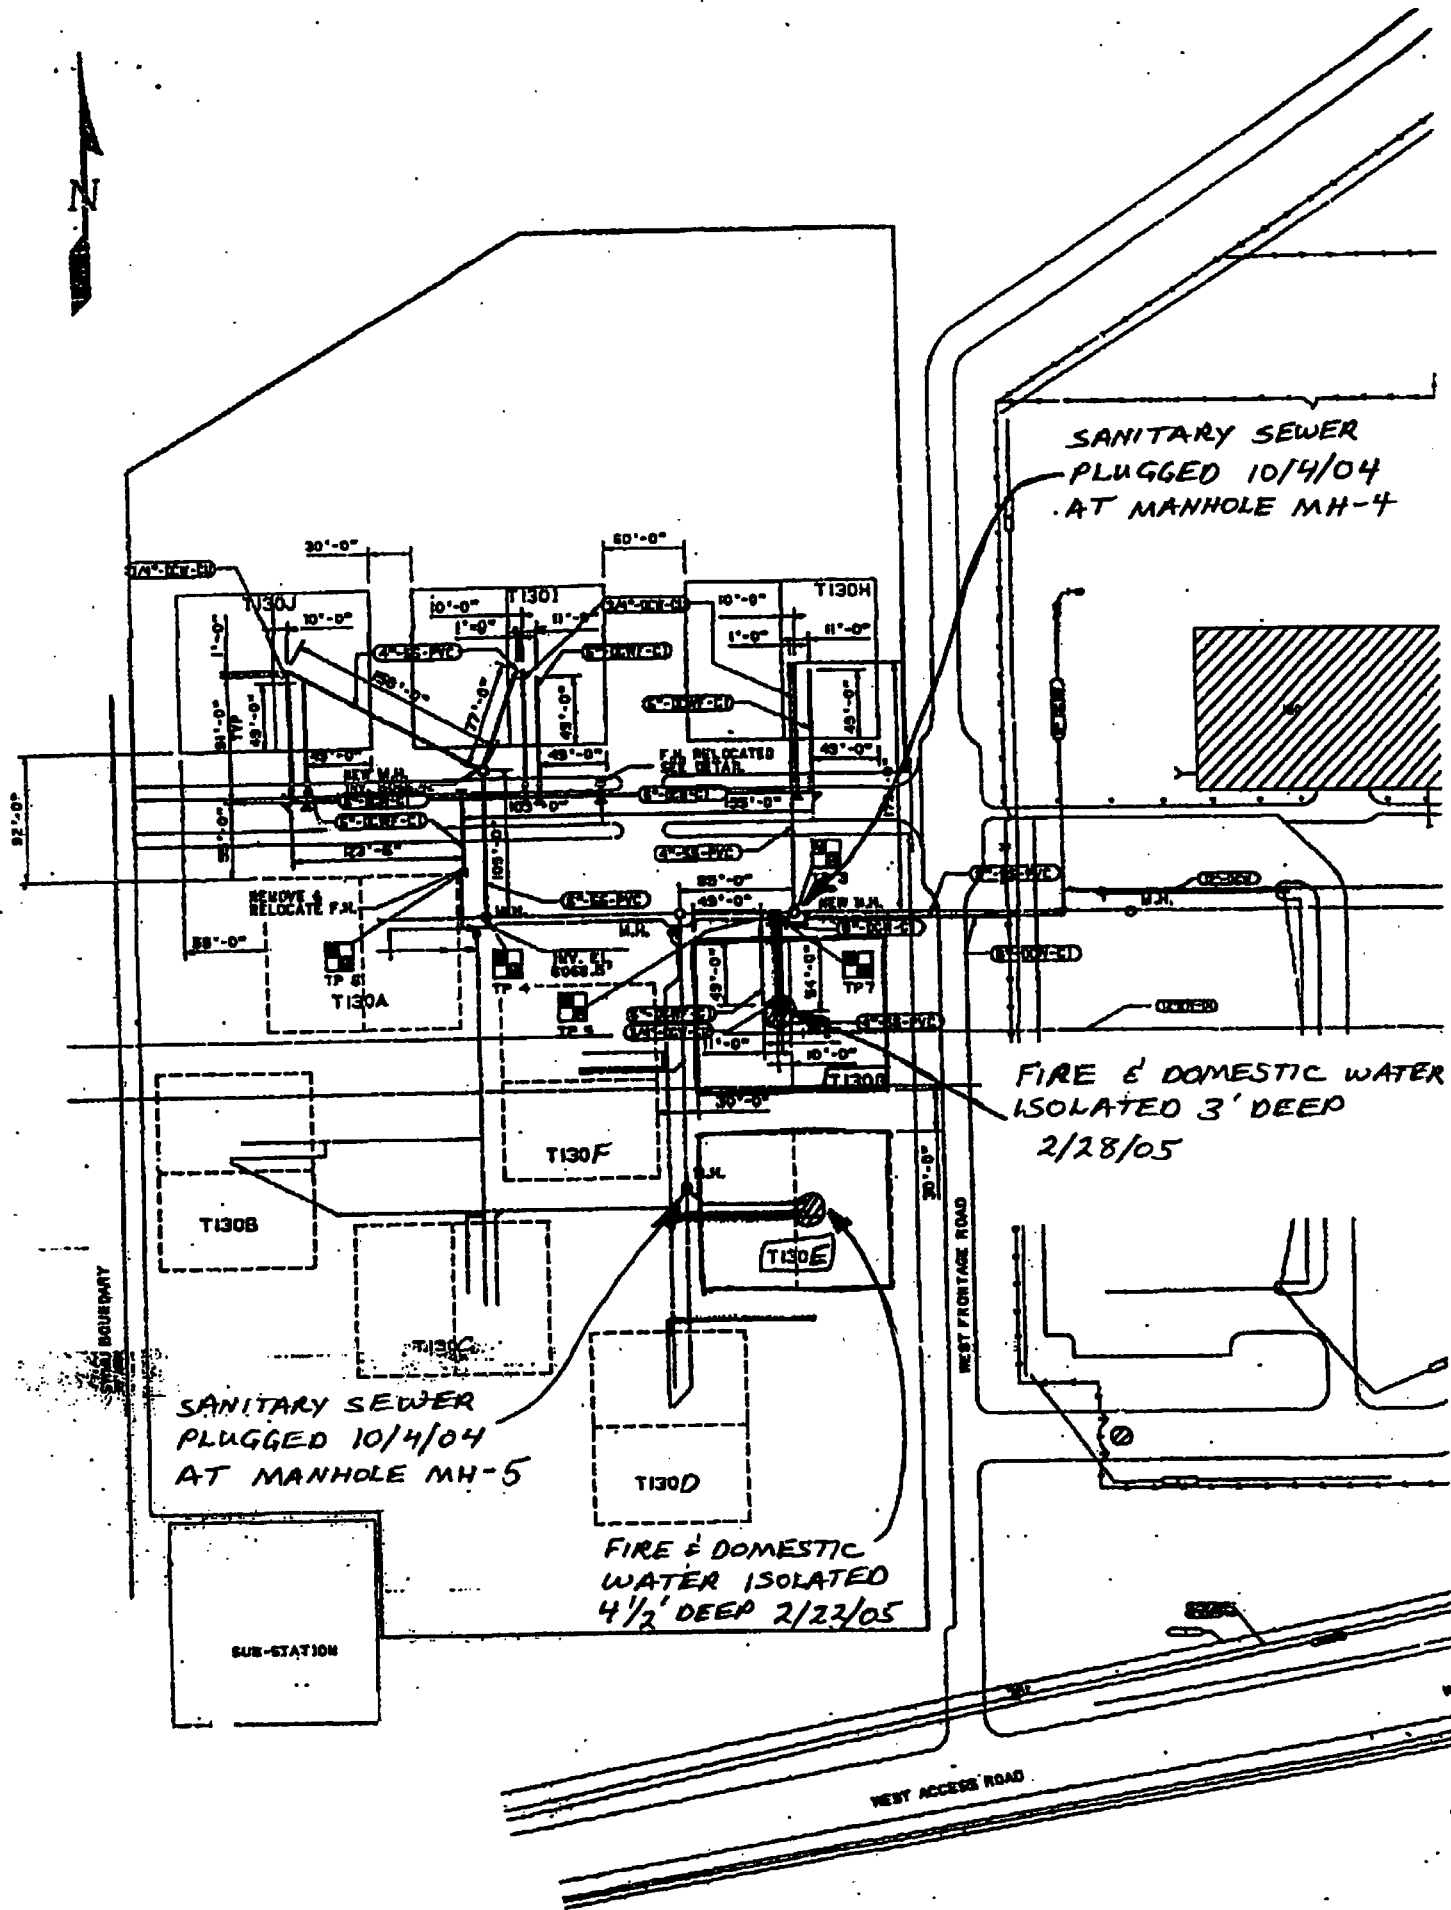


SANITARY SEWER
PLUGGED 10/4/04
AT MANHOLE MH-4

FIRE & DOMESTIC WATER
ISOLATED 3' DEEP
2/28/05

SANITARY SEWER
PLUGGED 10/4/04
AT MANHOLE MH-5

FIRE & DOMESTIC
WATER ISOLATED
4 1/2' DEEP 2/23/05

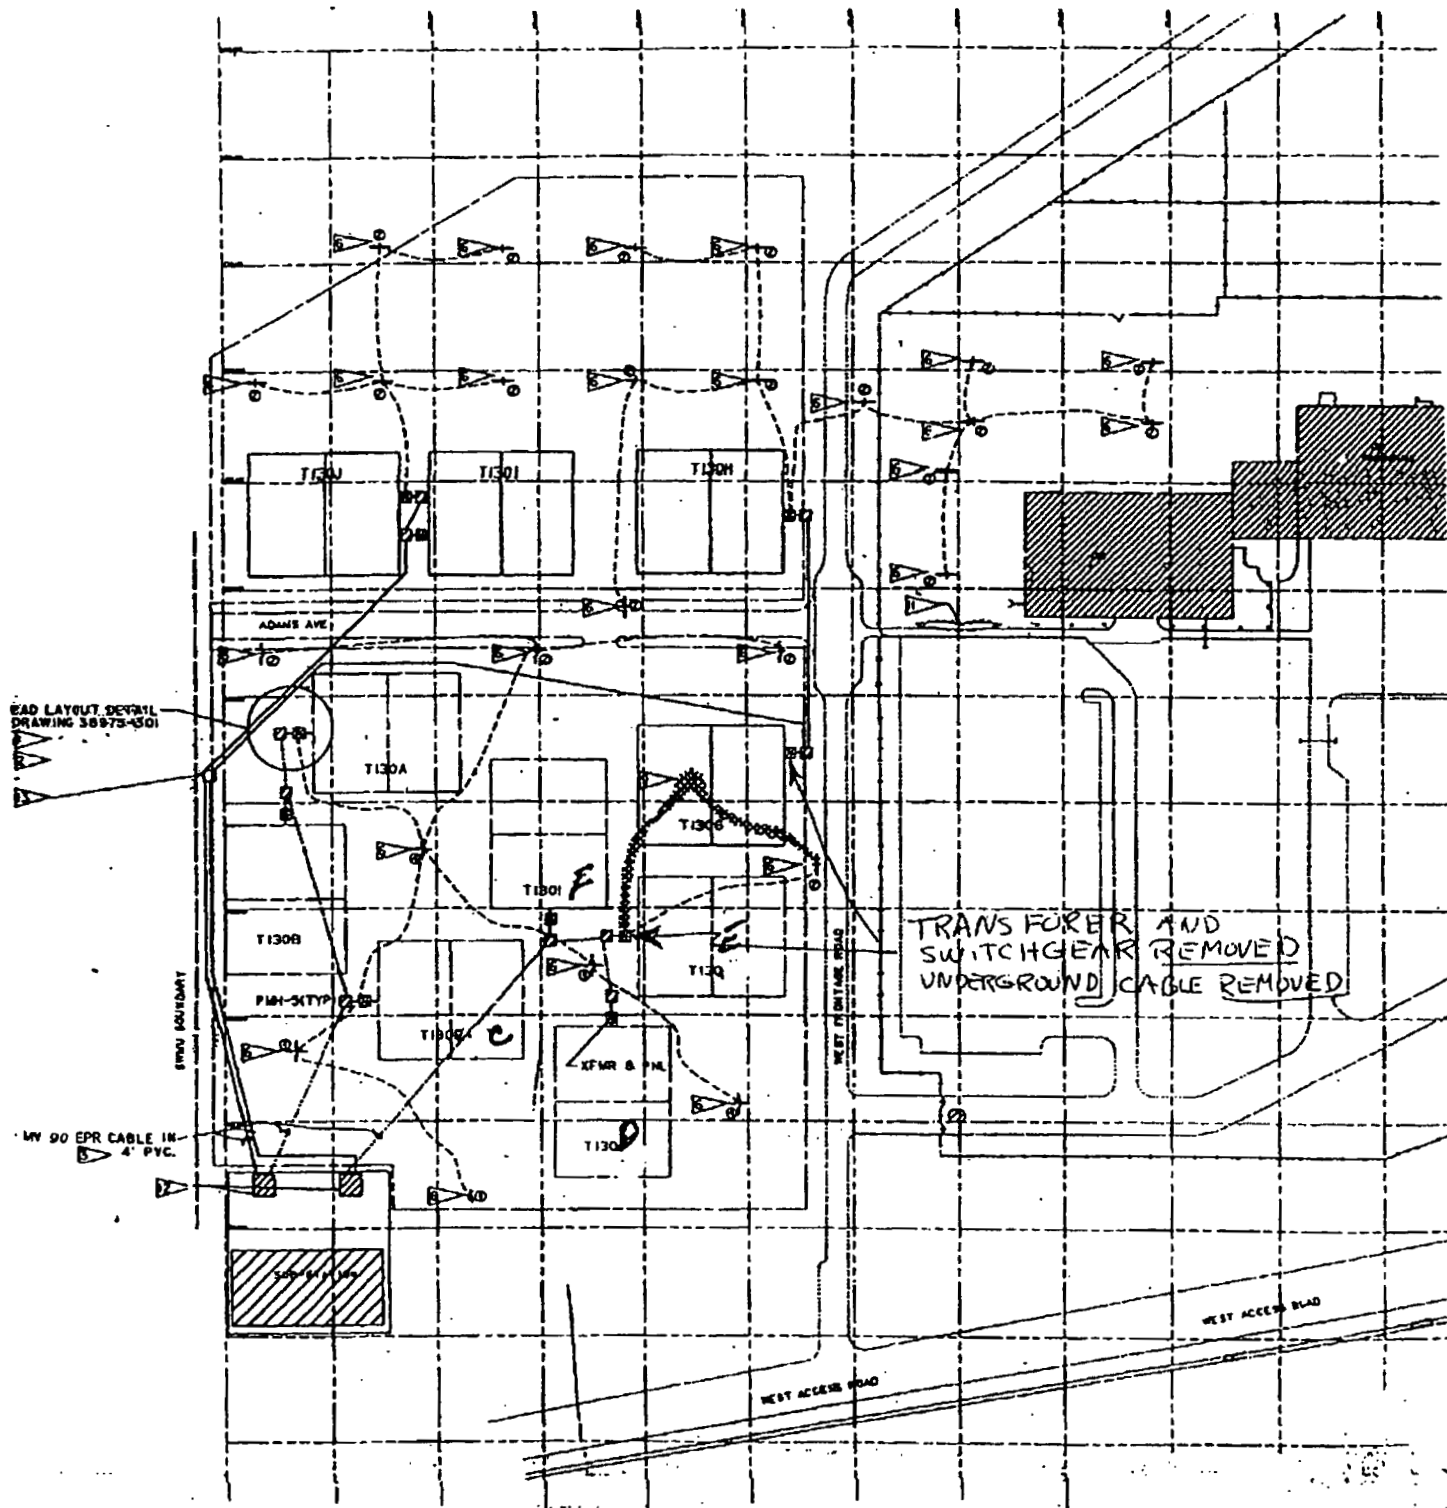

ELECTRICAL SITE PLAN

13/13
