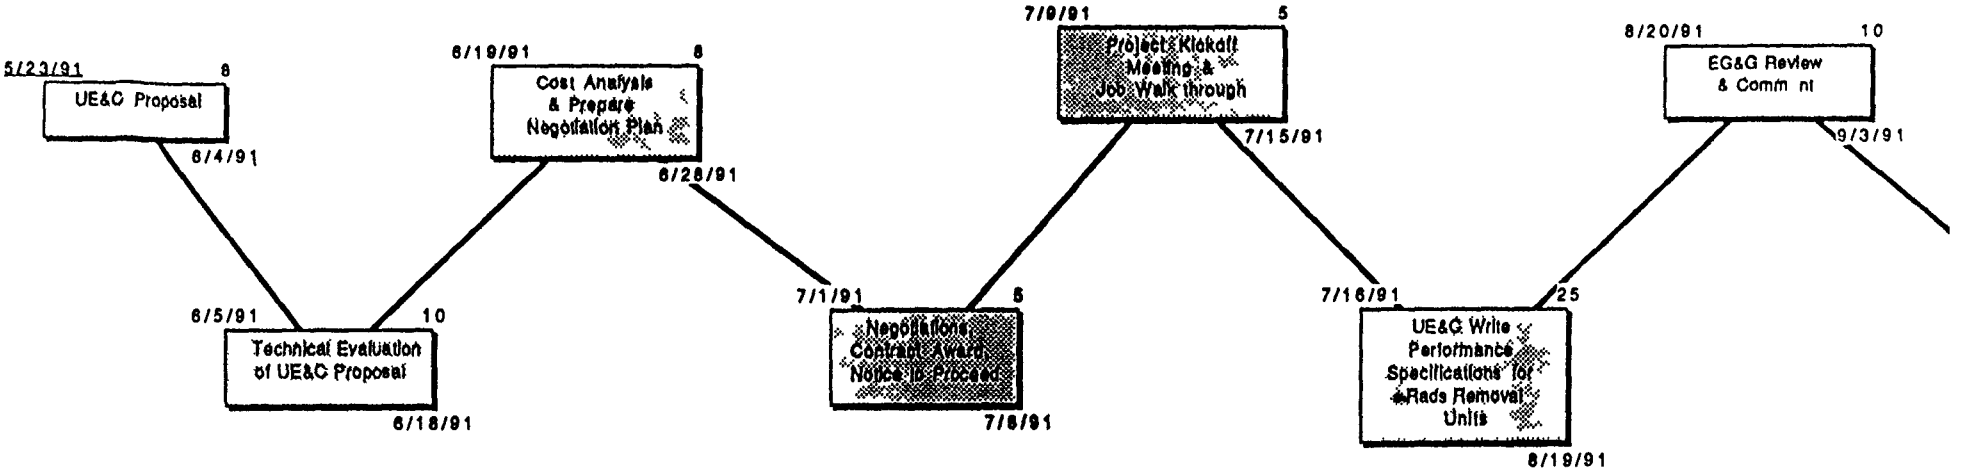

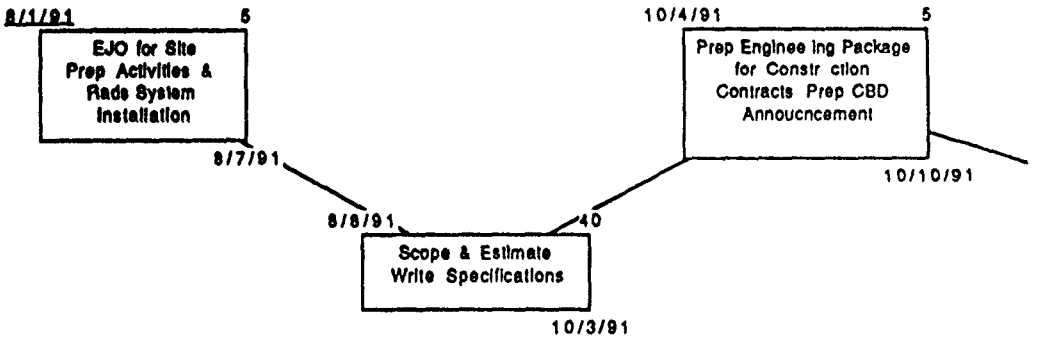

OU 2 So WALNUT CREEK IRA Radionuclides Removal System Design & Construction

Dated 6/30/91

Assumes Separate Design & Construct Contracts

ADMIN RECORD

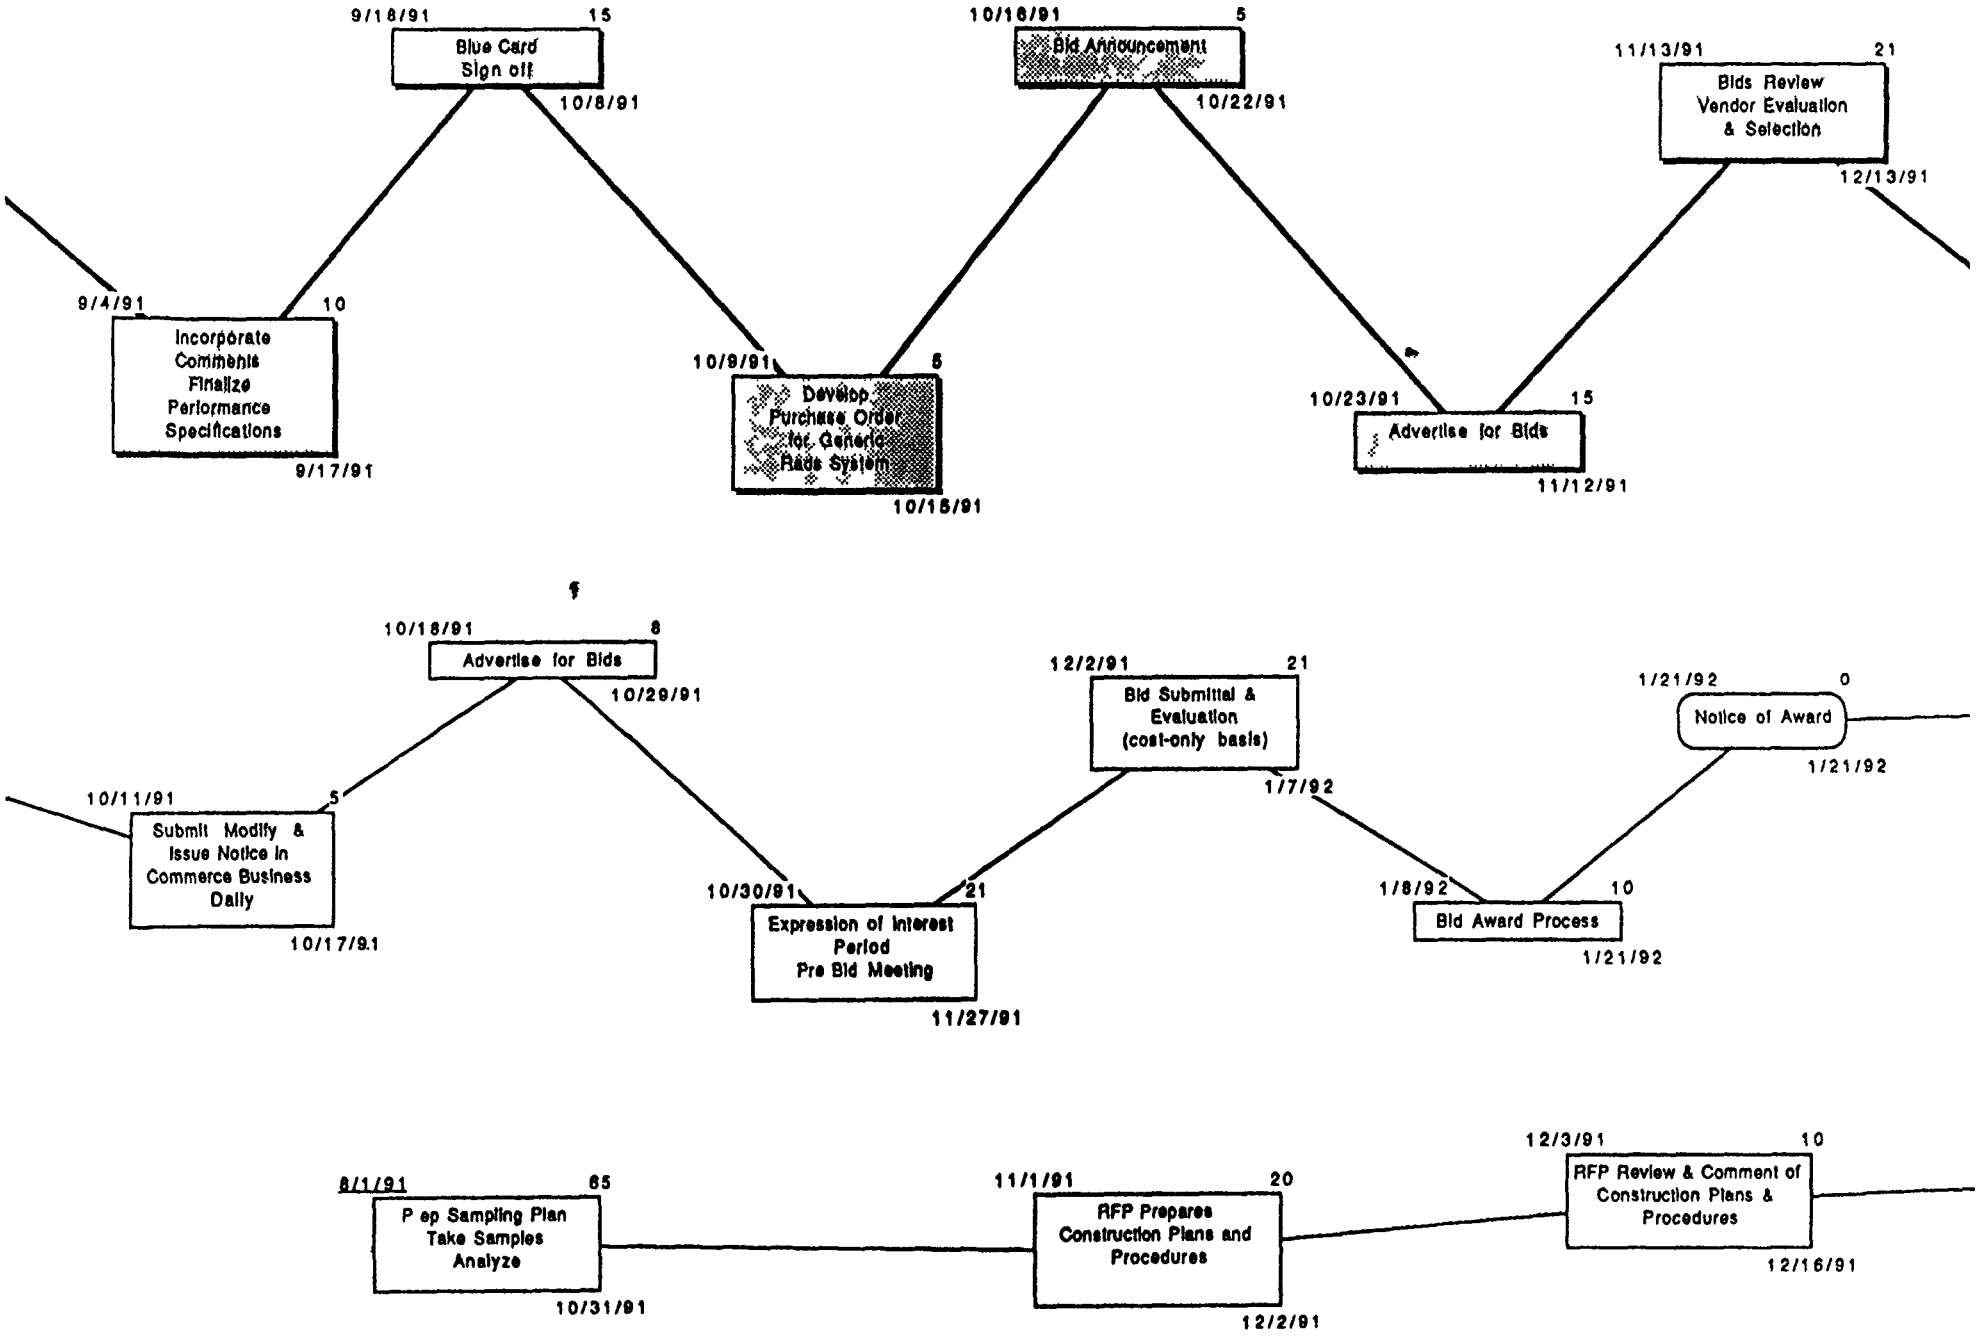
9/4/91
Incorporate Comments Finalize Performance Specifications
10
9/17/91
9/18/91
Blue Card Sign off
15
10/8/91
10/9/91
Develop Purchase Order for Generic Rads System
5
10/15/91
10/16/91
Bid Announcement
5
10/22/91
10/23/91
Advertise for Bids
15
11/12/91
11/13/91
Bids Review Vendor Evaluation & Selection
21
12/13/91
10/11/91
Submit Modify & Issue Notice in Commerce Business Daily
5
10/17/91
10/18/91
Advertise for Bids
8
10/29/91
10/30/91
Expression of Interest Period Pre Bid Meeting
21
11/27/91
12/2/91
Bid Submittal & Evaluation (cost-only basis)
21
1/7/92
1/8/92
Bid Award Process
10
1/21/92
1/21/92
Notice of Award
0
1/21/92
8/1/91
P ep Sampling Plan Take Samples Analyze
65
10/31/91
11/1/91
RFP Prepares Construction Plans and Procedures
20
12/2/91
12/3/91
RFP Review & Comment of Construction Plans & Procedures
10
12/16/91

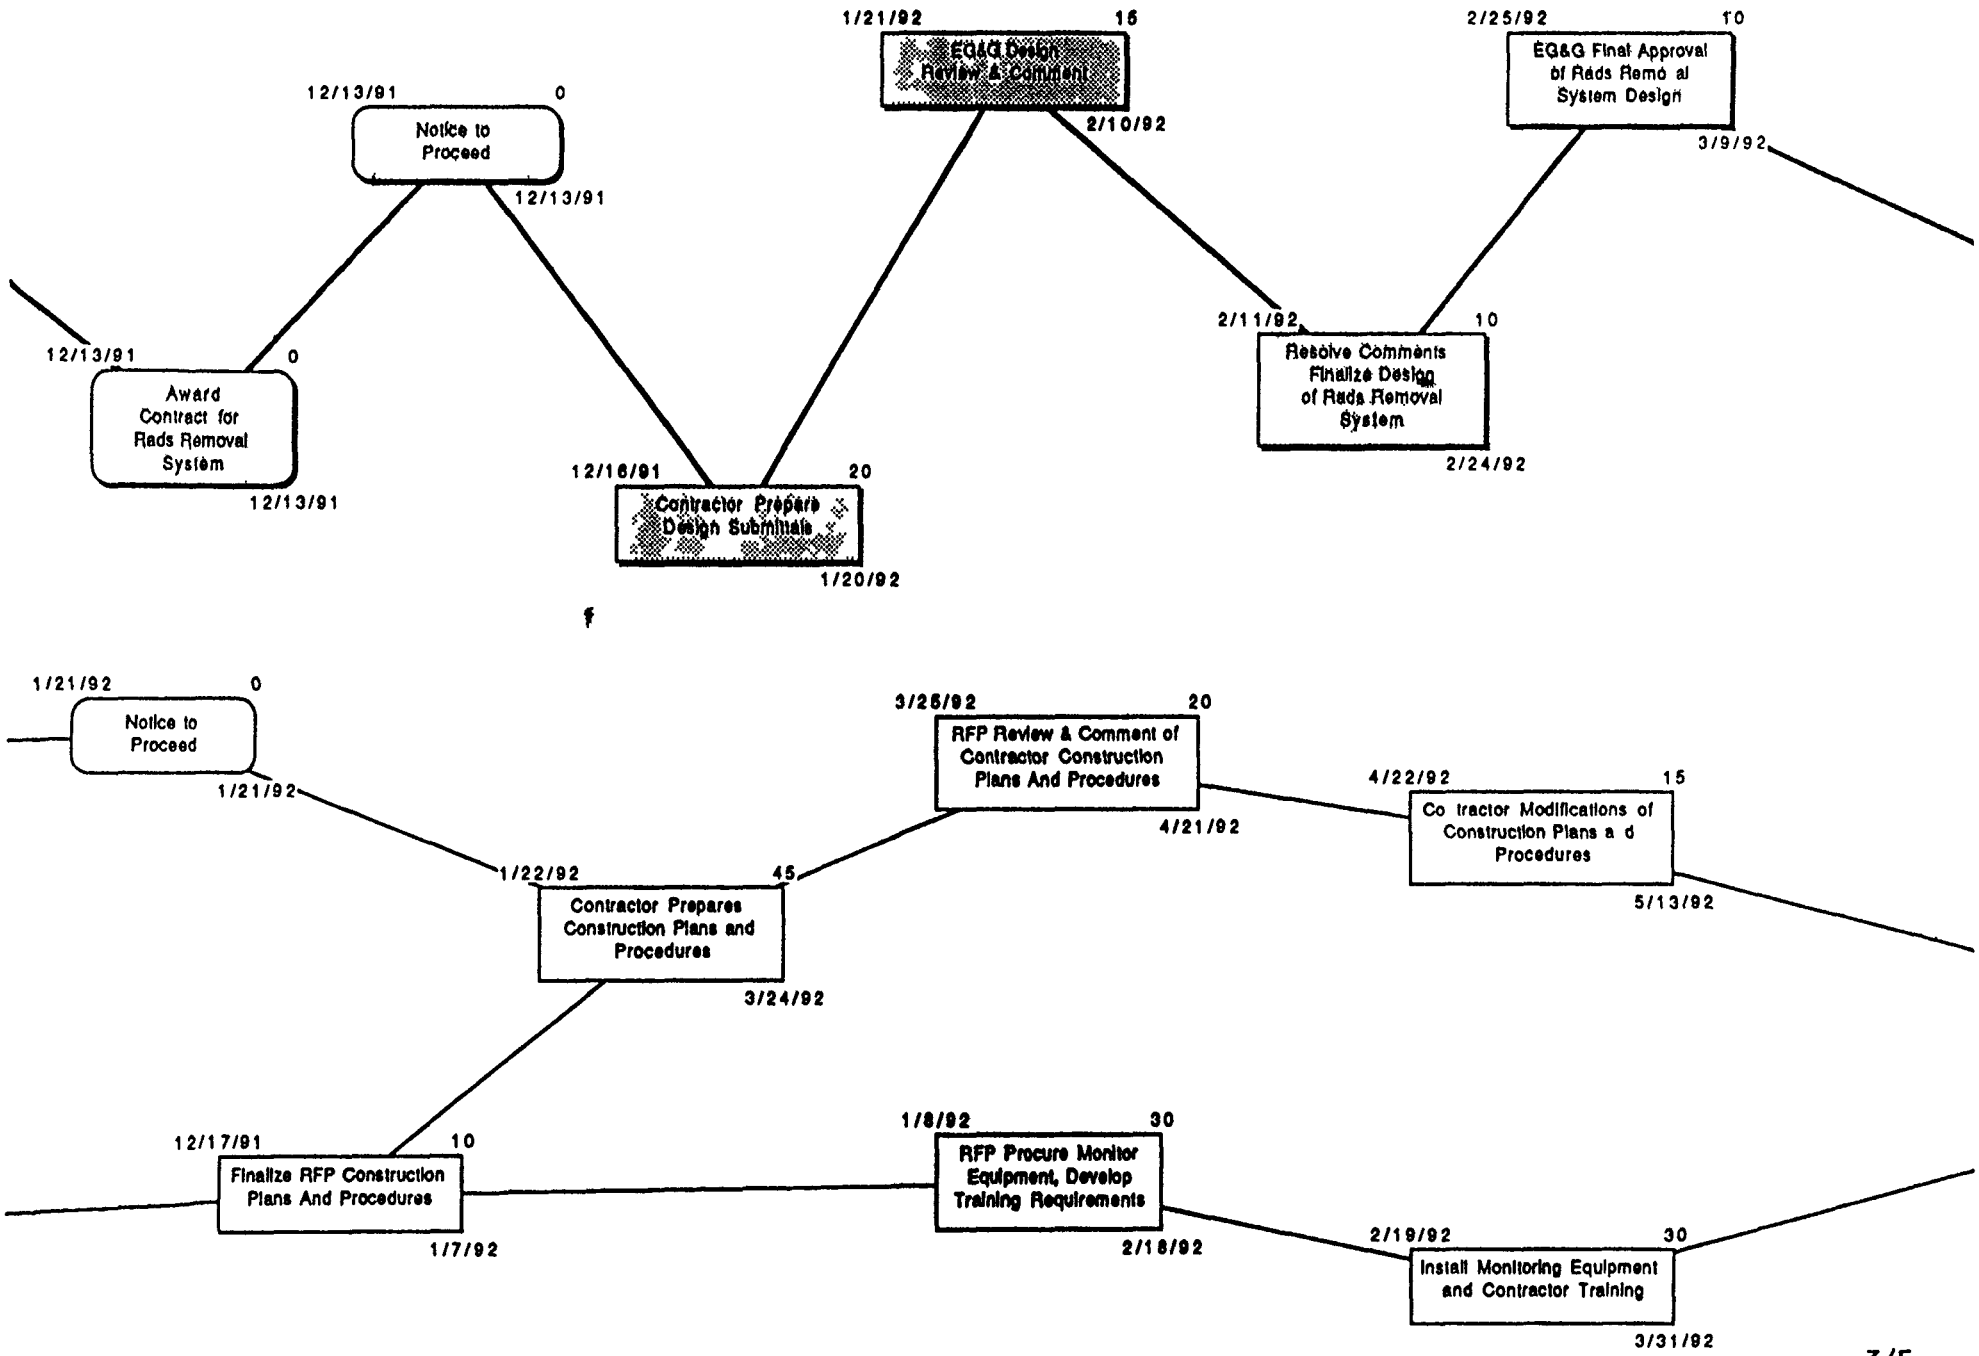
12/13/91
0
Notice to Proceed
12/13/91
12/13/91
0
Award Contract for Rads Removal System
12/13/91
12/16/91
20
Contractor Prepare Design Submittals
1/20/92
1/21/92
15
EG&G Design Review & Comment
2/10/92
2/11/92
10
Resolve Comments Finalize Design of Rads Removal System
2/24/92
2/25/92
10
EG&G Final Approval of Rads Removal System Design
3/9/92
1/21/92
0
Notice to Proceed
1/21/92
1/22/92
45
Contractor Prepares Construction Plans and Procedures
3/24/92
3/25/92
20
RFP Review & Comment of Contractor Construction Plans And Procedures
4/21/92
4/22/92
15
Contractor Modifications of Construction Plans and Procedures
5/13/92
12/17/91
10
Finalize RFP Construction Plans And Procedures
1/7/92
1/8/92
30
RFP Procure Monitor Equipment, Develop Training Requirements
2/18/92
2/19/92
30
Install Monitoring Equipment and Contractor Training
3/31/92

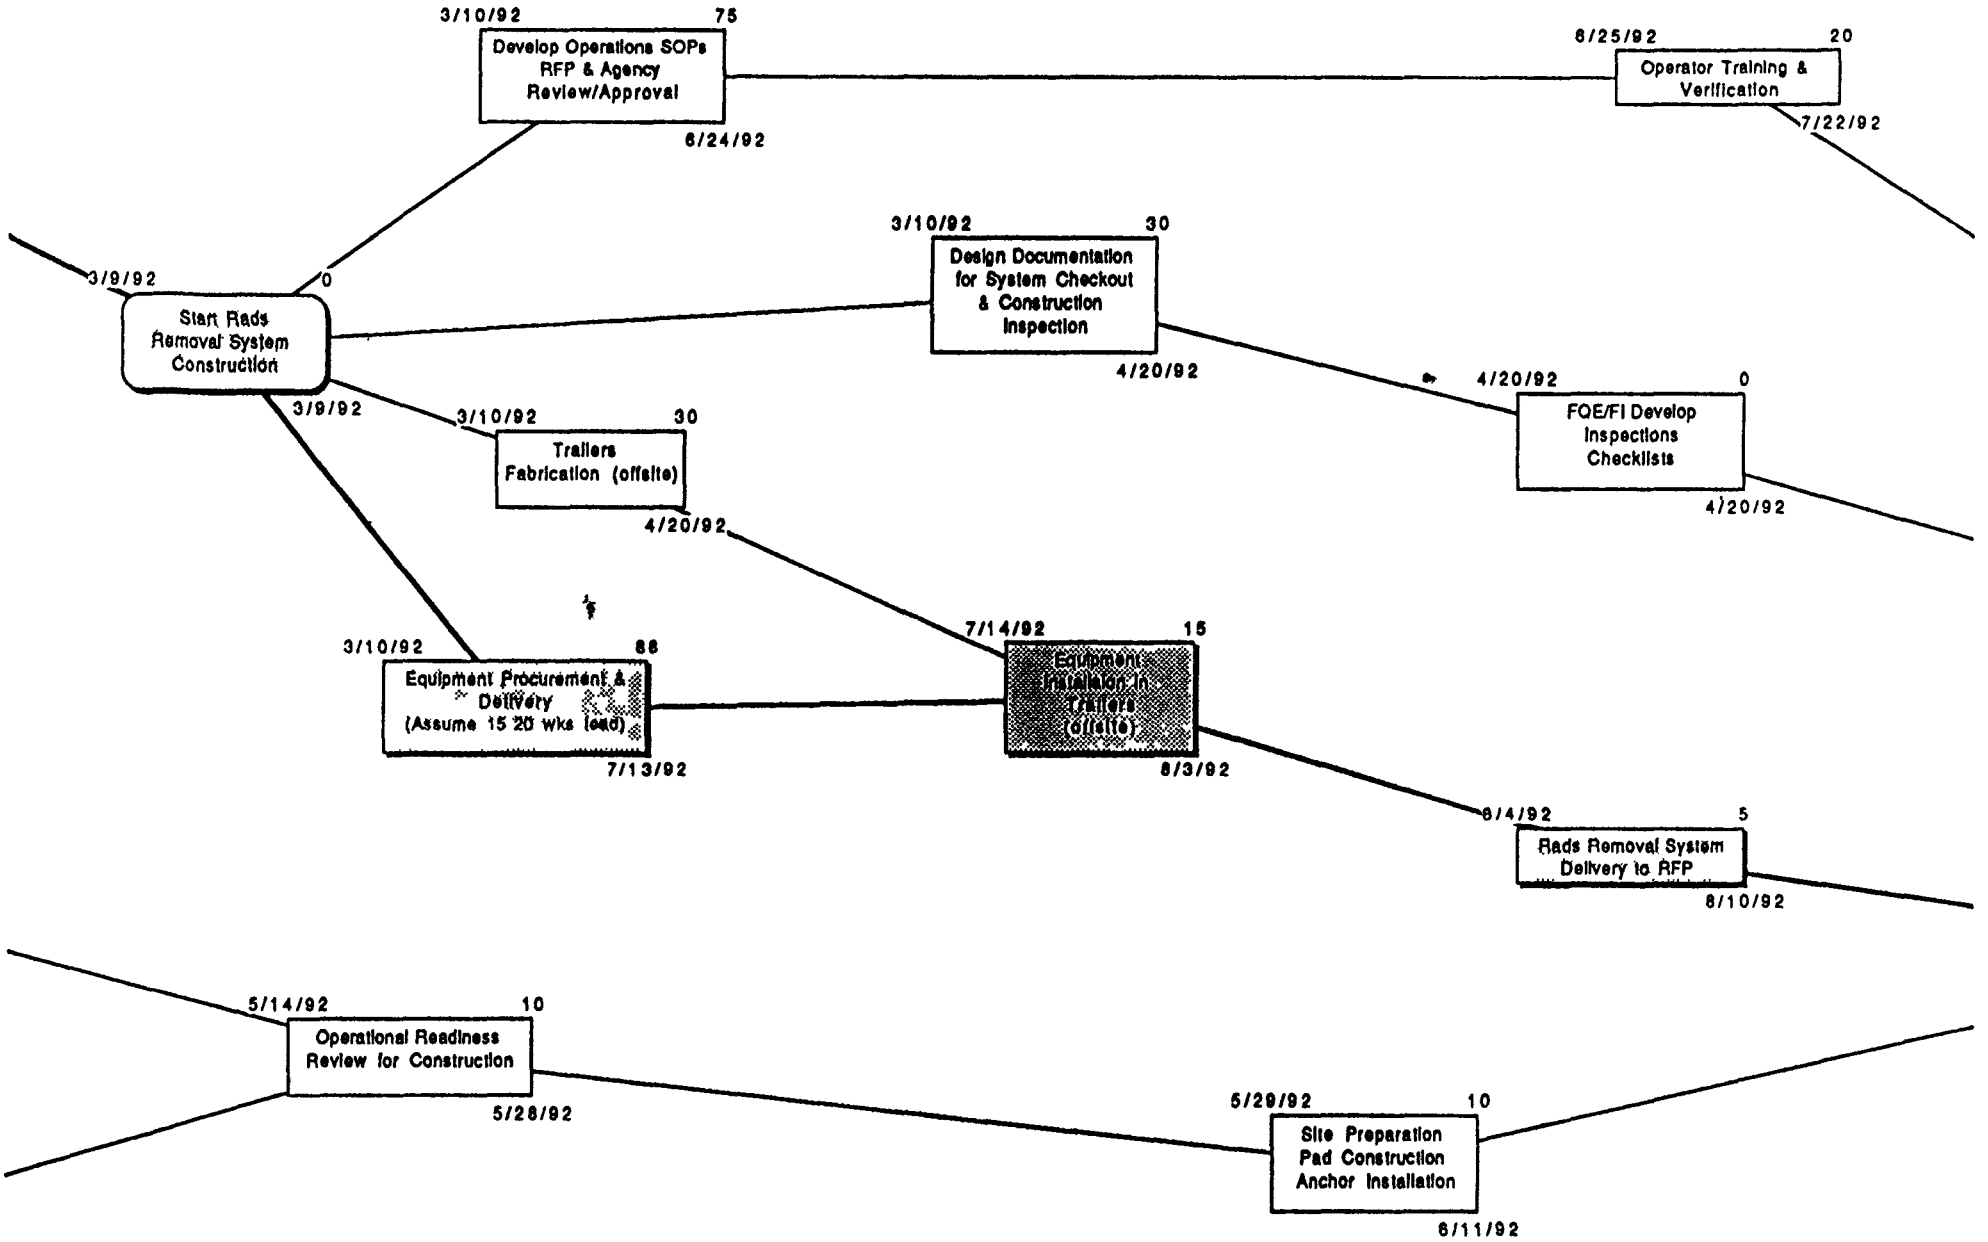
3/9/92
Start Rads Removal System Construction
0
3/10/92
75
Develop Operations SOPs RFP & Agency Review/Approval
6/24/92
6/25/92
20
Operator Training & Verification
7/22/92
3/10/92
30
Design Documentation for System Checkout & Construction Inspection
4/20/92
4/20/92
0
FQE/FI Develop Inspections Checklists
4/20/92
3/9/92
3/10/92
30
Trailers Fabrication (offsite)
4/20/92
3/10/92
86
Equipment Procurement & Delivery (Assume 15 20 wks lead)
7/13/92
7/14/92
15
Equipment Installation in Trailers (offsite)
8/3/92
8/4/92
5
Rads Removal System Delivery to RFP
8/10/92
5/14/92
10
Operational Readiness Review for Construction
5/28/92
5/29/92
10
Site Preparation Pad Construction Anchor Installation
6/11/92

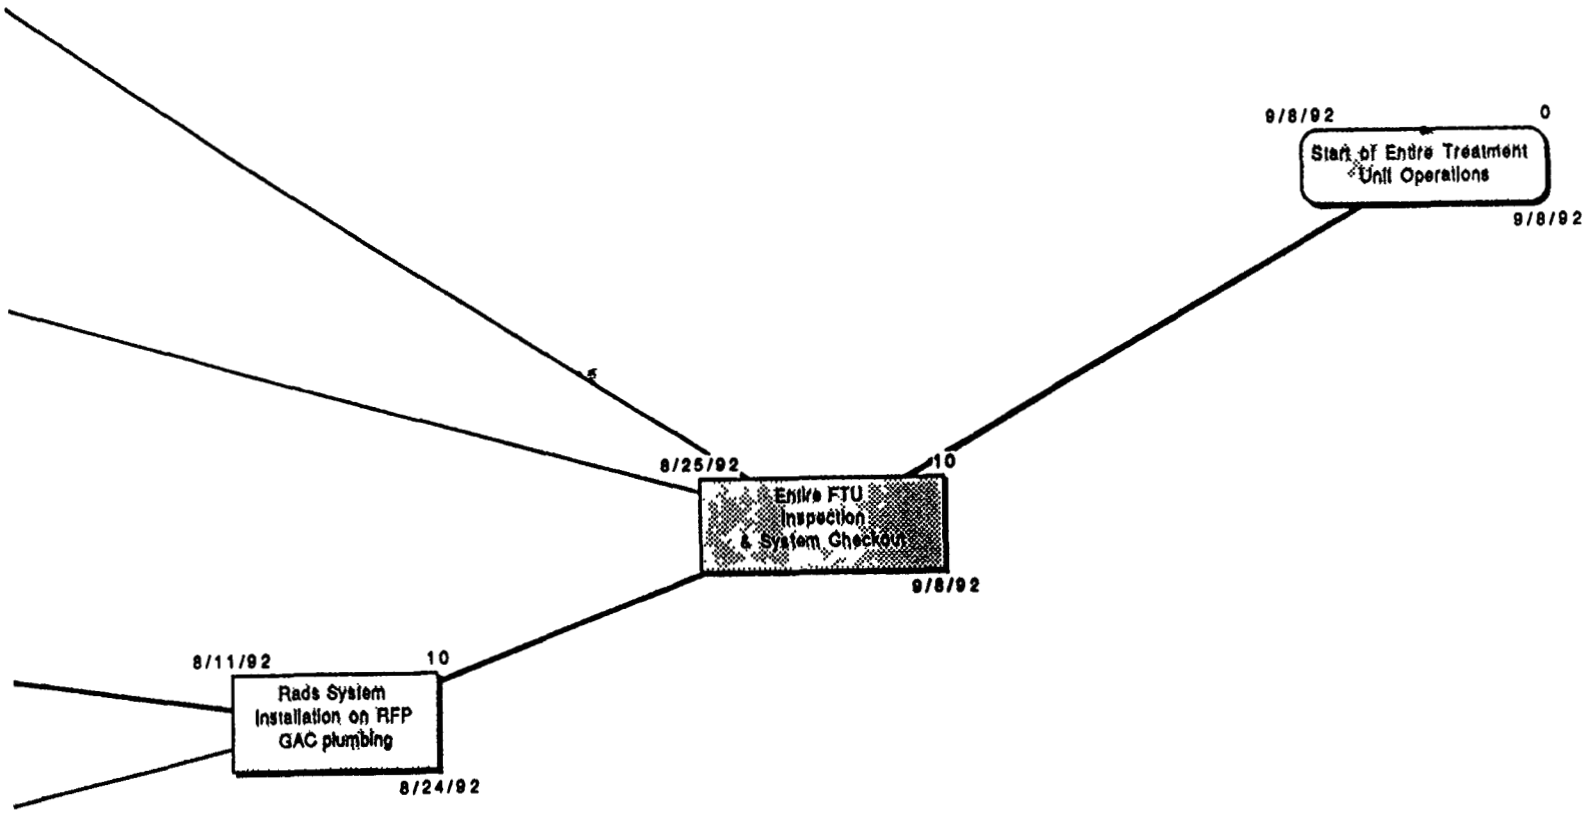
9/8/92
0
Start of Entire Treatment Unit Operations
9/8/92
5
8/25/92
10
Entire FTU Inspection & System Checkout
9/8/92
8/11/92
10
Rads System Installation on RFP GAC plumbing
8/24/92
